

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
UE15GEN-20	Client Review - Mech. Design Criteria	0d	28-Jan-25 08:00 A	13-Feb-25 17:00 A	
UE15GEN-25	Address Client Comments and Issue Final - Mech. Design Crite	0d	13-Feb-25 08:00 A	05-Mar-25 00:00 A	
00373.3.19.20.1.3 Electrical Design Criteria					
UE17GEN-05	Prep, Check, and Issue IDR - Electrical. Design Criteria	0d	16-Dec-24 08:00 A	14-Jan-25 17:00 A	
UE17GEN-10	IDR - Electrical. Design Criteria	0d	15-Jan-25 08:00 A	05-Feb-25 17:00 A	
UE17GEN-20	Client Review - Electrical. Design Criteria	0d	06-Feb-25 08:00 A	27-Feb-25 00:00 A	
UE17GEN-25	Address Client Comments and Issue Final - Electrical. Design (	0d	28-Feb-25 08:00 A	13-Mar-25 17:00 A	
00373.3.19.4 Site Preparation					
00373.3.19.4.1 Civil					
00373.3.19.4.1.8 Site Permitting					
UE121100-05	Prepare Site Development Plan Review	0d	16-Dec-24 08:00 A	17-Jan-25 00:00 A	
UE121100-15	Flood Plan Development Permit Review (Concurrent with SDP F	0d	07-Jan-25 08:00 A	04-Apr-25 00:00 A	
UE121100-10	Land Disturbance/Site Development Plan Review (STL County I	0d	07-Jan-25 08:00 A	21-May-25 17:00 A	
UE121100-25	MSD Development Plan Review	0d	10-Feb-25 08:00 A	21-May-25 17:00 A	
UE121100-35	SDP (STLCO Planning) - Final Site Improvements	0d	22-May-25 08:00 A	12-Sep-25 17:00 A	
UE121100-55	Mehville Fire Protection District - Permit	0d	23-Jun-25 08:00 A	19-Sep-25 08:00 A	
UE121100-45	MSD - Final Improvements & Private Sanitary	0d	23-Jun-25 08:00 A	10-Dec-25 17:00 A	
UE121100-65	STLCO Civil Plan Review (Final Site Improvements)	0d	18-Aug-25 08:00 A	11-Dec-25 17:00 A	
UE121100-85	Building Permit - Admin Building (Full Permit) Closed Out not ne	0d	10-Dec-25 08:00 A	10-Dec-25 17:00 A	
00373.3.19.4.1.1 SWPPP Drawings					
UE121101-05	Prep, Check, and Issue IDR Civil Drawings - SWPPP	0d	16-Jan-25 08:00 A	12-Feb-25 17:00 A	
UE121101-10	IDR Civil Drawings - SWPPP	0d	13-Feb-25 08:00 A	19-Feb-25 17:00 A	
UE121101-15	Address Comments and Issue for CR - SWPPP	0d	20-Feb-25 08:00 A	26-Feb-25 17:00 A	
UE121101-20	Client Review Civil Drawings - SWPPP	0d	27-Feb-25 08:00 A	18-Mar-25 00:00 A	
UE121101-25	Address Client Comments and Issue IFC Civil Drawings - SWPF	0d	19-Mar-25 08:00 A	31-Mar-25 00:00 A	
00373.3.19.4.1.2 Rough Grading					
UE121102-05	Prep, Check, and Issue IDR Civil Drawings - Rough Grading	0d	18-Feb-25 08:00 A	10-Mar-25 00:00 A	
UE121102-10	IDR Civil Drawings - Rough Grading	0d	11-Mar-25 08:00 A	17-Mar-25 17:00 A	
UE121102-15	Address Comments and Issue for CR Civil Drawings - Rough Gr	0d	18-Mar-25 08:00 A	24-Mar-25 17:00 A	
UE121102-20	Client Review Civil Drawings - Rough Grading	0d	25-Mar-25 08:00 A	14-Apr-25 17:00 A	
UE121102-25	Address Client Comments and Issue IFD Civil Drawings - Rough	0d	15-Apr-25 08:00 A	24-Apr-25 17:00 A	
UE121102-35	Address Client Comments and Issue IFC Civil Drawings - Rough	0d	15-Apr-25 08:00 A	03-Jun-25 17:00 A	
00373.3.19.4.1.3 Roadway Sections & Details					
UE121103-05	Prep, Check, and Issue IDR Civil Drawings - Road Profile/Sectio	0d	05-May-25 08:00 A	28-May-25 17:00 A	
UE121103-10	IDR Civil Drawings - Road Profile/Sections/Details	0d	29-May-25 08:00 A	10-Jun-25 17:00 A	
UE121103-15	Address Comments and Issue for CR Civil Drawings - Road Prof	0d	11-Jun-25 08:00 A	23-Jun-25 17:00 A	
UE121103-20	Client Review Civil Drawing - Road Profile/Sections/Details	0d	24-Jun-25 08:00 A	08-Jul-25 17:00 A	
UE121103-25	Address Client Comments and Issue IFC (Permit) Civil Drawings	0d	09-Jul-25 08:00 A	31-Jul-25 17:00 A	
00373.3.19.4.1.4 Roadway Plans					
UE121104-05	Prep, Check, and Issue IDR Civil Drawings - Roadway plans	0d	05-May-25 08:00 A	28-May-25 17:00 A	
UE121104-10	IDR Civil Drawings - Roadway plans	0d	29-May-25 08:00 A	10-Jun-25 17:00 A	
UE121104-15	Address Comments and Issue for CR Civil Drawings - Roadway	0d	11-Jun-25 08:00 A	23-Jun-25 17:00 A	
UE121104-20	Client Review Civil Drawings - Roadway plans	0d	24-Jun-25 08:00 A	08-Jul-25 17:00 A	
UE121104-25	Address Client Comments and Issue IFC (Permit) Civil Drawings	0d	09-Jul-25 08:00 A	31-Jul-25 17:00 A	
00373.3.19.4.1.5 Permanent Storm Drainage and Collection					
UE121105-05	Prep, Check, and Issue IDR Civil Drawings - Permanent Storm L	0d	27-Feb-25 08:00 A	10-Apr-25 17:00 A	
UE121105-10	IDR Civil Drawings - Permanent Storm Dranage & Collections	0d	11-Apr-25 08:00 A	17-Apr-25 17:00 A	
UE121105-15	Address Comments and Issue for CR Civil Drawings - Permaner	0d	17-Apr-25 08:00 A	28-Apr-25 17:00 A	
UE121105-20	Client Review Civil Drawings - Permanent Storm Drainage & Coll	0d	29-Apr-25 08:00 A	19-May-25 17:00 A	
UE121105-25	Address Client Comments and Issue IFC Civil Drawings - Perm:	0d	20-May-25 08:00 A	10-Jun-25 17:00 A	
00373.3.19.4.1.6 Fuel Oil Tank Berm					

Remaining Level of Effort

Actual Work

Actual Level of Effort

Primary Baseline


Milestone


Milestone

Remaining Work

Critical Remaining Work

Page 4 of 105

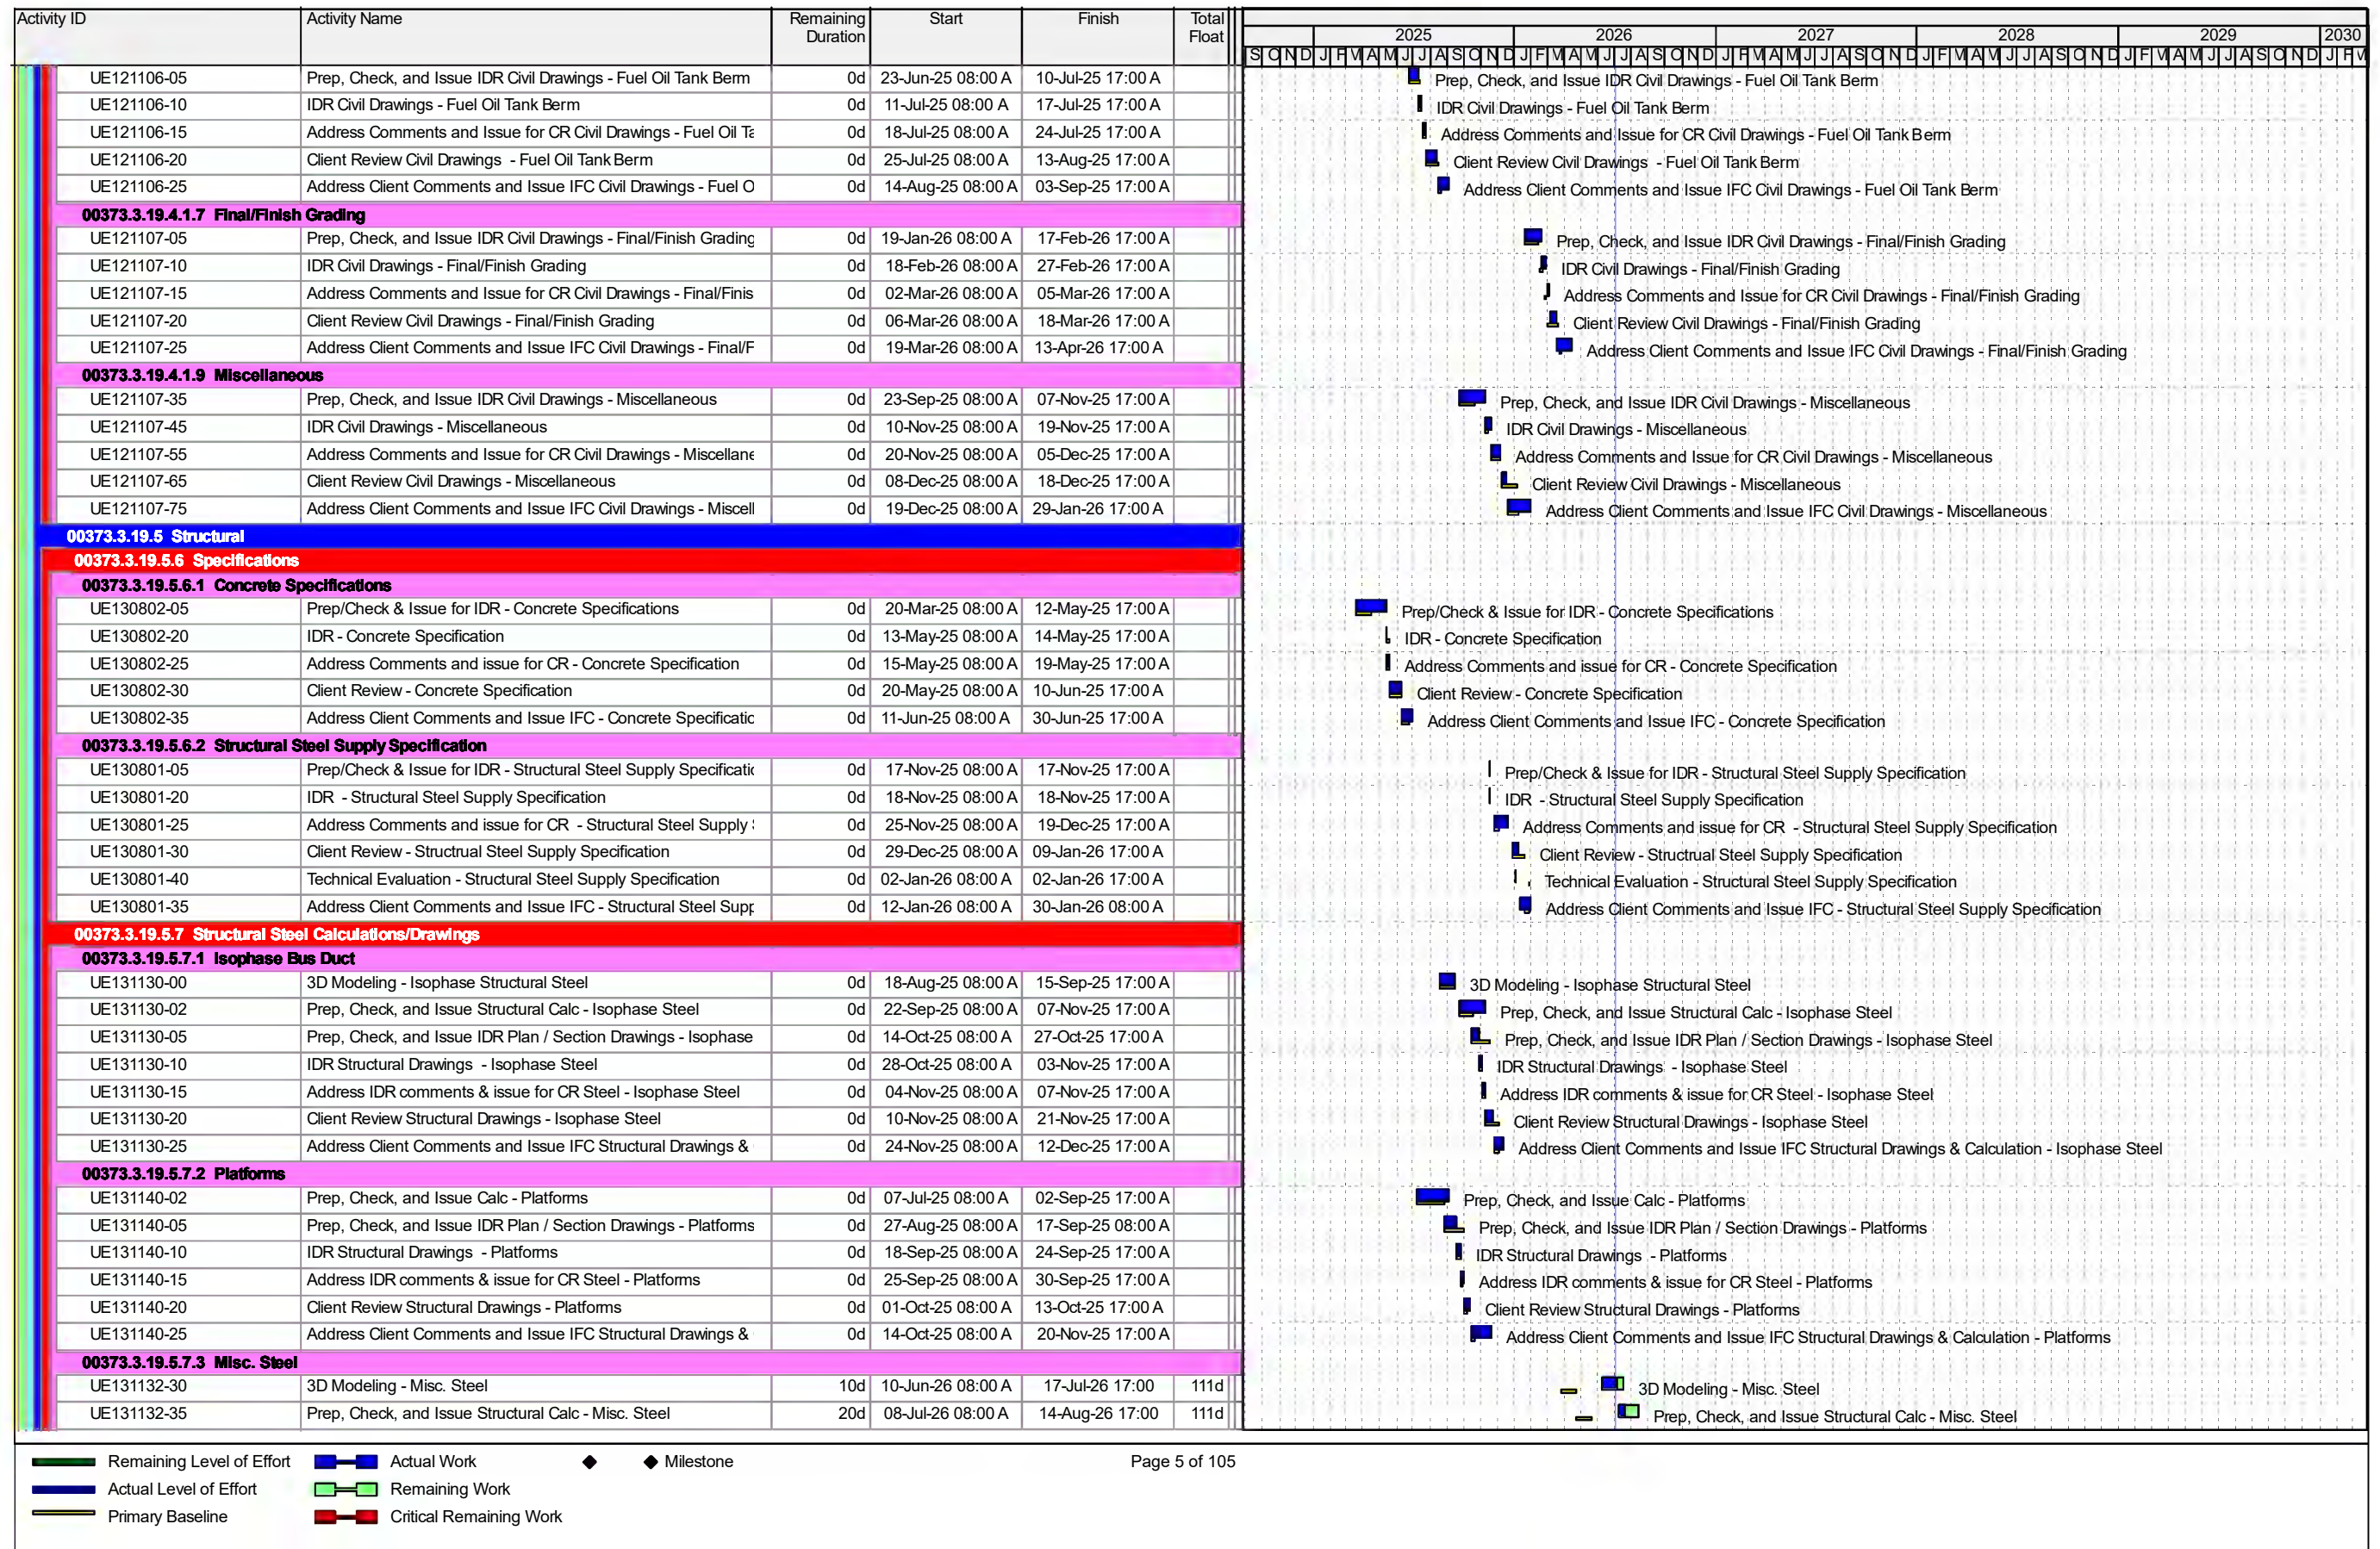

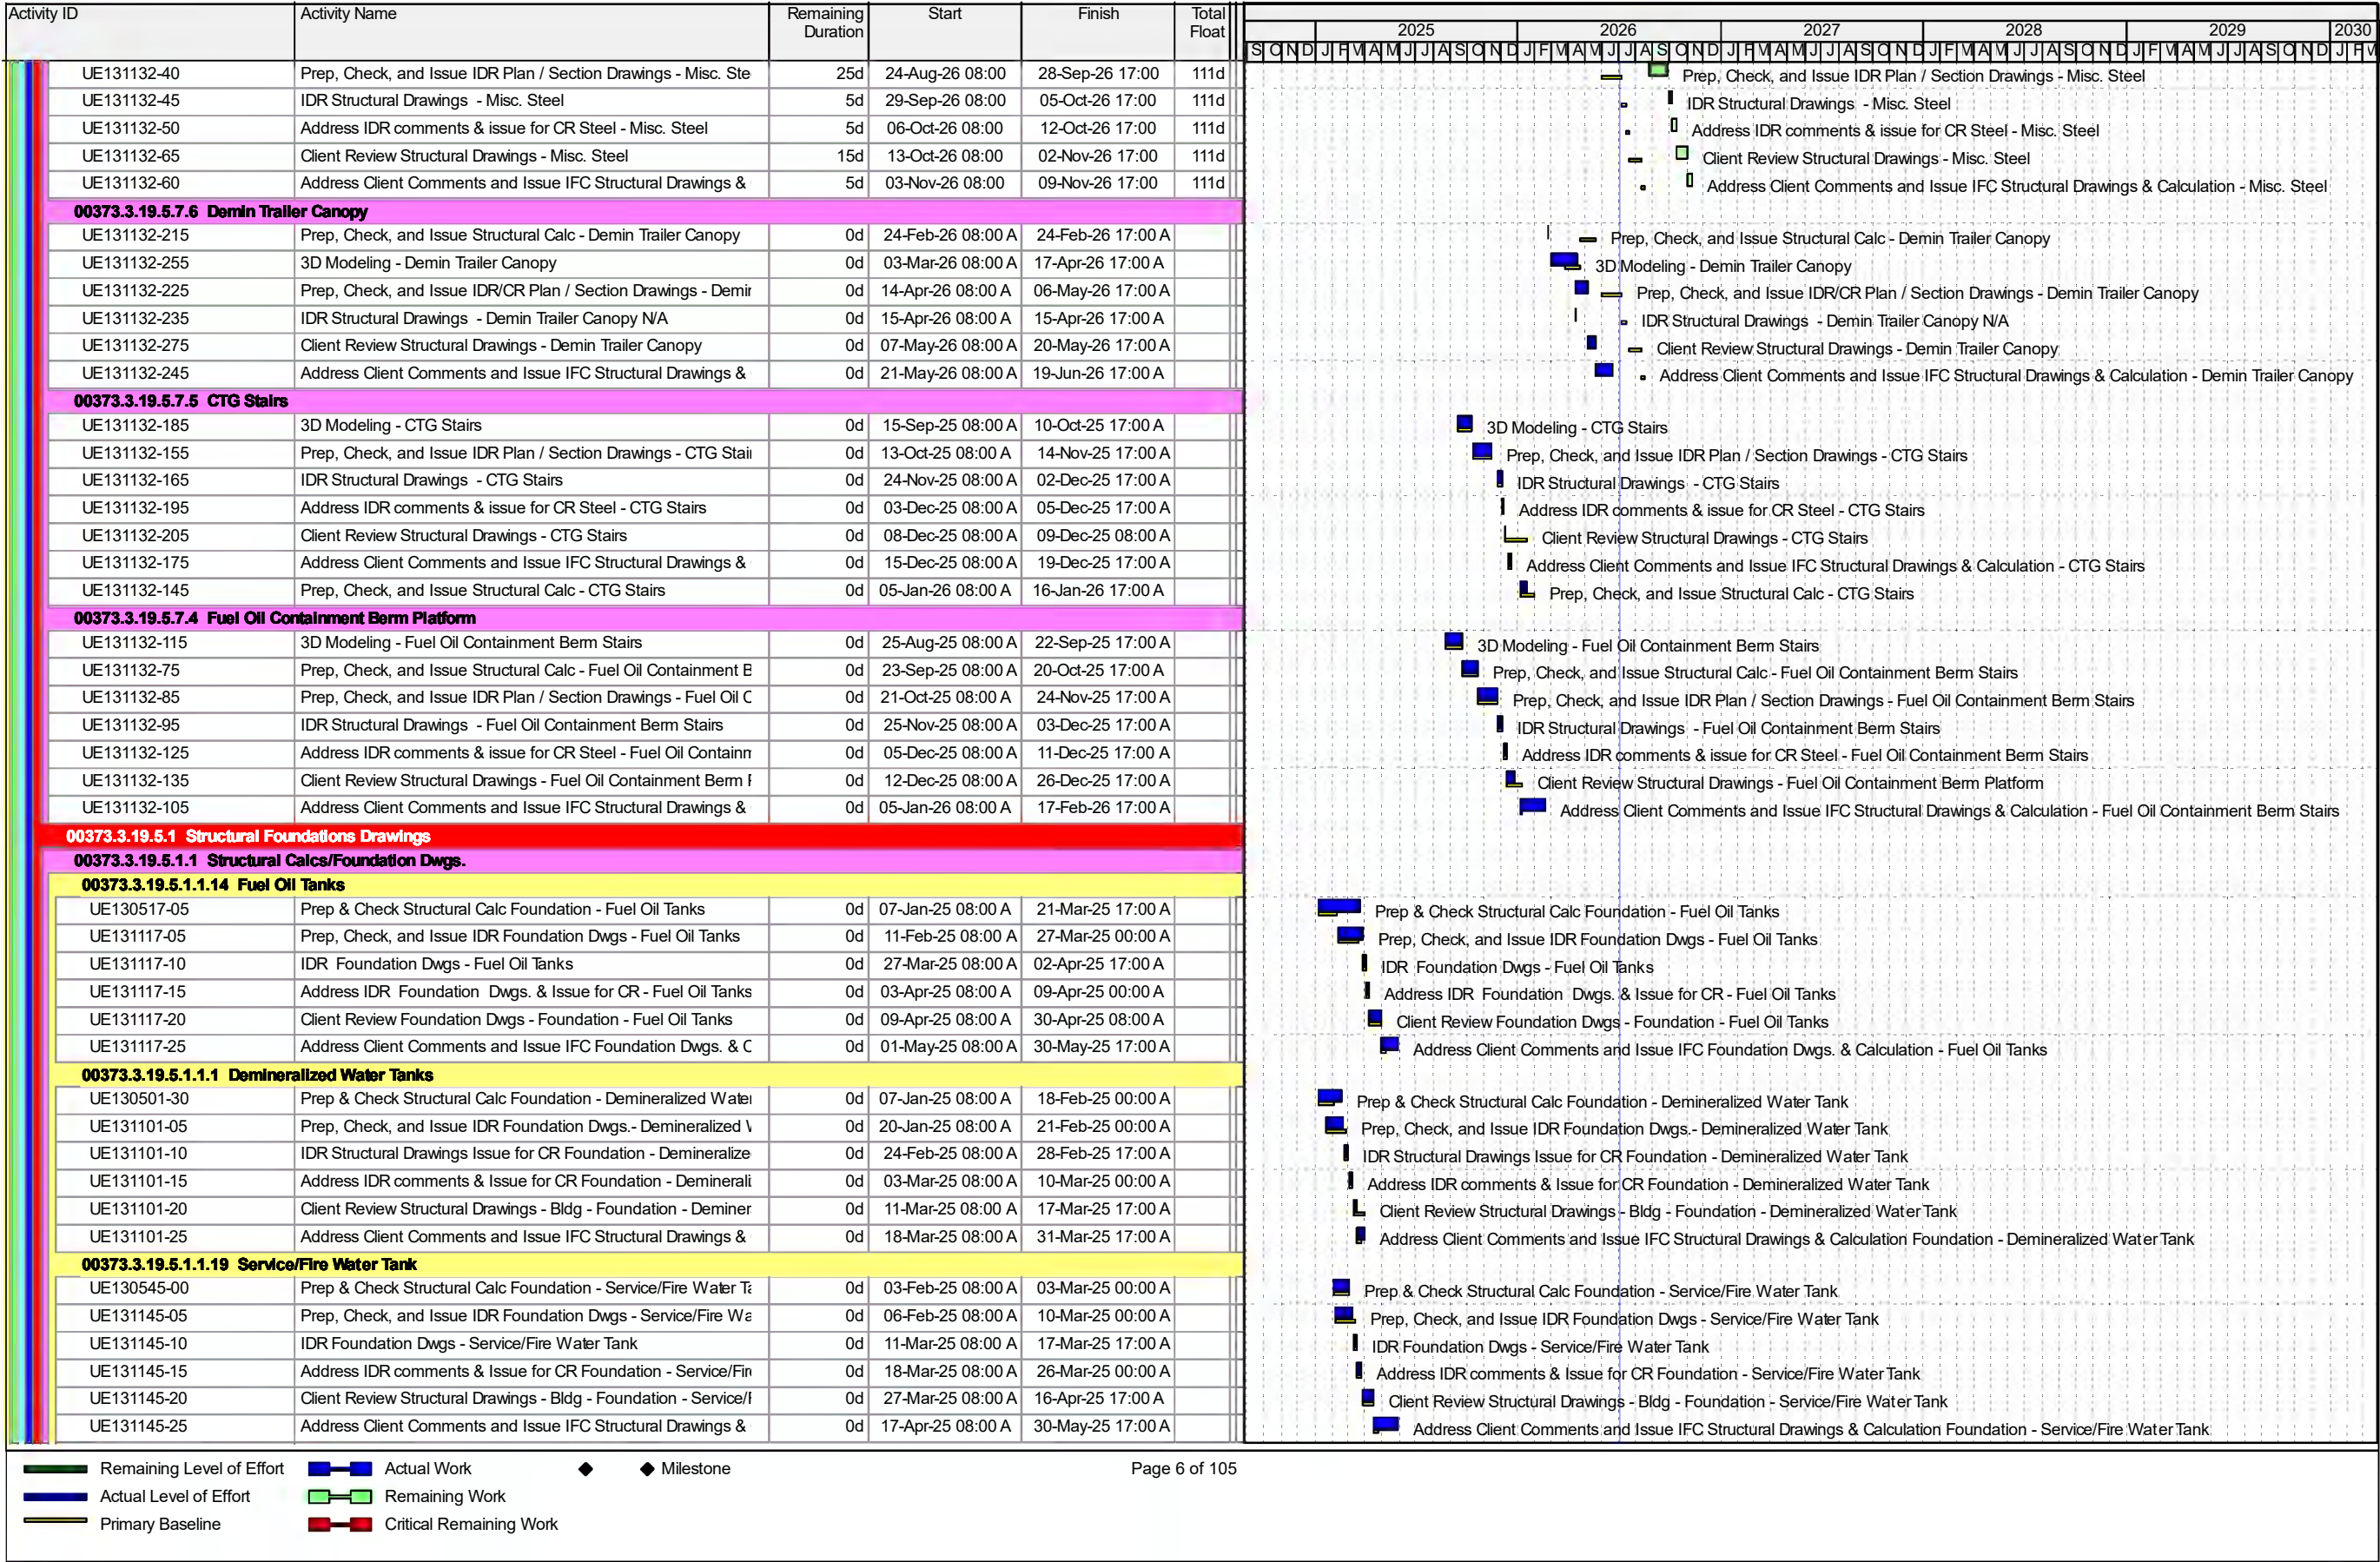

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
00373.3.19.5.1.1.2 Crane Pads					
UE130505-05	Prep, Check, and Issue Structural Calc Foundation - Crane Pad	0d	08-May-25 08:00 A	25-Aug-25 17:00 A	
UE131105-05	Prep, Check, and Issue IDR Foundation Dwgs.- Crane Pads	0d	22-May-25 08:00 A	25-Aug-25 17:00 A	
UE131105-10	IDR Foundation Dwgs - Crane Pads	0d	26-Aug-25 08:00 A	02-Sep-25 17:00 A	
UE131105-15	Address IDR Foundation Dwgs. & Issue for CR - Crane Pads	0d	03-Sep-25 08:00 A	13-Oct-25 17:00 A	
UE131105-20	Client Review Foundation Dwgs - Foundation - Crane Pads	0d	14-Oct-25 08:00 A	27-Oct-25 17:00 A	
UE131105-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	28-Oct-25 08:00 A	11-Nov-25 17:00 A	
00373.3.19.5.1.1.22 Sump Foundation					
UE130502-05	Prep, Check, and Issue Structural Calc Foundation - Sump Foui	0d	09-Jun-25 08:00 A	26-Nov-25 17:00 A	
UE131102-05	Prep, Check, and Issue IDR Foundation Dwgs.- Sump Foundati	0d	13-Nov-25 08:00 A	16-Jan-26 17:00 A	
UE131102-10	IDR Foundation Dwgs - Sump Foundations	0d	19-Jan-26 08:00 A	23-Jan-26 17:00 A	
UE131102-15	Address IDR Foundation Dwgs. & Issue for CR - Sump Founde	0d	26-Jan-26 08:00 A	06-Feb-26 17:00 A	
UE131102-20	Client Review Foundation Dwgs - Foundation - Sump Foundatio	0d	09-Feb-26 08:00 A	27-Feb-26 17:00 A	
UE131102-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	02-Mar-26 08:00 A	20-Mar-26 17:00 A	
00373.3.19.5.1.1.3 Station Service Transformers					
UE130506-05	Prep, & Check Structural Calc Foundation - Station Service Tran	0d	05-May-25 08:00 A	25-Aug-25 17:00 A	
UE131106-05	Prep, Check, and Issue IDR Foundation Dwgs.- Station Service	0d	15-May-25 08:00 A	25-Aug-25 17:00 A	
UE131106-10	IDR Foundation Dwgs - Station Service Transformers	0d	26-Aug-25 08:00 A	02-Sep-25 17:00 A	
UE131106-15	Address IDR Foundation Dwgs. & Issue for CR - Station Servic	0d	03-Sep-25 08:00 A	23-Sep-25 17:00 A	
UE131106-20	Client Review Foundation Dwgs - Foundation - Station Service T	0d	24-Sep-25 08:00 A	13-Oct-25 17:00 A	
UE131106-35	Address Client Comments and Issue IFC Pile Layout Dwgs. & C	0d	14-Oct-25 08:00 A	03-Nov-25 17:00 A	
UE131106-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	14-Oct-25 08:00 A	02-Jan-26 17:00 A	
00373.3.19.5.1.1.4 Gas Compressor Coolers					
UE130507-05	Prep & Check Structural Calc Foundation - Gas Compressor Coi	0d	29-Apr-25 08:00 A	02-Jun-25 17:00 A	
UE131107-05	Prep, Check, and Issue IDR Foundation Dwgs.- Gas Compressc	0d	13-May-25 08:00 A	10-Jul-25 17:00 A	
UE131107-10	IDR Foundation Dwgs - Gas Compressor Coolers	0d	11-Jul-25 08:00 A	17-Jul-25 17:00 A	
UE131107-15	Address IDR Foundation Dwgs. & Issue for CR - Gas Compres	0d	05-Aug-25 08:00 A	18-Aug-25 17:00 A	
UE131107-20	Client Review Foundation Dwgs - Foundation - Gas Compressor	0d	19-Aug-25 08:00 A	25-Aug-25 17:00 A	
UE131107-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	26-Aug-25 08:00 A	19-Sep-25 17:00 A	
00373.3.19.5.1.1.20 Fuel Oil Unloading					
UE130527-05	Prep, Check, and Issue Structural Calc Foundation - Fuel Oil Ur	0d	15-Sep-25 08:00 A	27-Jan-26 17:00 A	
UE131127-05	Prep, Check, and Issue IDR Foundation Dwgs.- Fuel Oil Unloadi	0d	06-Oct-25 08:00 A	29-Jan-26 17:00 A	
UE131127-10	IDR Foundation Dwgs - Fuel Oil Unloading	0d	30-Jan-26 08:00 A	09-Feb-26 08:00 A	
UE131127-15	Address IDR Foundation Dwgs. & Issue for CR - Fuel Oil Unloa	0d	09-Feb-26 08:00 A	12-Mar-26 17:00 A	
UE131127-20	Client Review Foundation Dwgs - Foundation - Fuel Oil Unloadin	0d	13-Mar-26 08:00 A	26-Mar-26 17:00 A	
UE131127-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	27-Mar-26 08:00 A	30-Apr-26 17:00 A	
00373.3.19.5.1.1.21 Closed Cooling Water Heat Exchanger					
UE130528-05	Prep & Check Foundation Calc. - Closed Cooling Water Heat Ex	0d	18-Mar-25 08:00 A	17-Apr-25 17:00 A	
UE131128-05	Prep, Check, and Issue IDR Foundation Dwgs.- Closed Cooling	0d	25-Mar-25 08:00 A	27-May-25 17:00 A	
UE131128-10	IDR Foundation Dwgs - Closed Cooling Water Heat Exchanger	0d	28-May-25 08:00 A	03-Jun-25 17:00 A	
UE131128-15	Address IDR Foundation Dwgs. & Issue for CR - Closed Coolin	0d	04-Jun-25 08:00 A	18-Aug-25 17:00 A	
UE131128-20	Client Review Foundation Dwgs - Foundation - Closed Cooling V	0d	19-Aug-25 08:00 A	25-Aug-25 17:00 A	
UE131128-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	26-Aug-25 08:00 A	18-Sep-25 17:00 A	
00373.3.19.5.1.1.5 CEMS Bldg.					
UE130508-05	Prep & Check Structural Calc Foundation - CEMS Bldg.	0d	08-Apr-25 08:00 A	30-May-25 17:00 A	
UE131108-05	Prep, Check, and Issue IDR Foundation Dwgs.- CEMS Bldg.	0d	07-May-25 08:00 A	30-May-25 17:00 A	
UE131108-10	IDR Foundation Dwgs - CEMS Bldg.	0d	02-Jun-25 08:00 A	06-Jun-25 17:00 A	
UE131108-15	Address IDR Foundation Dwgs. & Issue for CR - CEMS Bldg.	0d	09-Jun-25 08:00 A	18-Aug-25 17:00 A	
UE131108-20	Client Review Foundation Dwgs - Foundation - CEMS Bldg.	0d	19-Aug-25 08:00 A	25-Aug-25 17:00 A	
UE131108-25	Address Client Comments and Issue IFC Foundation Dwgs. & C	0d	26-Aug-25 08:00 A	12-Sep-25 17:00 A	
00373.3.19.5.1.1.6 Fuel Gas Yard Equipment					

Remaining Level of Effort

Actual Work

Milestone


Actual Level of Effort


Remaining Work

Primary Baseline

Critical Remaining Work

Page 7 of 105

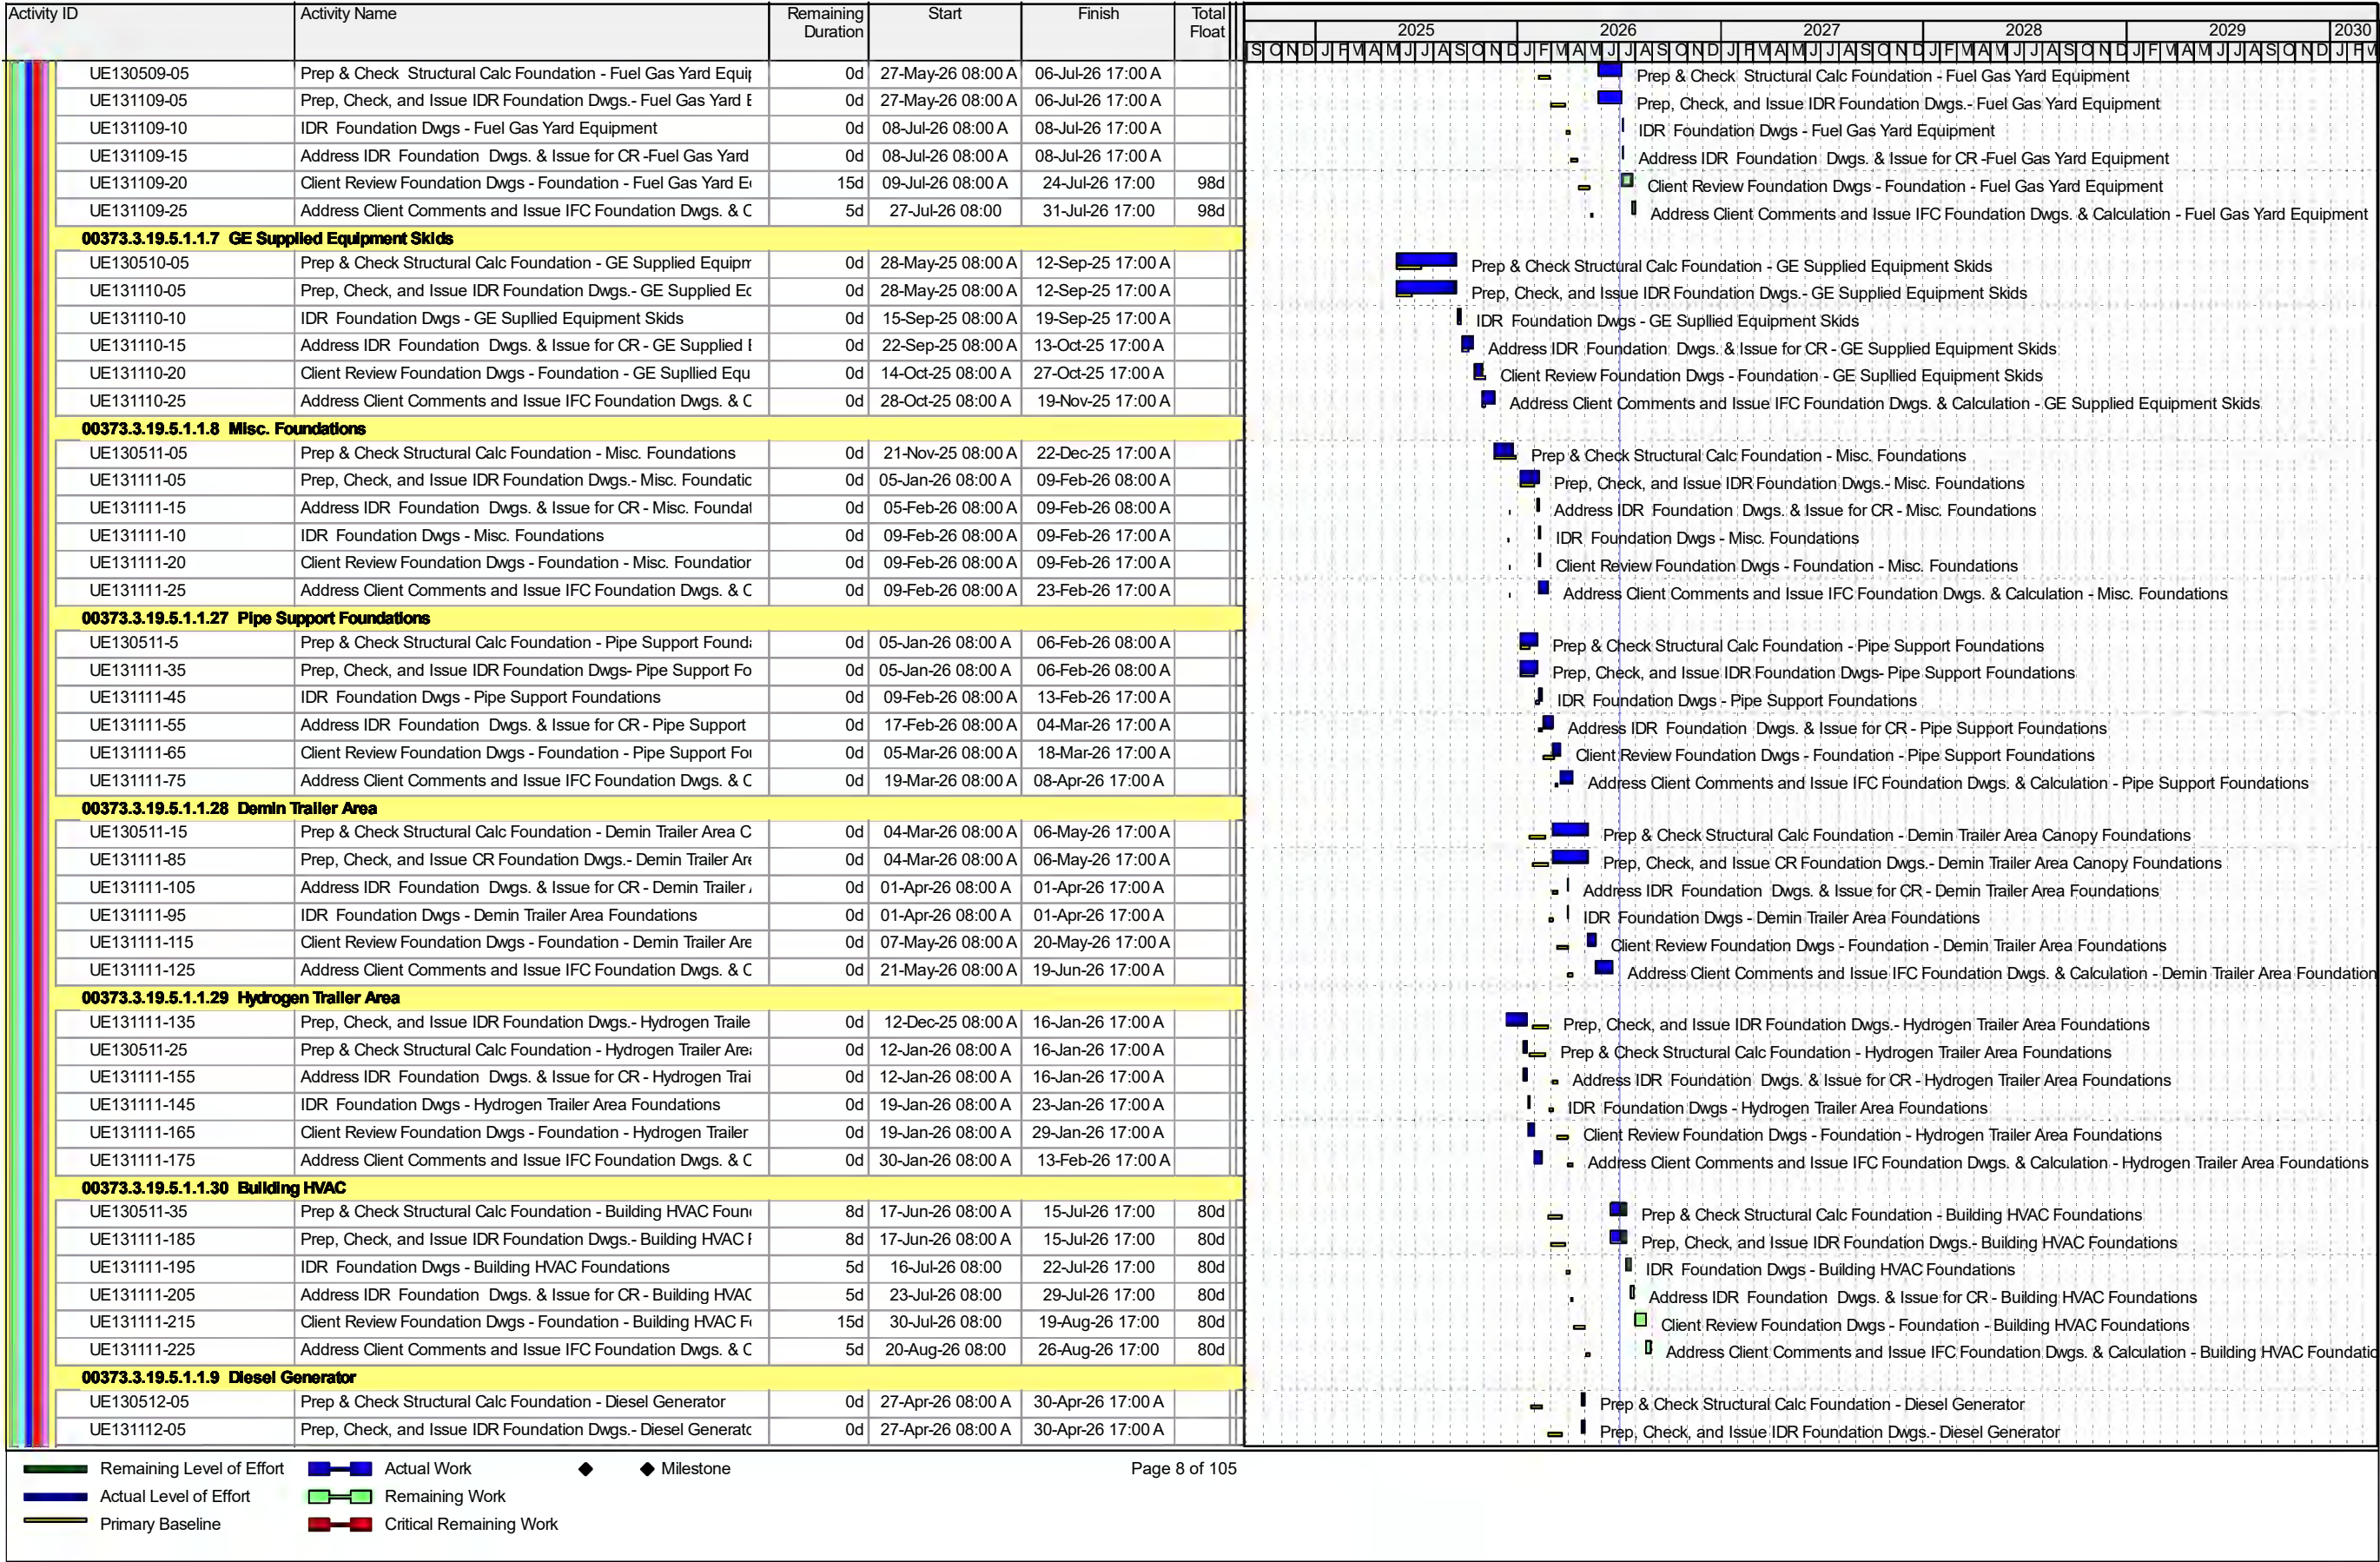

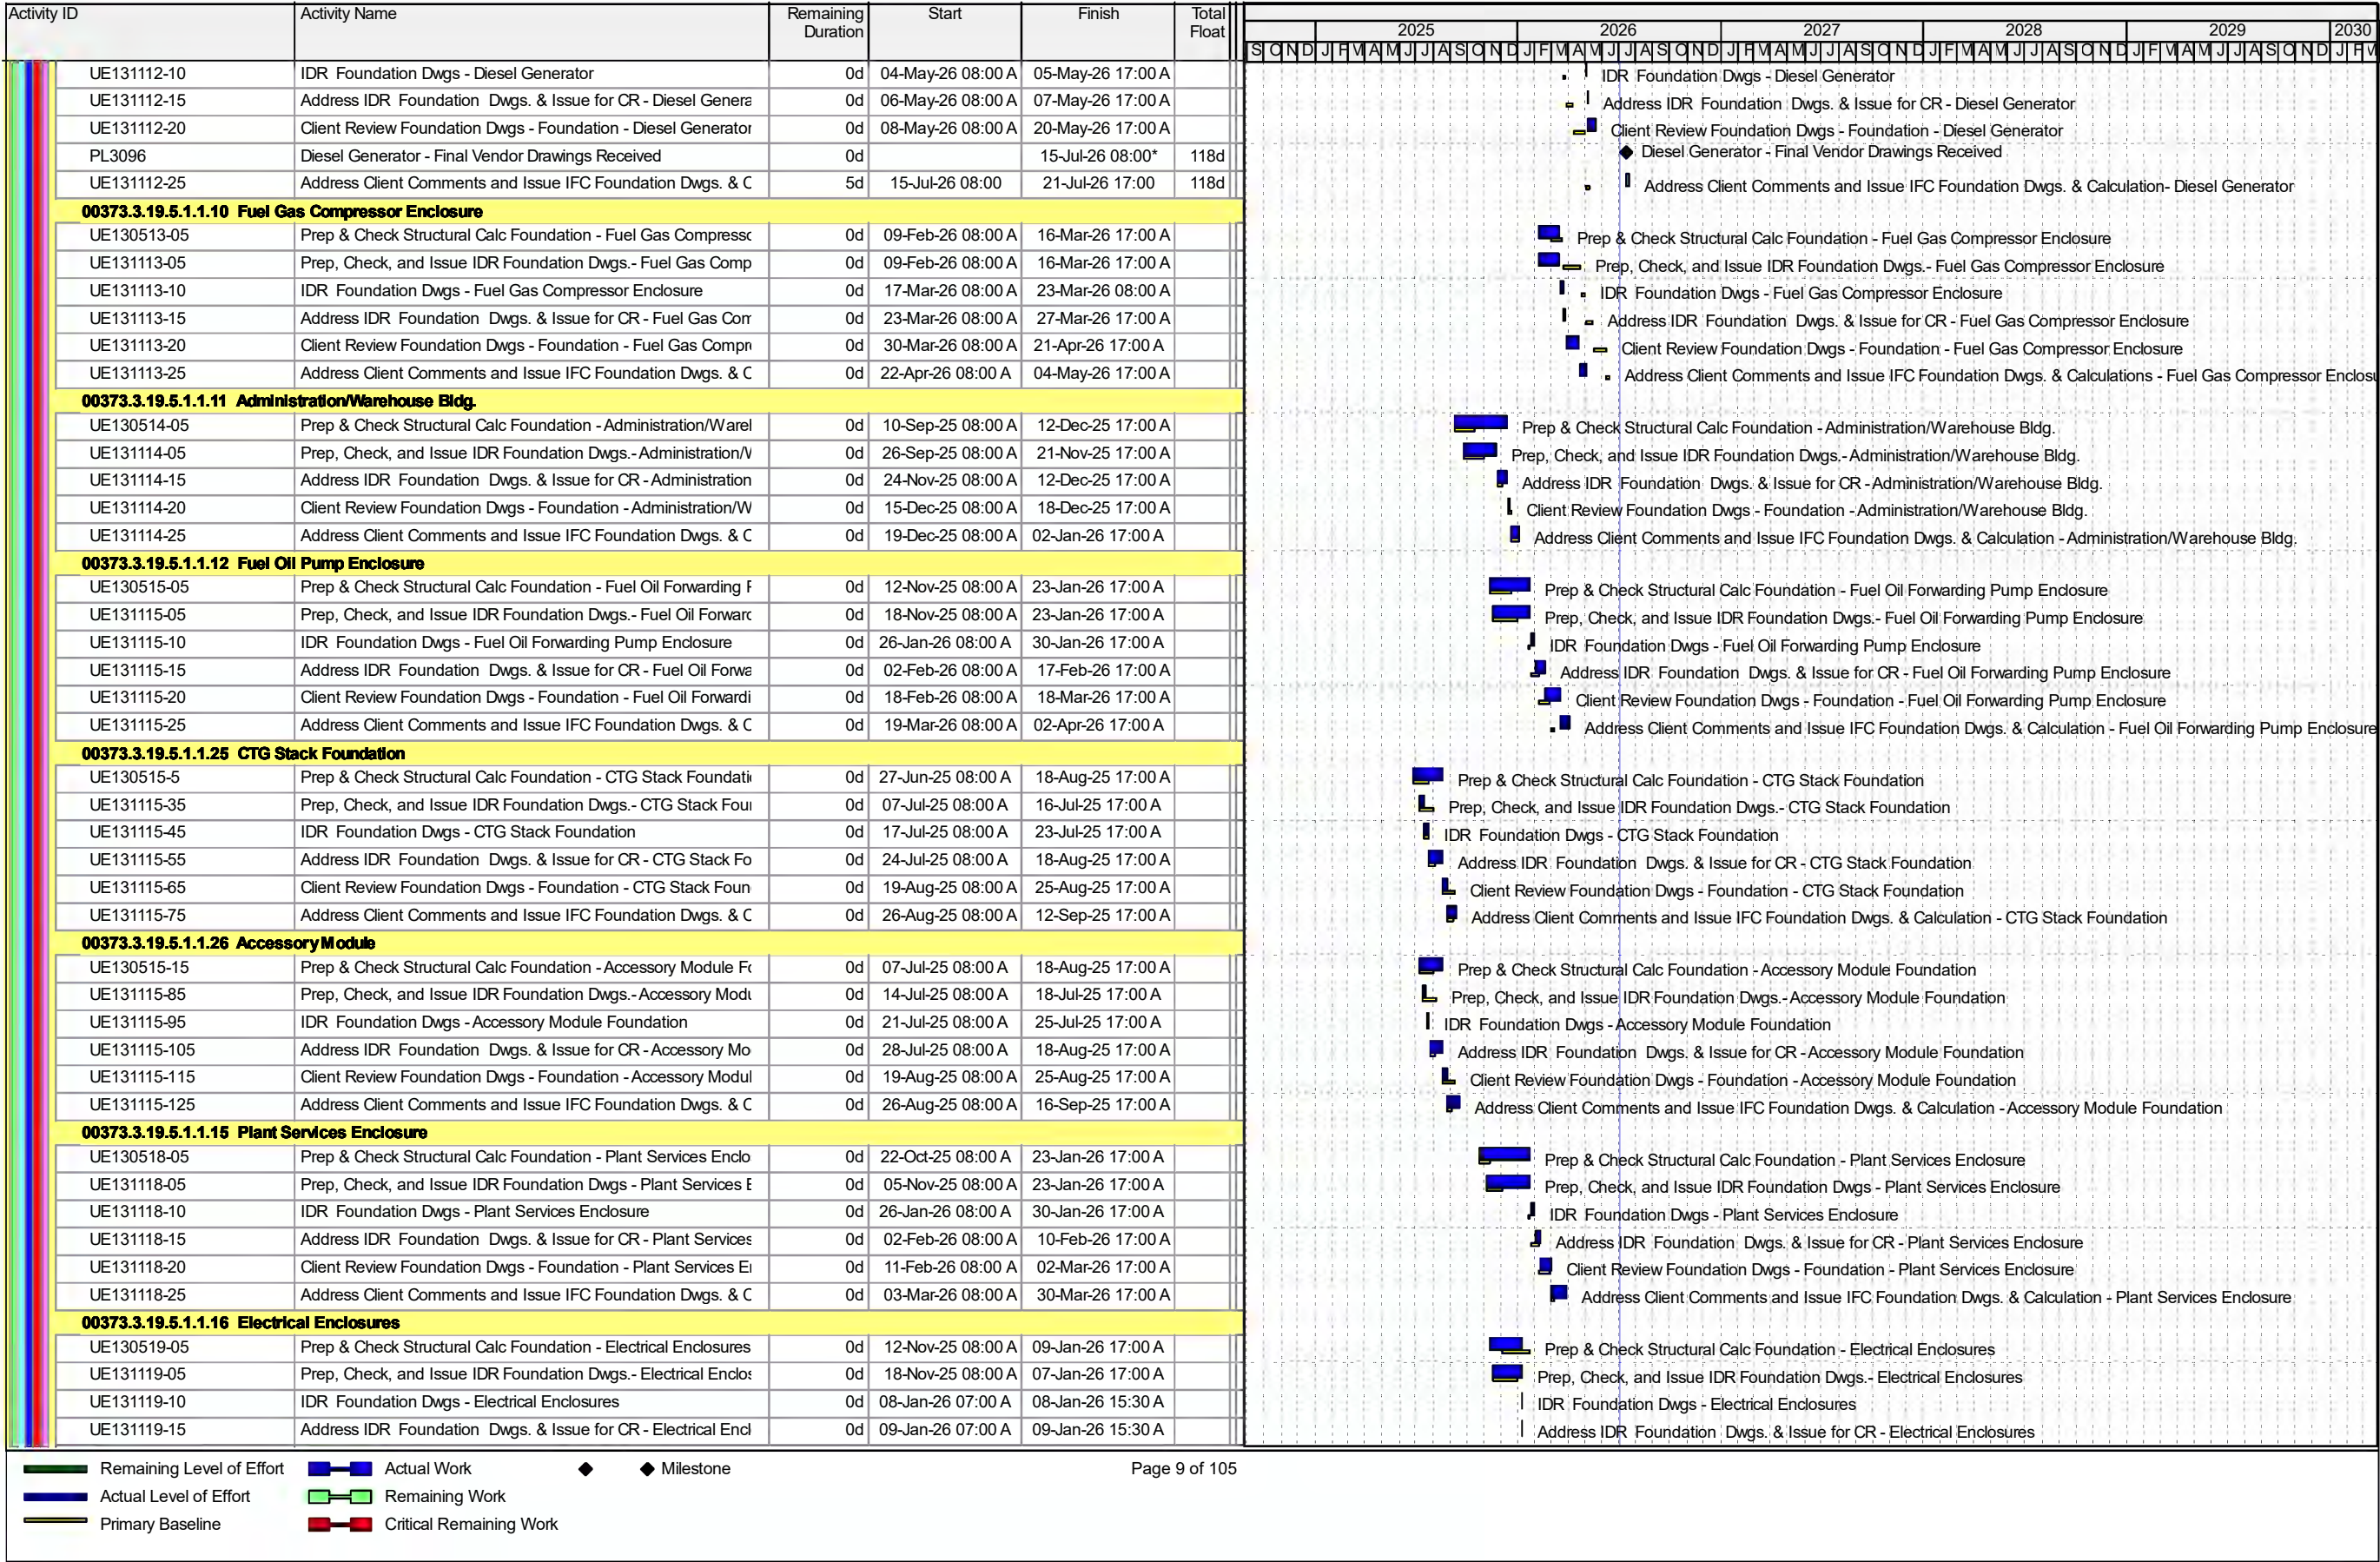

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
UE150566-99	Prep, Check, and Issue For Purpose - Mechanical Calc - Water	0d	13-Mar-25 08:00 A	04-Apr-25 17:00 A	
UE150561-99	Prep, Check, and Issue For Purpose - Mechanical Calc - Potabl	0d	25-Mar-25 08:00 A	17-Apr-25 17:00 A	
UE150509-99	Prep, Check, and Issue For Purpose - Mechanical Calc - HVAC /	0d	11-Jul-25 08:00 A	01-Oct-25 17:00 A	
UE150509-209	Prep, Check, and Issue For Purpose - Mechanical Calc - A295 L	0d	09-Sep-25 08:00 A	31-Oct-25 17:00 A	
UE150509-179	Prep, Check, and Issue For Purpose - Mechanical Calc - HVAC I	0d	15-Sep-25 08:00 A	21-Nov-25 17:00 A	
UE150509-109	Prep, Check, and Issue For Purpose - Mechanical Calc - HVAC	0d	17-Sep-25 08:00 A	21-Nov-25 17:00 A	
UE150509-139	Prep, Check, and Issue For Purpose - Mechanical Calc - HVAC I	0d	23-Oct-25 08:00 A	05-Mar-26 17:00 A	
UE150509-189	Prep, Check, and Issue For Purpose - Mechanical Calc - HVAC I	0d	14-Nov-25 08:00 A	05-Dec-25 17:00 A	
UE150509-219	Prep, Check, and Issue For Purpose - Mechanical Calc - Guard	0d	25-Nov-25 08:00 A	25-Nov-25 17:00 A	
00373.3.19.1.9 Mechanical Specifications					
00373.3.19.1.9.9 Site Utility Specification					
UE150800-05	Prep/Check & Issue for IDR Specification - Site Utilities Specifc	0d	16-Dec-24 08:00 A	20-Dec-24 00:00 A	
UE150800-20	IDR - Site Utilities Specficiation	0d	30-Dec-24 08:00 A	07-Jan-25 17:00 A	
UE150800-25	Address Comments and issue for CR Mech Spec - Site Utilities :	0d	06-Jan-25 08:00 A	10-Jan-25 17:00 A	
UE150800-30	Cient Review - Site Utilities Specficiation	0d	13-Jan-25 08:00 A	30-Jan-25 00:00 A	
UE150800-35	Address Client Comments & Issue for Use - Site Utilities Specifc	0d	31-Jan-25 08:00 A	12-Feb-25 00:00 A	
00373.3.19.1.9.2 Air Compressors/Receivers/&Dryers					
UE150801-05	Prep/Check & Issue for IDR Specification - Air Compressors/Rec	0d	16-Jan-25 08:00 A	29-Jan-25 17:00 A	
UE150801-20	IDR Specification - Air Compressors/Receivers & Dryers	0d	30-Jan-25 08:00 A	07-Feb-25 17:00 A	
UE150801-25	Address Comments and issue for CR Mech Spec - Air Compres:	0d	10-Feb-25 08:00 A	13-Feb-25 00:00 A	
UE150801-30	Cient Review Specification - Air Compressors/Receivers & Dryer	0d	14-Feb-25 08:00 A	05-Mar-25 00:00 A	
UE150801-35	Address Client Comments and Finalize Spec. - Air Compressors	0d	06-Mar-25 08:00 A	17-Mar-25 00:00 A	
UE150801-40	Technical Evaluation of Bids -Air Compressors/Receivers & Drie	0d	21-Jul-25 08:00 A	30-Jul-25 17:00 A	
00373.3.19.1.9.15 Fuel Gas Valves					
UE150804-05	Prep/Check & Issue for IDR Specification - Fuel Gas Valves	0d	10-Mar-25 08:00 A	19-Mar-25 00:00 A	
UE150804-20	IDR Specification - Fuel Gas Valves	0d	20-Mar-25 08:00 A	26-Mar-25 17:00 A	
UE150804-25	Address Comments and issue for CR Mech Spec - Fuel Gas Va	0d	27-Mar-25 08:00 A	03-Apr-25 17:00 A	
UE150804-30	Cient Review Specification - Fuel Gas Valves	0d	04-Apr-25 08:00 A	21-Apr-25 17:00 A	
UE150804-35	Address Client Comments and Finalize Spec. - Fuel Gas Valves	0d	22-Apr-25 08:00 A	07-May-25 17:00 A	
UE150804-40	Technical Evaluation of Bids - Fuel Gas Valves	0d	23-Feb-26 08:00 A	10-Apr-26 17:00 A	
00373.3.19.1.9.1 Sump Pumps					
UE150802-05	Prep/Check & Issue for IDR - Sump Pumps Specification	0d	07-Apr-25 08:00 A	25-Apr-25 17:00 A	
UE150802-20	IDR - Sump Pumps Specification	0d	28-Apr-25 08:00 A	02-May-25 17:00 A	
UE150802-25	Address Comments and issue for CR - Sump Pumps Specificati	0d	05-May-25 08:00 A	06-May-25 17:00 A	
UE150802-30	Cient Review - Sump Pumps Specification	0d	07-May-25 08:00 A	28-May-25 17:00 A	
UE150802-35	Address Client Comments and Finalize Spec. - Sump Pumps Si	0d	29-May-25 08:00 A	31-Jul-25 17:00 A	
UE150802-40	Technical Evaluation of Bids - Sump Pumps Specification	0d	10-Nov-25 08:00 A	06-Jan-26 17:00 A	
00373.3.19.1.9.3 Fuel Oil Unloading Pumps					
UE150803-05	Prep/Check & Issue for IDR - Fuel Oil Unloading Pumps Specifc	0d	24-Feb-25 08:00 A	13-Mar-25 17:00 A	
UE150803-20	IDR - Fuel Oil Unloading Pump Specification	0d	14-Mar-25 08:00 A	20-Mar-25 17:00 A	
UE150803-25	Address Comments and issue for CR - Fuel Oil Unloading Pump	0d	21-Mar-25 08:00 A	27-Mar-25 17:00 A	
UE150803-30	Cient Review - Fuel Oil Unloading Pumps Specification	0d	27-Mar-25 08:00 A	16-Apr-25 17:00 A	
UE150803-35	Address Client Comments and Finalize Spec. - Fuel Oil Unloadir	0d	17-Apr-25 08:00 A	06-May-25 17:00 A	
UE150803-40	Technical Evaluation of Bids - Fuel Oil Unloading Pumps	0d	15-Sep-25 08:00 A	31-Oct-25 17:00 A	
00373.3.19.1.9.8 Service Water Pumps					
UE150808-05	Prep/Check & Issue for IDR - Service Water Pumps Specificatio	0d	27-Jan-25 08:00 A	10-Feb-25 17:00 A	
UE150808-20	IDR - Service Water Pumps Specification	0d	10-Feb-25 08:00 A	14-Feb-25 17:00 A	
UE150808-25	Address Comments and issue for CR - Service Water Pumps St	0d	18-Feb-25 08:00 A	21-Feb-25 00:00 A	
UE150808-30	Cient Review - Service Water Pumps Specification	0d	24-Feb-25 08:00 A	17-Mar-25 08:00 A	
UE150808-35	Address Client Comments and Finalize Spec. - Service Water P	0d	18-Mar-25 08:00 A	19-Mar-25 00:00 A	
UE150808-40	Technical Evaluation of Bids - Service Water Pumps Specificatic	0d	22-Aug-25 08:00 A	31-Oct-25 17:00 A	

■ Remaining Level of Effort

■ Actual Work

◆ Milestone

■ Actual Level of Effort

■ Remaining Work

■ Primary Baseline

■ Critical Remaining Work

Page 11 of 105

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
00373.3.19.1.9.5 Oil Water Separator					
UE150805-05	Prep/Check & Issue for IDR - Oil Water Separator Specification	0d	07-Apr-25 08:00 A	25-Apr-25 17:00 A	
UE150805-20	IDR Specification - Oil Water Separator Specification	0d	28-Apr-25 08:00 A	02-May-25 17:00 A	
UE150805-25	Address Comments and issue for CR - Oil Water Separato	0d	05-May-25 08:00 A	06-May-25 17:00 A	
UE150805-30	Client Review - Oil Water Separator Specification	0d	07-May-25 08:00 A	27-May-25 17:00 A	
UE150805-35	Address Client Comments and Finalize Spec. - Oil Water Separ	0d	28-May-25 08:00 A	10-Jun-25 17:00 A	
UE150805-40	Technical Evaluation of Bids - Oil Water Separator Specification	0d	13-Oct-25 08:00 A	12-Dec-25 17:00 A	
00373.3.19.1.9.6 U/G Shop Fabricated Tanks					
UE150806-05	Prep/Check & Issue for IDR - U/G Shop Fabricated Tanks Specif	0d	08-Apr-25 08:00 A	28-Apr-25 17:00 A	
UE150806-20	IDR - U/G Shop Fabricated Tanks Specification	0d	29-Apr-25 08:00 A	30-Apr-25 17:00 A	
UE150806-25	Address Comments and issue for CR - U/G Shop Fabricated Tar	0d	01-May-25 08:00 A	05-May-25 17:00 A	
UE150806-30	Client Review - U/G Shop Fabricated Tanks Specification	0d	06-May-25 08:00 A	27-May-25 17:00 A	
UE150806-35	Address Client Comments and Finalize Spec. - U/G Shop Fabric	0d	28-May-25 08:00 A	11-Jun-25 17:00 A	
UE150806-40	Technical Evaluation of Bids - U/G Shop Fabricated Tanks Speci	0d	12-Aug-25 08:00 A	03-Nov-25 08:00 A	
00373.3.19.1.9.16 A/G Shop Fabricated Tanks					
UE1508066-05	Prep/Check & Issue for IDR - A/G Shop Fabricated Tanks Specif	0d	19-May-25 08:00 A	02-Jun-25 17:00 A	
UE1508066-20	IDR - A/G Shop Fabricated Tanks Specification	0d	03-Jun-25 08:00 A	09-Jun-25 17:00 A	
UE1508066-25	Address Comments and issue for CR - A/G Shop Fabricated Tar	0d	10-Jun-25 08:00 A	13-Jun-25 17:00 A	
UE1508066-30	Client Review - A/G Shop Fabricated Tanks Specification	0d	16-Jun-25 08:00 A	03-Jul-25 17:00 A	
UE1508066-35	Address Client Comments and Finalize Spec. - A/G Shop Fabric	0d	07-Jul-25 08:00 A	28-Jul-25 17:00 A	
UE1508066-40	Technical Evaluation of Bids - A/G Shop Fabricated Tanks Speci	0d	02-Dec-25 08:00 A	12-Dec-25 17:00 A	
00373.3.19.1.9.7 BOP Manual Valves					
UE150807-05	Prep/Check & Issue for IDR- BOP Manual Valves Specification I	0d	08-Dec-25 08:00 A	08-Dec-25 17:00 A	
UE150807-20	IDR - BOP Manual Valvess Specification	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A	
UE150807-25	Address Comments and issue for CR - BOP Manual Valves Spe	0d	16-Dec-25 08:00 A	16-Dec-25 17:00 A	
UE150807-30	Client Review - BOP Manual Valves Specification	0d	17-Dec-25 08:00 A	17-Dec-25 17:00 A	
UE150807-35	Address Client Comments and Finalize Spec. - BOP Manual Va	0d	18-Dec-25 08:00 A	18-Dec-25 17:00 A	
UE150807-40	Technical Evaluation of Bids - BOP Manual Valves	0d	14-Jun-26 08:00 A	19-Jun-26 17:00 A	
00373.3.19.1.9.11 Safety Showers					
UE150809-05	Prep/Check & Issue for IDR - Safety Showers & Eyewashes Spe	0d	18-Aug-25 08:00 A	29-Aug-25 17:00 A	
UE150809-20	IDR - Safety Showers & Eyewashes Specification	0d	02-Sep-25 08:00 A	08-Sep-25 17:00 A	
UE150809-25	Address Comments and issue for CR - Safety Showers & Eyewa	0d	09-Sep-25 08:00 A	10-Sep-25 17:00 A	
UE150809-30	Client Review - Safety Showers & Eyewashes Specification	0d	11-Sep-25 08:00 A	29-Sep-25 17:00 A	
UE150809-35	Address Client Comments and Finalize Spec. - Safety Showers	0d	30-Sep-25 08:00 A	24-Oct-25 08:00 A	
UE150809-40	Technical Evaluation of Bids - Safety Showers & Eyewashes Sp	0d	13-Feb-26 08:00 A	24-Mar-26 17:00 A	
00373.3.19.1.9.14 Lift Station					
UE150812-05	Prep/Check & Issue for IDR - Lift Station Specification	0d	18-Aug-25 08:00 A	19-Aug-25 17:00 A	
UE150812-10	IDR - Lift Station Specification	0d	19-Aug-25 08:00 A	19-Aug-25 17:00 A	
UE150812-15	Address Comments and issue for CR - Lift Station Specification	0d	19-Aug-25 08:00 A	20-Aug-25 17:00 A	
UE150812-20	Client Review - Lift Station Specification	0d	21-Aug-25 08:00 A	09-Sep-25 17:00 A	
UE150812-25	Address Client Comments and Finalize Spec. - Lift Station Spec	0d	10-Sep-25 08:00 A	22-Sep-25 08:00 A	
UE150812-30	Technical Evaluation of Bids - Lift Station Specification	0d	27-Oct-25 08:00 A	01-Dec-25 17:00 A	
00373.3.19.1.9.12 Expansion Joint Data Sheets					
UE150810-05	Prep, Check, and Issue IDR - Data Sheets - Expansion Joints	0d	05-Aug-25 08:00 A	08-Aug-25 08:00 A	
UE150810-10	IDR - Mechanical Data Sheets - Expansion Joints	0d	12-Aug-25 08:00 A	18-Aug-25 17:00 A	
UE150810-15	Address Comments and Issue for CR Data Sheets - Expansion	0d	20-Aug-25 08:00 A	28-Aug-25 17:00 A	
UE150810-20	Client Review - Data Sheets - Expansion Joints	0d	29-Aug-25 08:00 A	18-Sep-25 08:00 A	
UE150810-25	Address Client Comments and Issue IFC - Data Sheets - Expan	0d	19-Sep-25 08:00 A	26-Sep-25 08:00 A	
00373.3.19.1.9.13 Backflow Preventor Data Sheets					
UE150811-05	Prep, Check, and Issue IDR - Mechanical Lists/Data Sheets - B:	0d	12-Aug-25 08:00 A	25-Aug-25 17:00 A	
UE150811-10	IDR - Mechanical Lists/Data Sheets - Backflow Preventor	0d	26-Aug-25 08:00 A	02-Sep-25 17:00 A	

Remaining Level of Effort

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Milestone

Page 12 of 105

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	Gantt Chart																																																			
						2025 2026 2027 2028 2029 2030																																																			
UE150811-15	Address Comments and Issue for CR Mechanical Lists/Data Sh	0d	03-Sep-25 08:00 A	09-Sep-25 17:00 A		Address Comments and Issue for CR Mechanical Lists/Data Sheets - Backflow Preventor																																																			
UE150811-20	Client Review - Mechanical Lists/Data Sheets - Backflow Preven	0d	10-Sep-25 08:00 A	30-Sep-25 08:00 A		Client Review - Mechanical Lists/Data Sheets - Backflow Preventor																																																			
UE150811-25	Address Client Comments and Issue IFC - Mechanical Lists/Dat	0d	01-Oct-25 08:00 A	22-Oct-25 08:00 A		Address Client Comments and Issue IFC - Mechanical Lists/Data Sheets - Backflow Preventor																																																			
00373.3.19.1.2 Mechanical Subcontractor Specifications																																																									
00373.3.19.1.2.1 HVAC																																																									
UE150901-20	IDR Supply/Installation Specification - HVAC	0d	16-Feb-26 08:00 A	16-Feb-26 17:00 A		IDR Supply/Installation Specification - HVAC																																																			
UE150901-25	Address Comments and issue for CR Mech Spec - HVAC	0d	16-Feb-26 08:00 A	16-Feb-26 17:00 A		Address Comments and issue for CR Mech Spec - HVAC																																																			
UE150901-05	Prep/Check & Issue for CR Supply/Installation Specification - HV	0d	03-Mar-26 08:00 A	27-Mar-26 17:00 A		Prep/Check & Issue for CR Supply/Installation Specification - HVAC																																																			
UE150901-30	Client ReviewSupply/Installation - HVAC	0d	30-Mar-26 08:00 A	10-Apr-26 17:00 A		Client ReviewSupply/Installation - HVAC																																																			
UE150901-35	Address Client Comments and Finalize Spec. - HVAC	0d	13-Apr-26 08:00 A	23-Apr-26 08:00 A		Address Client Comments and Finalize Spec. - HVAC																																																			
00373.3.19.1.2.2 Fire Protection/Detection																																																									
UE150902-05	Prep/Check & Issue for IDR Supply/Installation Specification - Fi	0d	25-Jun-25 08:00 A	16-Jul-25 17:00 A		Prep/Check & Issue for IDR Supply/Installation Specification - Fire Protection/Detection																																																			
UE150902-20	IDR Supply/Installation Specification - Fire Protection/Detection	0d	17-Jul-25 08:00 A	23-Jul-25 17:00 A		IDR Supply/Installation Specification - Fire Protection/Detection																																																			
UE150902-25	Address Comments and issue for CR Supply/Installation Specifi	0d	24-Jul-25 08:00 A	29-Jul-25 17:00 A		Address Comments and issue for CR Supply/Installation Specification - Fire Protection/Detection																																																			
UE150902-30	Client Review Supply/Installation Specification - Fire Protection/I	0d	30-Jul-25 08:00 A	18-Aug-25 17:00 A		Client Review Supply/Installation Specification - Fire Protection/Detection																																																			
UE150902-35	Address Client Comments and Finalize Supply/Installation Spec	0d	19-Aug-25 08:00 A	09-Sep-25 17:00 A		Address Client Comments and Finalize Supply/Installation Specification. - Fire Protection/Detection																																																			
00373.3.19.1.2.3 Piping Insulation																																																									
UE150903-05	Prep/Check & Issue for IDR - Piping Insulation Supply/Installatio	0d	06-Oct-25 08:00 A	30-Oct-25 17:00 A		Prep/Check & Issue for IDR - Piping Insulation Supply/Installation Specification																																																			
UE150903-20	IDR - Piping Insulation Supply/Installation Specification	0d	31-Oct-25 08:00 A	06-Nov-25 17:00 A		IDR - Piping Insulation Supply/Installation Specification																																																			
UE150903-25	Address Comments and issue for CR - Piping Insulation Supply,	0d	07-Nov-25 08:00 A	26-Nov-25 08:00 A		Address Comments and issue for CR - Piping Insulation Supply/Installation Specification																																																			
UE150903-30	Client Review - Piping Insulation Supply/Installation Specificator	0d	01-Dec-25 08:00 A	09-Dec-25 08:00 A		Client Review - Piping Insulation Supply/Installation Specification																																																			
UE150903-35	Address Client Comments and Finalize Spec. - Piping Insulation	0d	10-Dec-25 08:00 A	09-Jan-26 17:00 A		Address Client Comments and Finalize Spec. - Piping Insulation Supply/Installation Specification																																																			
00373.3.19.1.1 Mechanical Lists																																																									
00373.3.19.1.1.1 Equipment List																																																									
UE150701-05	Prep, Check, and Issue IDR - Prelim Equip List	0d	05-Dec-24 08:00 A	20-Dec-24 17:00 A		Prep, Check, and Issue IDR - Prelim Equip List																																																			
UE150701-10	IDR - Prelim. Equip List	0d	30-Dec-24 08:00 A	03-Jan-25 17:00 A		IDR - Prelim. Equip List																																																			
UE150701-20	Address Comments and Issue for CR - Prelim.Equip List	0d	06-Jan-25 08:00 A	10-Jan-25 17:00 A		Address Comments and Issue for CR - Prelim.Equip List																																																			
UE150701-25	Client Review - Prelim. Equip List	0d	13-Jan-25 08:00 A	31-Jan-25 17:00 A		Client Review - Prelim. Equip List																																																			
UE150701-30	Address Client Comments and Issue IFD - Equip List	0d	03-Feb-25 08:00 A	24-Feb-25 00:00 A		Address Client Comments and Issue IFD - Equip List																																																			
PL3040	Air Compressors. Receivers, & Dryers - Final Vendor Drawings R	0d	02-Sep-25 08:00 A	19-Jan-26 17:00 A		Air Compressors. Receivers, & Dryers - Final Vendor Drawings Received																																																			
UE150701-35	Prep, Check, and Issue IFC - Final Equipment List	0d	15-May-26 08:00 A	02-Jun-26 17:00 A		Prep, Check, and Issue IFC - Final Equipment List																																																			
00373.3.19.1.1.6 Spare Parts List																																																									
UE150701-45	Prep, Check, and Issue - Spare Parts List	15d	08-Oct-26 08:00	28-Oct-26 17:00	143d	Prep, Check, and Issue - Spare Parts List																																																			
UE150701-95	Address Comments & Issue IFC - Spare Parts List	10d	29-Oct-26 08:00	11-Nov-26 17:00	143d	Address Comments & Issue IFC - Spare Parts List																																																			
00373.3.19.1.1.2 Piping Line List																																																									
UE150702-05	Prep, Check, and Issue IDR - Mechanical Lists - Line List	0d	02-Jun-25 08:00 A	09-Jul-25 17:00 A		Prep, Check, and Issue IDR - Mechanical Lists - Line List																																																			
UE150702-10	IDR - Mechanical Lists/Data Sheets - Line List	0d	10-Jul-25 08:00 A	16-Jul-25 17:00 A		IDR - Mechanical Lists/Data Sheets - Line List																																																			
UE150702-15	Address Comments and Issue for CR - Mechanical Lists/Data S	0d	17-Jul-25 08:00 A	26-Aug-25 17:00 A		Address Comments and Issue for CR - Mechanical Lists/Data Sheets - Line List																																																			
UE150702-20	Client Review - Mechanical Lists/Data Sheets - Line List	0d	27-Aug-25 08:00 A	16-Sep-25 17:00 A		Client Review - Mechanical Lists/Data Sheets - Line List																																																			
UE150702-25	Address Client Comments and Issue IFC - Mechanical Lists/Dat	0d	17-Sep-25 08:00 A	09-Oct-25 08:00 A		Address Client Comments and Issue IFC - Mechanical Lists/Data Sheets - Line List																																																			
00373.3.19.1.1.3 Valve List																																																									
UE150703-05	Prep, Check, and Issue IDR - Mechanical Lists/Data Sheets - Ve	0d	02-Jun-25 08:00 A	09-Jul-25 17:00 A		Prep, Check, and Issue IDR - Mechanical Lists/Data Sheets - Valve List																																																			
UE150703-10	IDR - Mechanical Lists/Data Sheets - Valve List	0d	10-Jul-25 08:00 A	16-Jul-25 17:00 A		IDR - Mechanical Lists/Data Sheets - Valve List																																																			
UE150703-15	Address Comments and Issue for CR Mechanical Lists/Data Sh	0d	17-Jul-25 08:00 A	25-Aug-25 17:00 A		Address Comments and Issue for CR Mechanical Lists																																																			


Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	
	UE161142-15	Address IDR Comments and Issue for CR - Equipment GA Dwg.	0d	03-Mar-25 08:00 A	14-Mar-25 17:00 A	
	UE161142-20	Client Review - Equipment GA Dwg. - Plant Services Area	0d	17-Mar-25 08:00 A	03-Apr-25 00:00 A	
	UE161142-25	Address Client Comments Issue for Purpose - Equipment GA C	0d	04-Apr-25 08:00 A	08-May-25 17:00 A	
00373.3.19.3.4.3.4 Fuel Gas Area						
	UE161146-05	Prep, Check, and Issue IDR . - Equipment GA Drawing - Fuel G	0d	23-Jan-25 08:00 A	31-Jan-25 00:00 A	
	UE161146-10	IDR - Equipment GA Dwg. - Fuel Gas Area	0d	03-Feb-25 08:00 A	07-Feb-25 17:00 A	
	UE161146-15	Address IDR Comments and Issue for CR - Equipment GA Dwg.	0d	10-Feb-25 08:00 A	21-Feb-25 17:00 A	
	UE161146-20	Client Review - Equipment GA Dwg. - Fuel Gas Area	0d	24-Feb-25 08:00 A	13-Mar-25 17:00 A	
	UE161146-25	Address Client Comments Issue for Purpose - Equipment GA C	0d	10-Apr-25 08:00 A	06-May-25 17:00 A	
00373.3.19.3.4.6 Underground Piping						
	UE161100-10	Preliminary UG Pipe Model	0d	24-Apr-25 08:00 A	20-Jun-25 17:00 A	
	UE161100-25	Final U/G Pipe Model	0d	20-Jun-25 08:00 A	01-Aug-25 17:00 A	
00373.3.19.3.4.6.1 Underground Piping						
	UE161150-05	Prep, Check, and Issue IDR Piping Drawings - U/G Piping	0d	23-Jun-25 08:00 A	15-Aug-25 17:00 A	
	UE161150-10	IDR Piping Drawings - U/G Piping	0d	18-Aug-25 08:00 A	09-Sep-25 17:00 A	
	UE161150-15	Address Comments and Issue for CR Piping Drawings - U/G Pip	0d	10-Sep-25 08:00 A	26-Sep-25 17:00 A	
	UE161150-20	Client Review Piping Drawings - U/G Piping	0d	29-Sep-25 08:00 A	09-Oct-25 17:00 A	
	UE161150-30	Finalize Dwg, & Issue IFC - U/G Piping	0d	10-Oct-25 08:00 A	31-Oct-25 17:00 A	
00373.3.19.3.4.4 P&IDs						
00373.3.19.3.4.4.16 P&ID Index & Lead Sheets						
	UE161190-05	Prep, Check, and Issue IDR Piping Drawings - P&ID - Drawing Ir	0d	07-Jan-25 08:00 A	31-Jan-25 00:00 A	
	UE161190-10	IDR Piping Drawings - P&ID - Drawing Index & Lead Sheets	0d	03-Feb-25 08:00 A	14-Feb-25 17:00 A	
	UE161190-15	Address Comments and Issue for CR Piping Drawings - P&ID - I	0d	18-Feb-25 08:00 A	24-Feb-25 00:00 A	
	UE161190-20	Client Review Piping Drawings - P&ID - Drawing Index & Lead S	0d	25-Feb-25 08:00 A	10-Mar-25 00:00 A	
	UE161190-25	Address Client Comments and Issue IFD Piping Drawings - P&I	0d	11-Mar-25 08:00 A	11-Apr-25 17:00 A	
	UE161190-30	Address Client Comments and Issue IFC Piping Drawings - P&I	0d	15-Sep-25 08:00 A	26-Sep-25 17:00 A	
00373.3.19.3.4.4.1 Fuel Gas						
	UE161101-05	Prep, Check, and Issue IDR P&ID's - Fuel Gas	0d	10-Feb-25 08:00 A	11-Mar-25 00:00 A	
	UE161101-10	IDR P&ID's - Fuel Gas	0d	12-Mar-25 08:00 A	25-Mar-25 17:00 A	
	UE161101-15	Address Comments and Issue for CR P&ID's - Fuel Gas	0d	26-Mar-25 08:00 A	03-Apr-25 17:00 A	
	UE161101-20	Client Review P&ID's - Fuel Gas	0d	04-Apr-25 08:00 A	21-Apr-25 17:00 A	
	UE161101-25	Address Client Comments and Issue IFD P&ID's - Fuel Gas	0d	22-Apr-25 08:00 A	15-May-25 17:00 A	
00373.3.19.3.4.4.2 Fuel Oil						
	UE161102-05	Prep, Check, and Issue IDR P&ID's - Fuel Oil	0d	10-Feb-25 08:00 A	12-Mar-25 17:00 A	
	UE161102-10	IDR P&ID's - Fuel Oil	0d	13-Mar-25 08:00 A	26-Mar-25 17:00 A	
	UE161102-15	Address Comments and Issue for CR P&ID's - Fuel Oil	0d	27-Mar-25 08:00 A	04-Apr-25 00:00 A	
	UE161102-20	Client Review P&ID's - Fuel Oil	0d	07-Apr-25 08:00 A	21-Apr-25 17:00 A	
	UE161102-25	Address Client Comments and Issue IFD P&ID's - Fuel Oil	0d	22-Apr-25 08:00 A	05-May-25 17:00 A	
00373.3.19.3.4.4.3 Demineralized Water						
	UE161103-05	Prep, Check, and Issue IDR P&ID's - Demineralized Water	0d	25-Feb-25 08:00 A	25-Mar-25 00:00 A	
	UE161103-10	IDR P&ID's - Demineralized Water	0d	26-Mar-25 08:00 A	08-Apr-25 17:00 A	
	UE161103-15	Address Comments and Issue for CR P&ID's - Demineralized W	0d	09-Apr-25 08:00 A	17-Apr-25 17:00 A	
	UE161103-20	Client Review P&ID's - Demineralized Water	0d	17-Apr-25 08:00 A	28-Apr-25 17:00 A	
	UE161103-25	Address Client Comments and Issue IFD P&ID's - Demineralize	0d	29-Apr-25 08:00 A	07-May-25 17:00 A	
00373.3.19.3.4.4.4 Service Water						
	UE161104-05	Prep, Check, and Issue IDR P&ID's - Service Water	0d	31-Jan-25 08:00 A	27-Feb-25 17:00 A	
	UE161104-10	IDR P&ID's - Service Water	0d	28-Feb-25 08:00 A	13-Mar-25 17:00 A	
	UE161104-15	Address Comments and Issue for CR P&ID's - Service Water	0d	14-Mar-25 08:00 A	21-Mar-25 00:00 A	
	UE161104-20	Client Review P&ID's - Service Water	0d	24-Mar-25 08:00 A	08-Apr-25 00:00 A	
	UE161104-25	Address Client Comments and Issue IFD P&ID's - Service Wate	0d	09-Apr-25 08:00 A	05-May-25 08:00 A	
00373.3.19.3.4.4.5 Closed Cooling Water						

Remaining Level of Effort

Actual Level of Effort

[illegible]


[illegible]

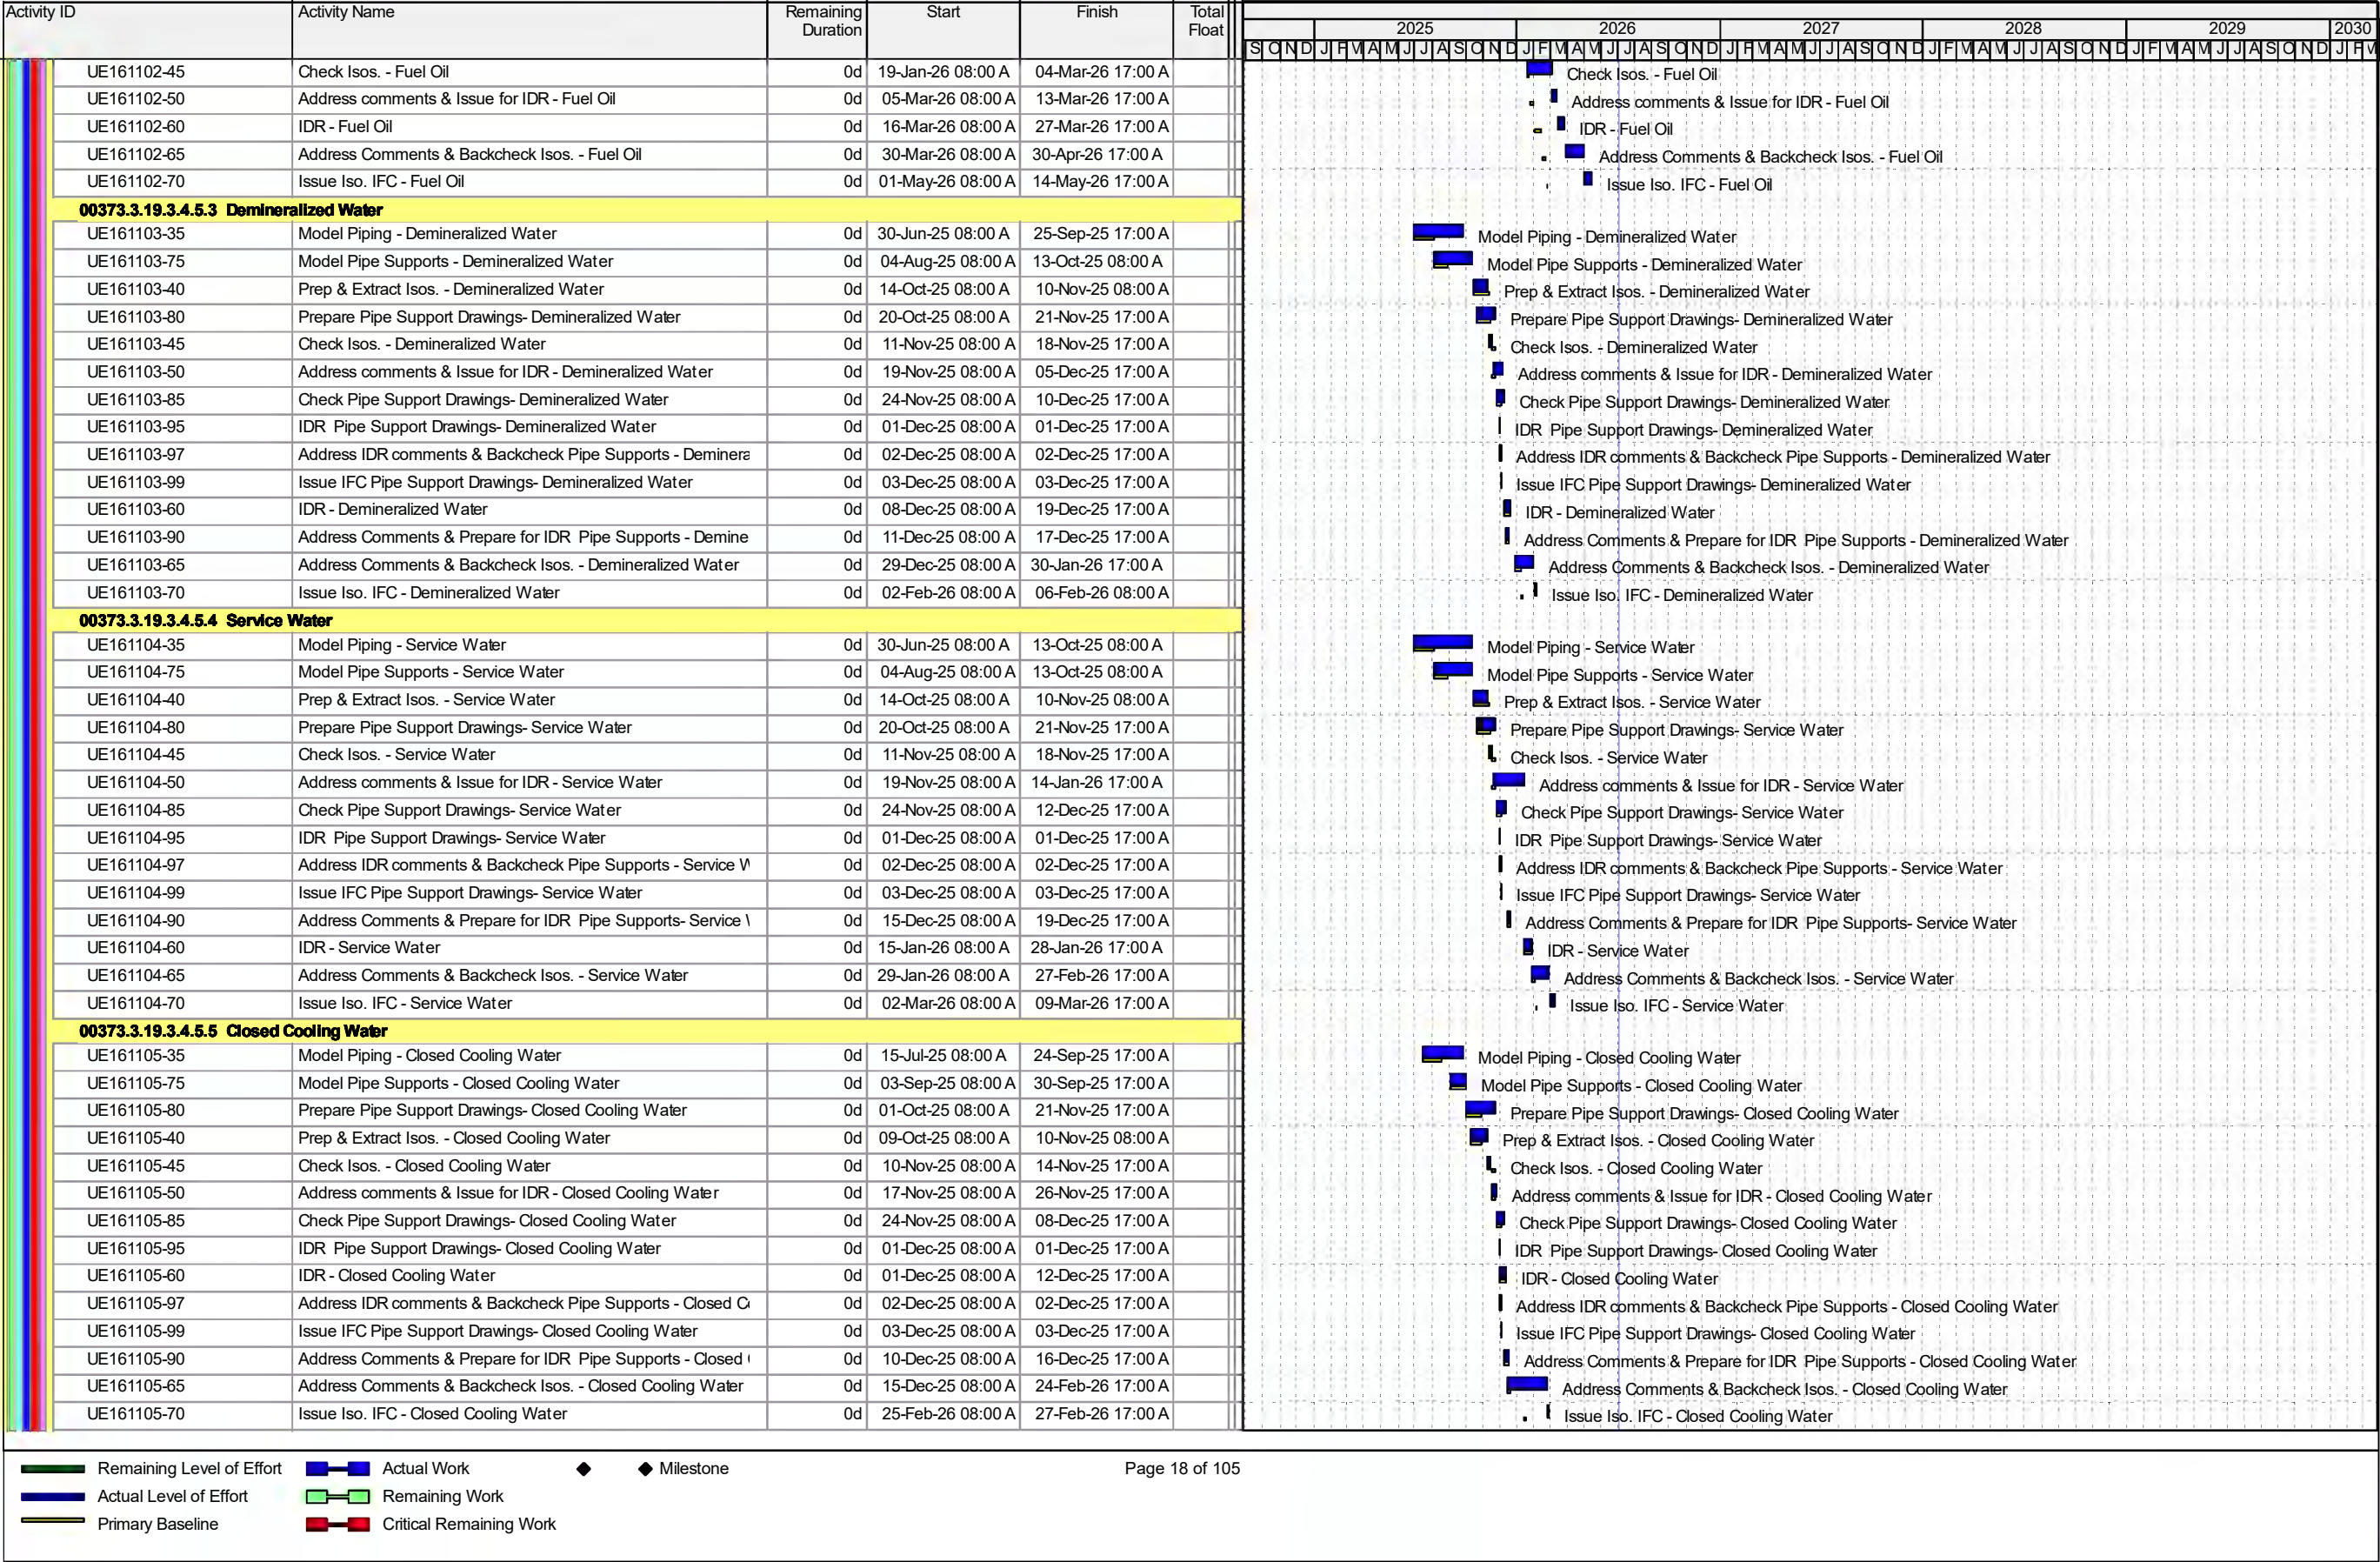



Page 18 of 105


[illegible]

[illegible]

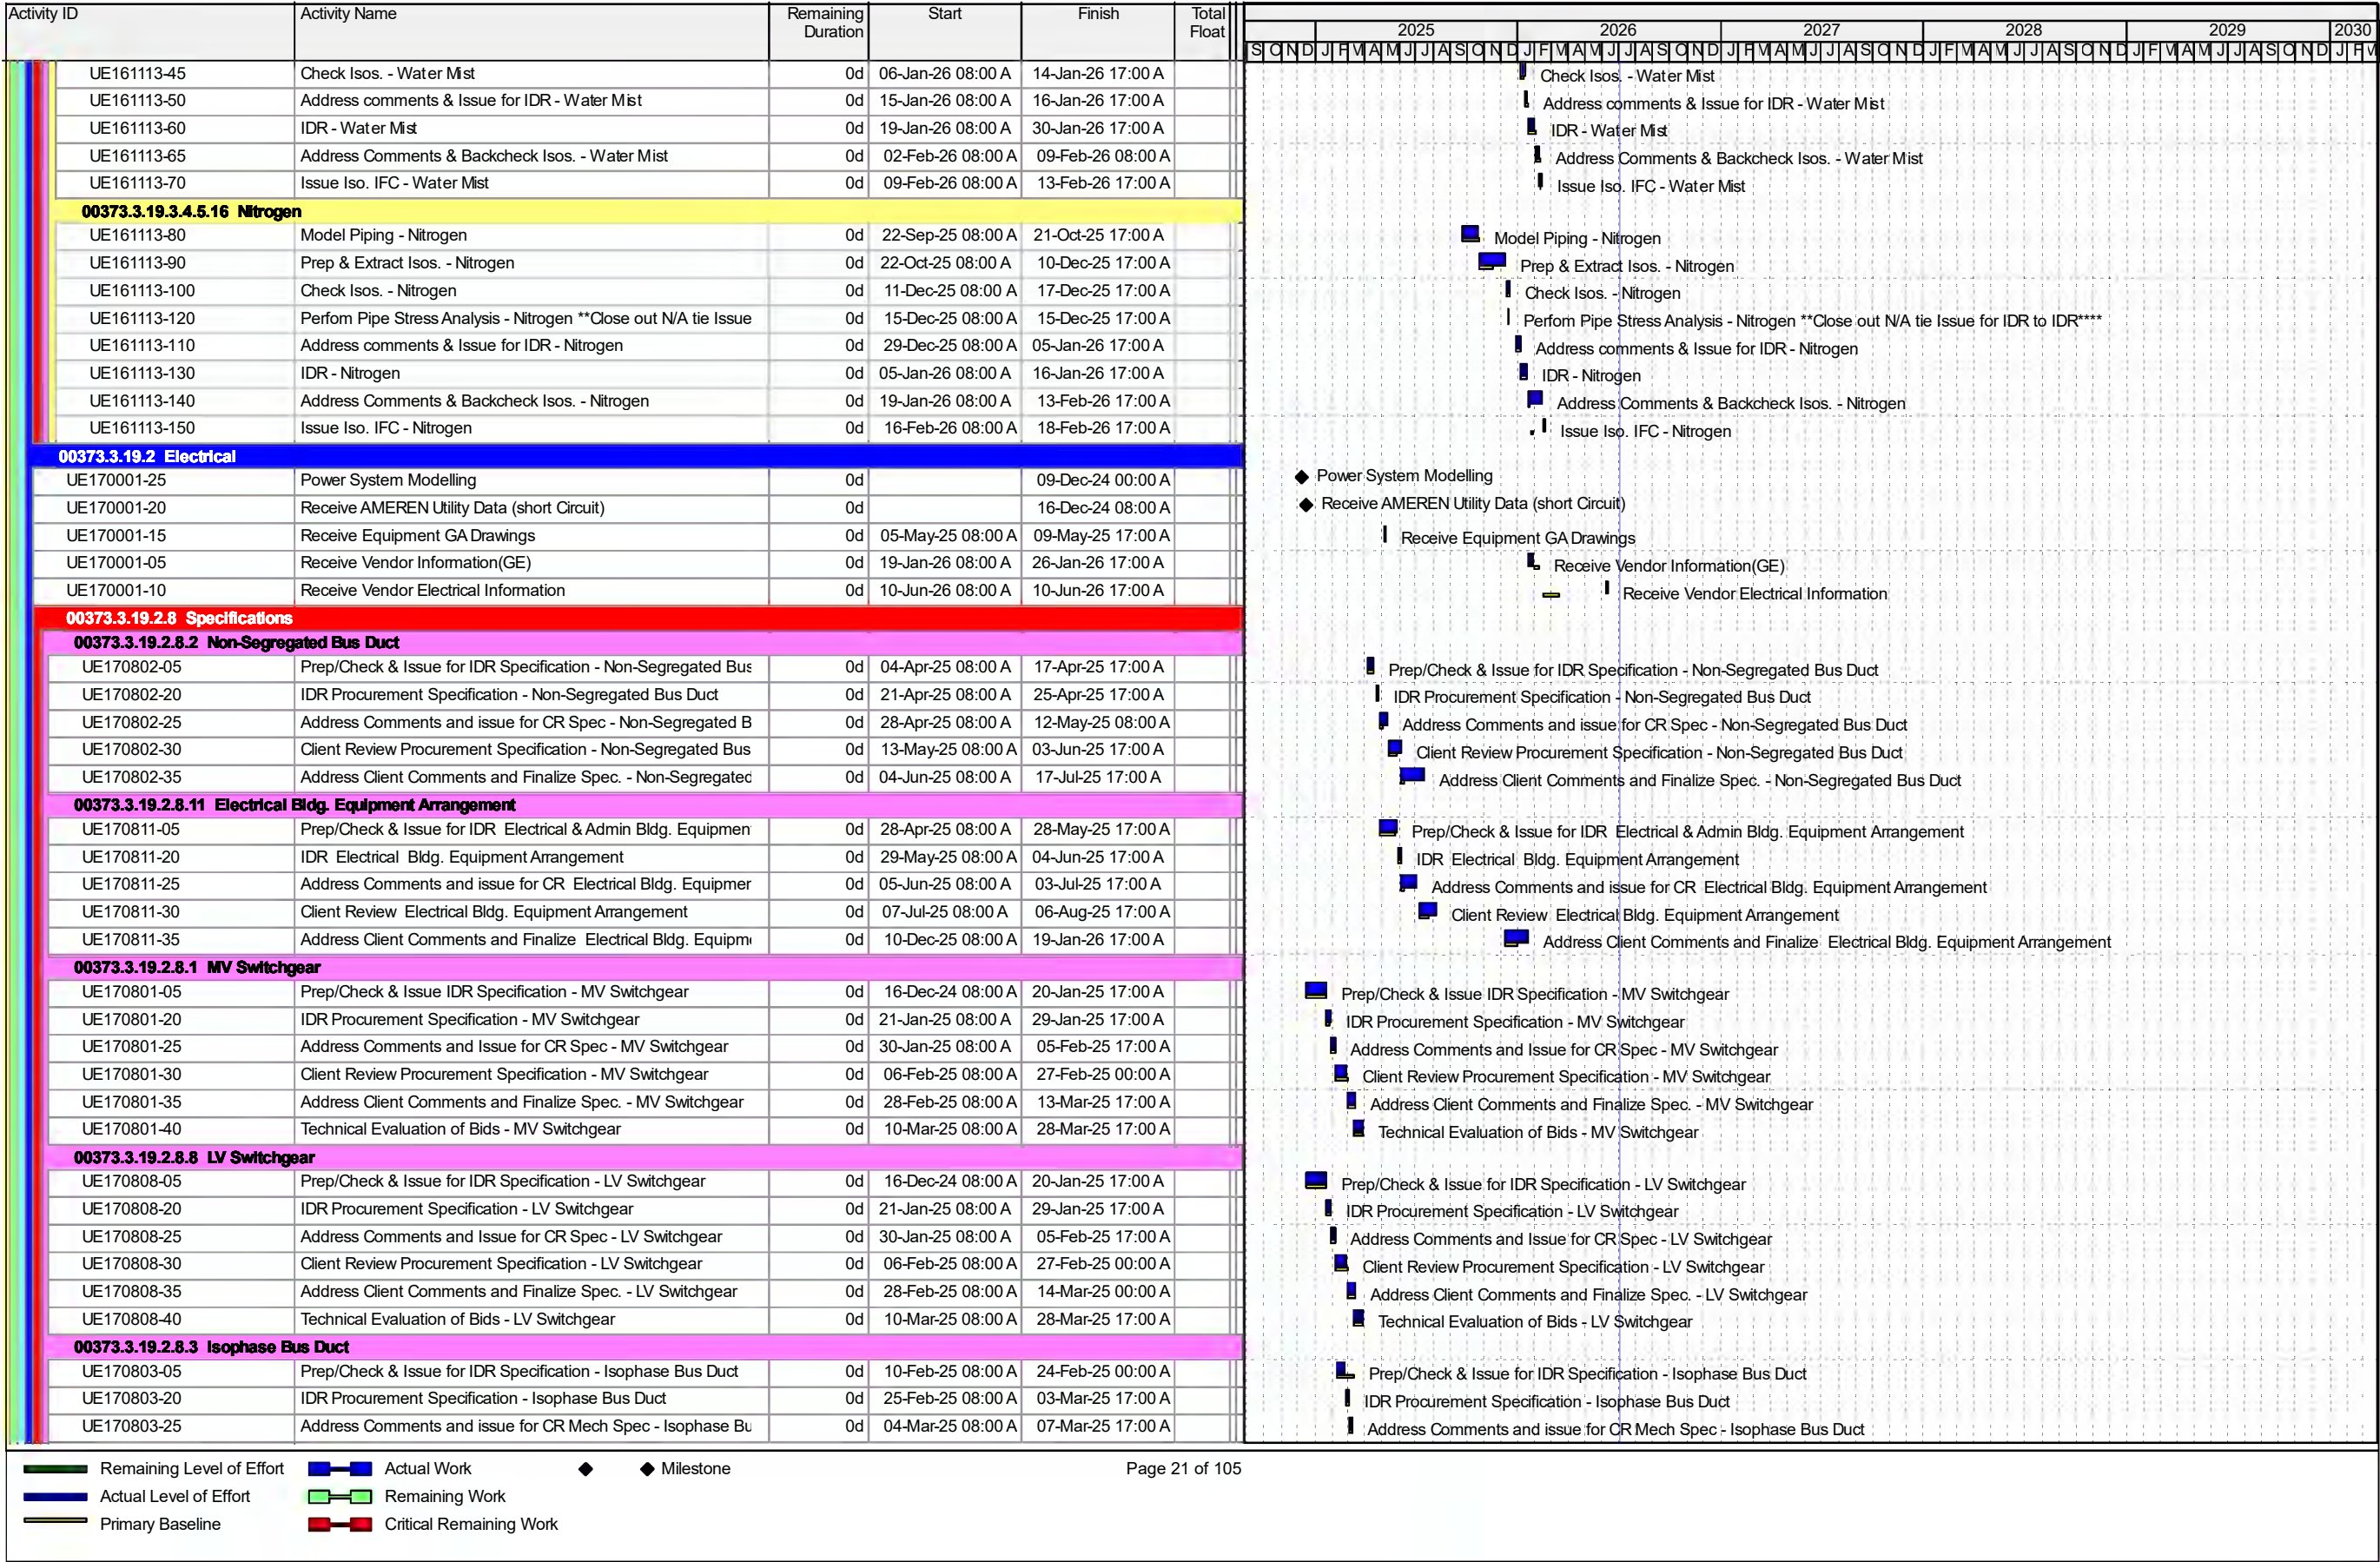

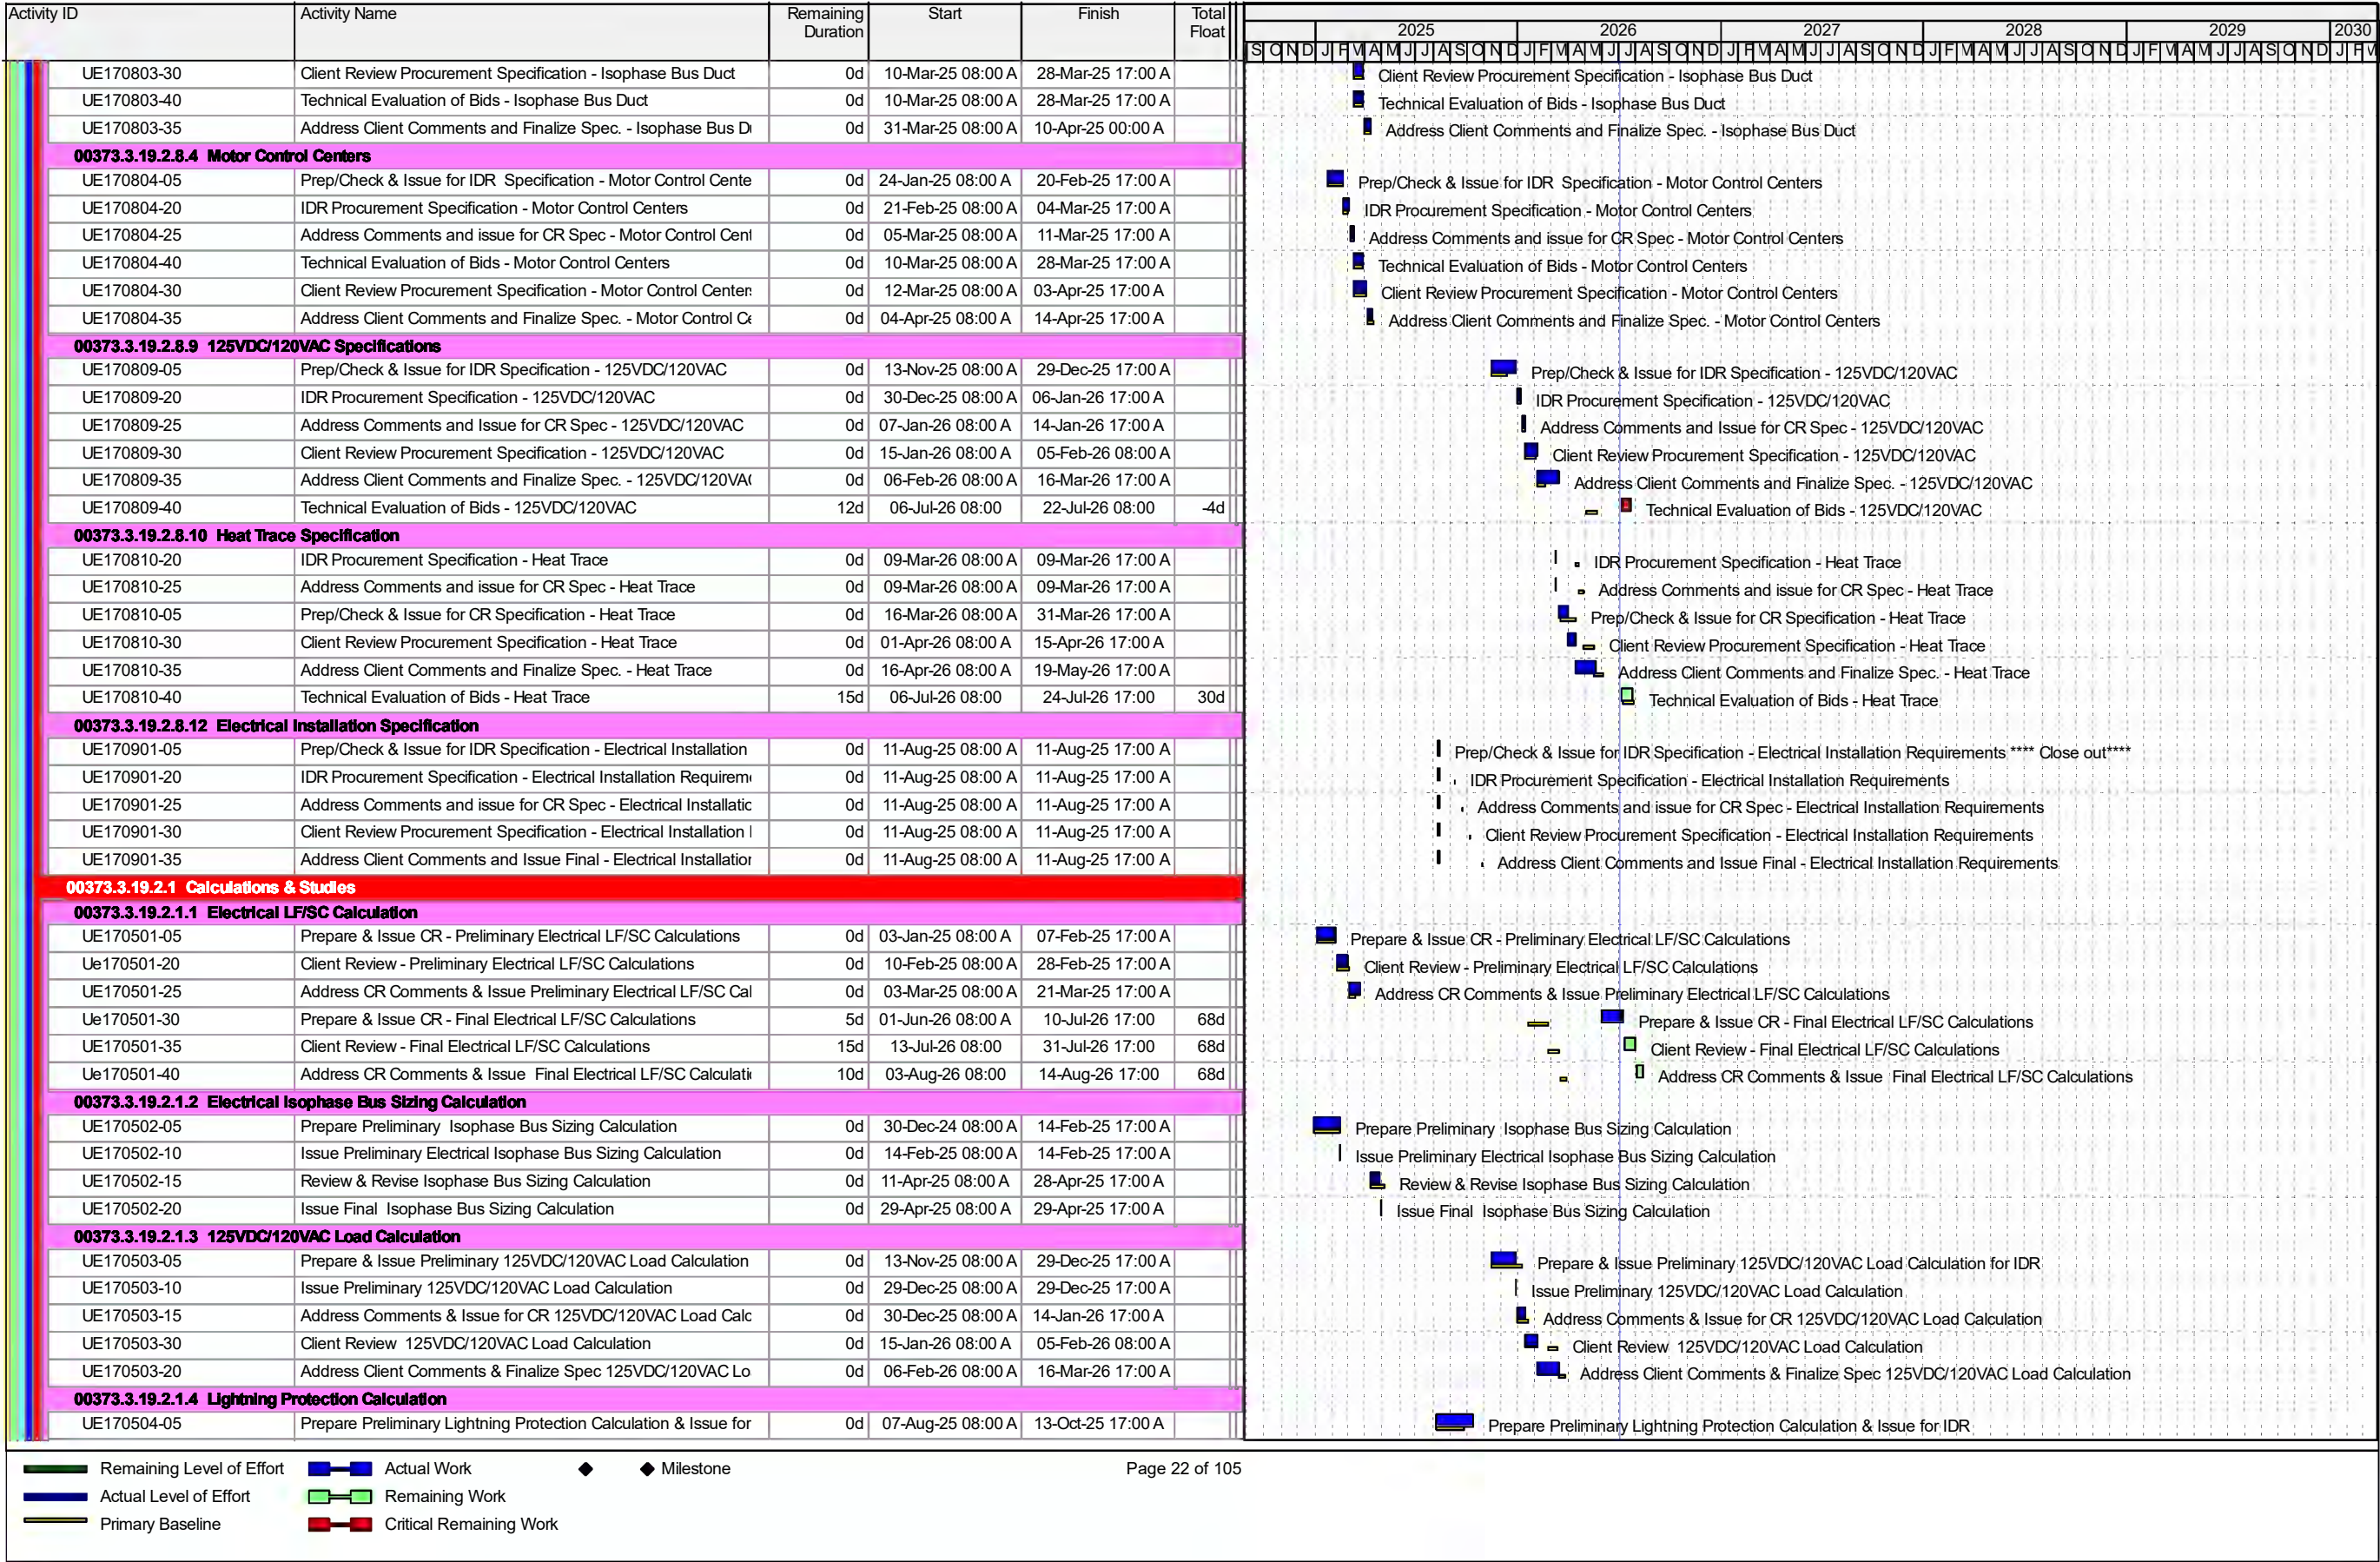


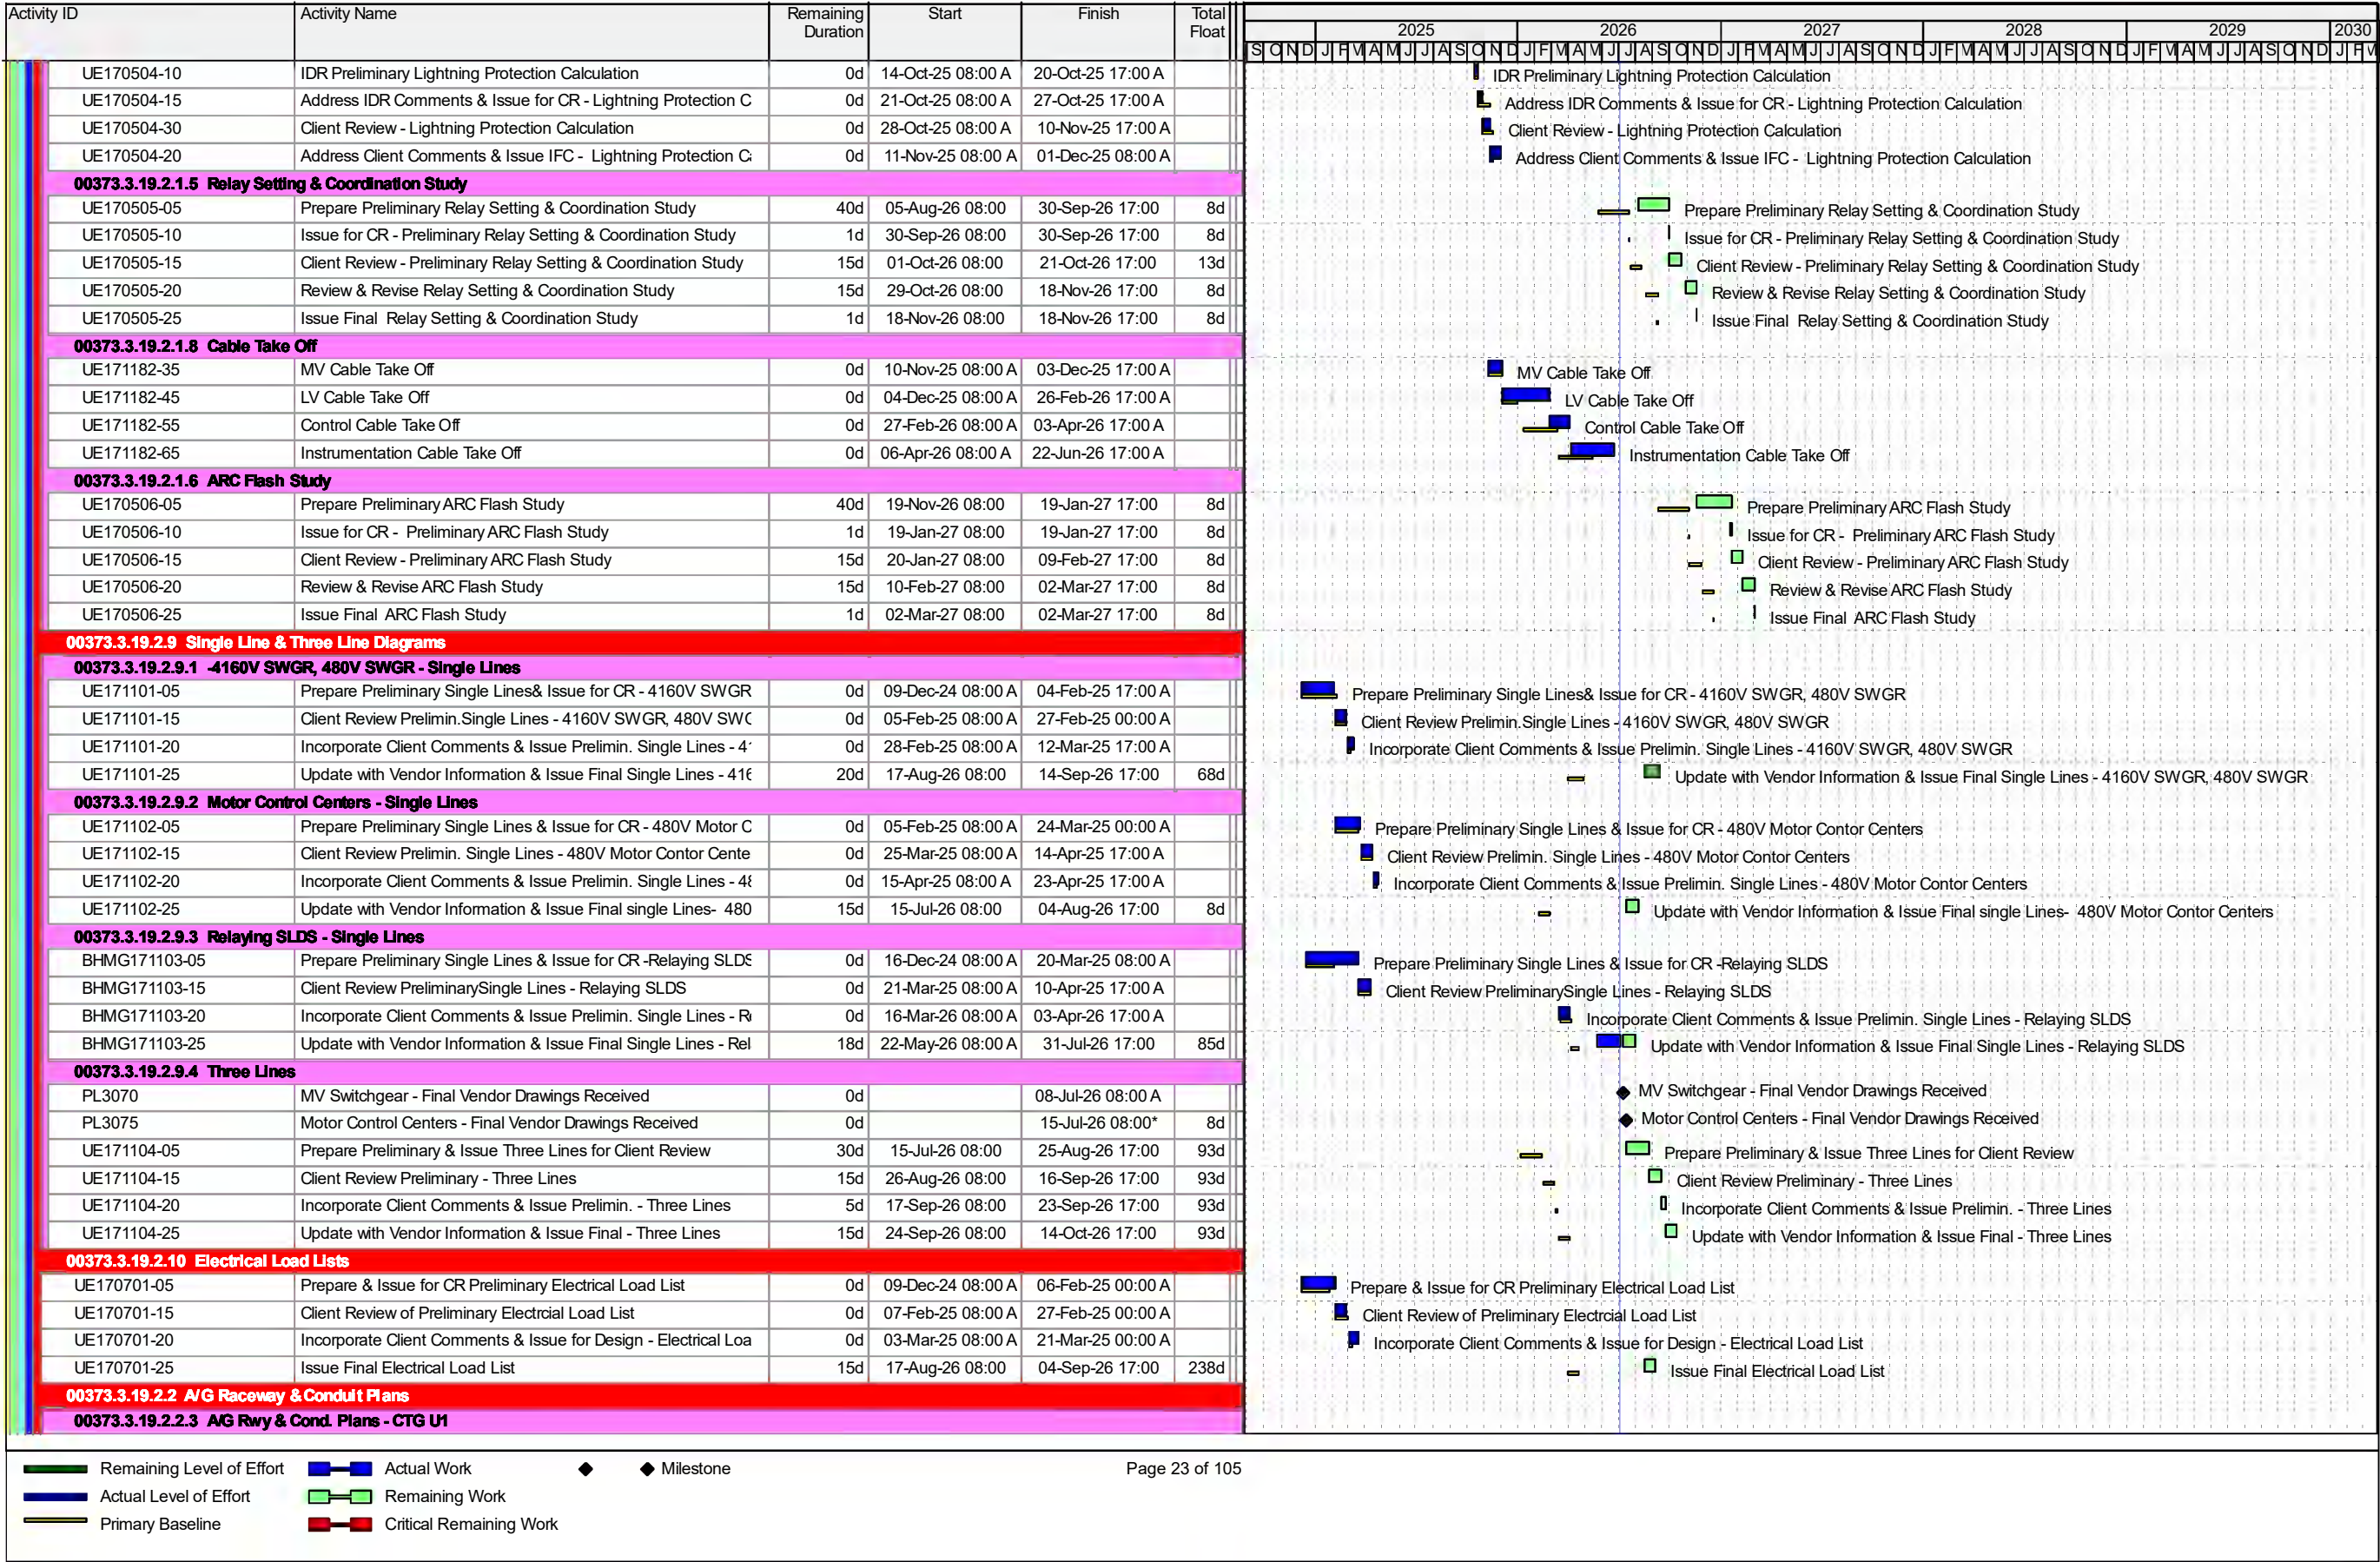


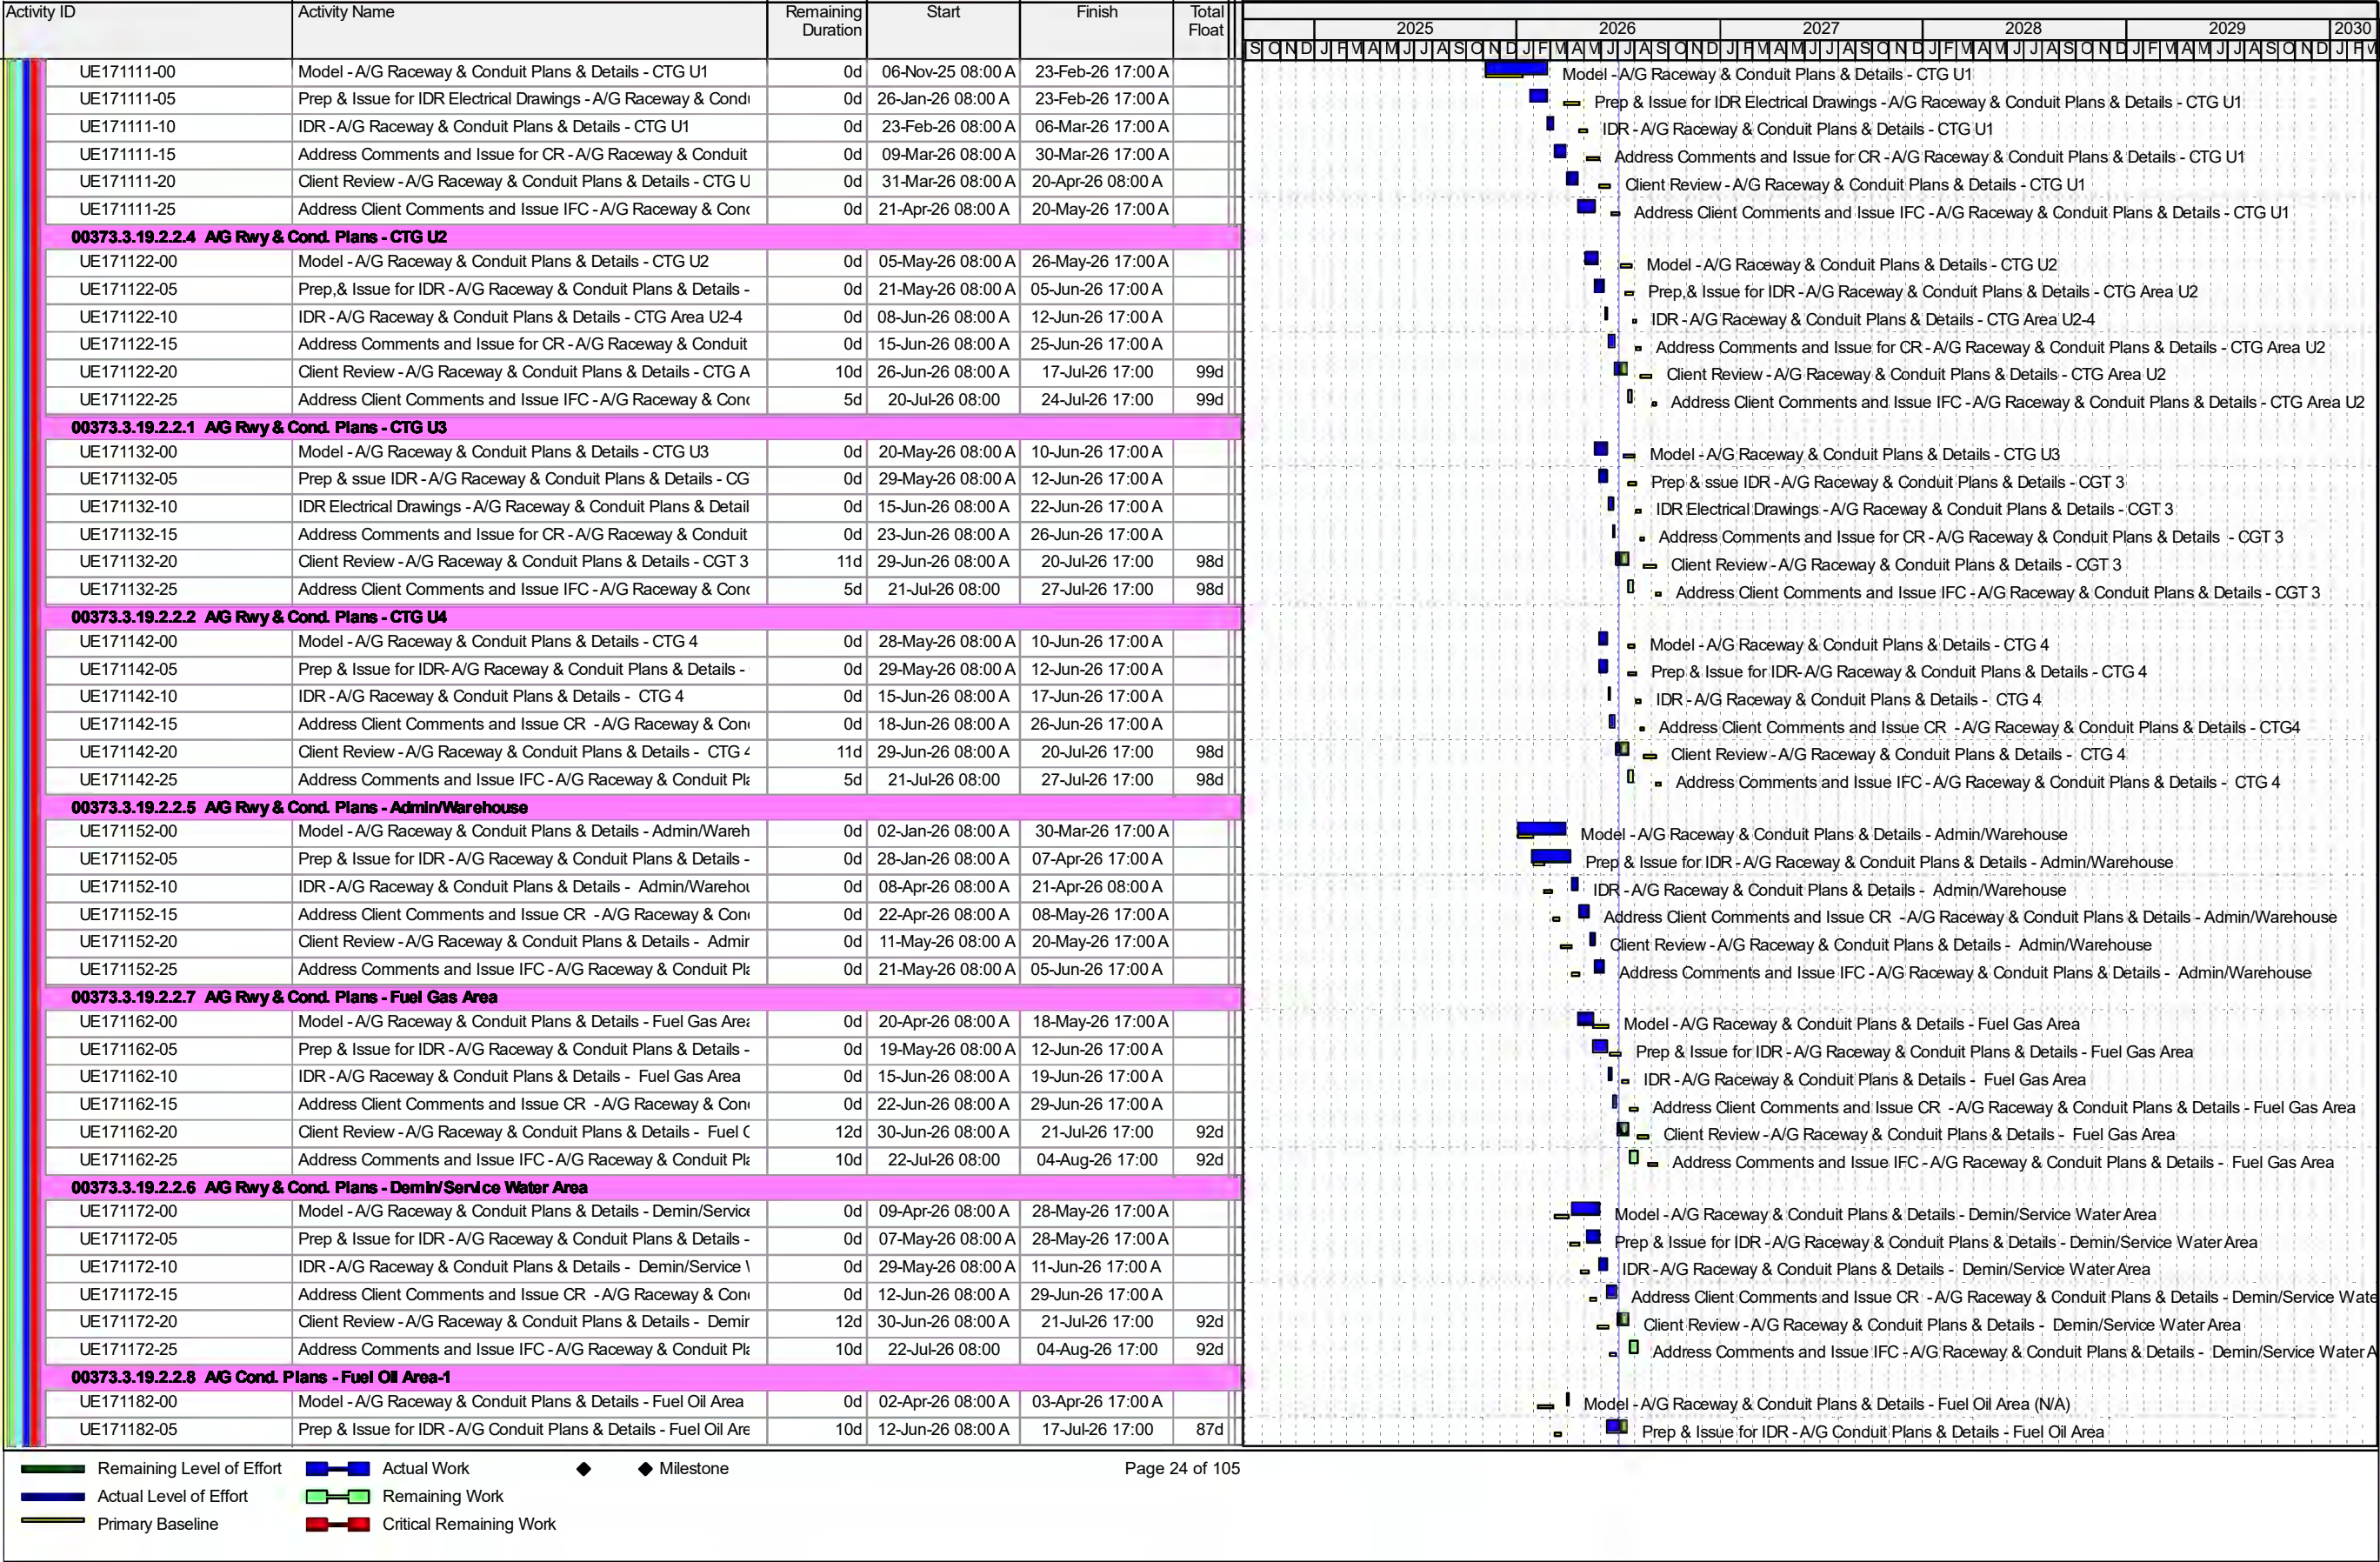


Page 24 of 105

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
UE171182-10	IDR - A/G Conduit Plans & Details - Fuel Oil Area	10d	20-Jul-26 08:00	31-Jul-26 17:00	120d
UE171182-15	Address IDR Comments and Issue CR -A/G Conduit Plans & D	10d	03-Aug-26 08:00	14-Aug-26 17:00	120d
UE171182-20	Client Review -A/G Conduit Plans & Details - Fuel Oil Area	15d	17-Aug-26 08:00	04-Sep-26 17:00	120d
UE171182-25	Address Comments and Issue IFC -A/G Conduit Plans & Detail	10d	08-Sep-26 08:00	21-Sep-26 17:00	120d
00373.3.19.2.4 U/G Raceway Plans					
00373.3.19.2.4.3 U/G Rwy & Cond. Plans - CTG U1					
UE171116-05	Prep & Issue for IDR - UG Raceway Plans & Details - CTG 1	0d	02-Apr-25 08:00 A	19-May-25 17:00 A	
UE171116-00	Model - U/G Raceway Plans & Details - CTG 1	0d	05-May-25 08:00 A	14-Jul-25 17:00 A	
UE171116-10	IDR - UG Raceway Plans & Details - CTG 1	0d	20-May-25 08:00 A	03-Jun-25 17:00 A	
UE171116-15	Address Comments and Issue for CR - U/G Raceway Plans & D	0d	04-Jun-25 08:00 A	30-Jun-25 17:00 A	
UE171116-20	Client Review - UG Raceway Plans & Details - CTG 1	0d	01-Jul-25 08:00 A	21-Jul-25 08:00 A	
UE171116-25	Address Client Comments and Issue IFC - Ductbank Plans & De	0d	22-Jul-25 08:00 A	29-Aug-25 08:00 A	
UE171116-45	Client Review - UG Raceway Plans & Details (Embedded Condi	0d	01-Oct-25 08:00 A	08-Oct-25 17:00 A	
UE171116-35	Address Client Comments and Issue IFC - U/G Raceway Plans	0d	09-Oct-25 08:00 A	27-Oct-25 17:00 A	
00373.3.19.2.4.4 U/G Rwy & Cond. Plans - CTG U2					
UE171126-00	Model - U/G Raceway & Conduit Plans & Details - CTG U2	0d	04-Jun-25 08:00 A	24-Sep-25 17:00 A	
UE171126-05	Prep & Issue for IDR - U/G Raceway & Conduit Plans & Details -	0d	14-Jul-25 08:00 A	25-Jul-25 17:00 A	
UE171126-10	IDR - U/G Raceway & Conduit Plans & Details - CTG Area U2	0d	28-Jul-25 08:00 A	01-Aug-25 17:00 A	
UE171126-15	Address Comments and Issue for CR - U/G Raceway & Conduit	0d	04-Aug-25 08:00 A	18-Nov-25 17:00 A	
UE171126-20	Client Review - U/G Raceway & Conduit Plans & Details - CTG L	0d	19-Nov-25 08:00 A	01-Dec-25 17:00 A	
UE171126-25	Address Client Comments and Issue IFC - U/G Raceway & Coni	0d	24-Nov-25 08:00 A	12-Dec-25 17:00 A	
UE171126-35	Address Client Comments and Issue IFC - U/G Raceway & Coni	0d	01-Dec-25 08:00 A	12-Dec-25 17:00 A	
00373.3.19.2.4.1 U/G Rwy & Cond. Plans - CTG U3					
UE171136-00	Model - U/G Raceway & Conduit Plans & Details - CTG U3	0d	26-Nov-25 08:00 A	30-Dec-25 17:00 A	
UE171136-05	Prep & Issue IDR - U/G Raceway & Conduit Plans & Details - CGT	0d	05-Dec-25 08:00 A	19-Dec-25 17:00 A	
UE171136-10	IDR Electrical Drawings - U/G Raceway & Conduit Plans & Detail	0d	29-Dec-25 08:00 A	05-Jan-26 17:00 A	
UE171136-15	Address Comments and Issue for CR - U/G Raceway & Conduit	0d	06-Jan-26 08:00 A	13-Jan-26 17:00 A	
UE171136-20	Client Review - U/G Raceway & Conduit Plans & Details - CGT 3	0d	14-Jan-26 08:00 A	21-Jan-26 17:00 A	
UE171136-25	Address Client Comments and Issue IFC - U/G Raceway & Coni	0d	22-Jan-26 08:00 A	05-Feb-26 08:00 A	
UE171136-35	Address Client Comments and Issue IFC - U/G Raceway & Coni	0d	22-Jan-26 08:00 A	05-Feb-26 08:00 A	
00373.3.19.2.4.2 U/G Rwy & Cond. Plans - CTG U4					
UE171146-00	Model - U/G Raceway & Conduit Plans & Details - CTG 4	0d	15-Dec-25 08:00 A	15-Jan-26 17:00 A	
UE171146-05	Prep & Issue for IDR- U/G Raceway & Conduit Plans & Details -	0d	05-Jan-26 08:00 A	16-Jan-26 17:00 A	
UE171146-15	Address Client Comments and Issue CR - U/G Raceway & Con	0d	12-Jan-26 08:00 A	16-Jan-26 17:00 A	
UE171146-10	IDR -U/G Raceway & Conduit Plans & Details - CTG 4	0d	19-Jan-26 08:00 A	23-Jan-26 17:00 A	
UE171146-20	Client Review - U/G Raceway & Conduit Plans & Details - CTG 4	0d	19-Jan-26 08:00 A	27-Jan-26 17:00 A	
UE171146-25	Address Comments and Issue IFC - U/G Raceway & Conduit Pl	0d	28-Jan-26 08:00 A	05-Feb-26 08:00 A	
UE171146-35	Address Comments and Issue IFC - U/G Raceway & Conduit Pl	0d	28-Jan-26 08:00 A	05-Feb-26 08:00 A	
00373.3.19.2.4.5 U/G Rwy & Cond. Plans -Admin/Warehouse					
UE171156-00	Model - U/G Raceway & Conduit Plans & Details - Admin/Wareh	0d	08-Dec-25 08:00 A	09-Feb-26 17:00 A	
UE171156-05	Prep & Issue for IDR - U/G Raceway & Conduit Plans & Details -	0d	13-Jan-26 08:00 A	09-Feb-26 17:00 A	
UE171156-15	Address Client Comments and Issue CR - U/G Raceway & Con	0d	28-Jan-26 08:00 A	10-Feb-26 17:00 A	
UE171156-10	IDR - U/G Raceway & Conduit Plans & Details - Admin/Warehoi	0d	10-Feb-26 08:00 A	23-Feb-26 17:00 A	
UE171156-20	Client Review - U/G Raceway & Conduit Plans & Details - Admir	0d	11-Feb-26 08:00 A	24-Feb-26 17:00 A	
UE171156-25	Address Comments and Issue IFC - U/G Raceway & Conduit Pl	0d	25-Feb-26 08:00 A	12-Mar-26 17:00 A	
00373.3.19.2.4.6 U/G Rwy & Cond. Plans -Demin/Service Water Area					
UE171176-12	Return Comments on Field Erected Fisher Tank Drawings - Den	0d	04-Feb-26 08:00 A	04-Feb-26 17:00 A</	

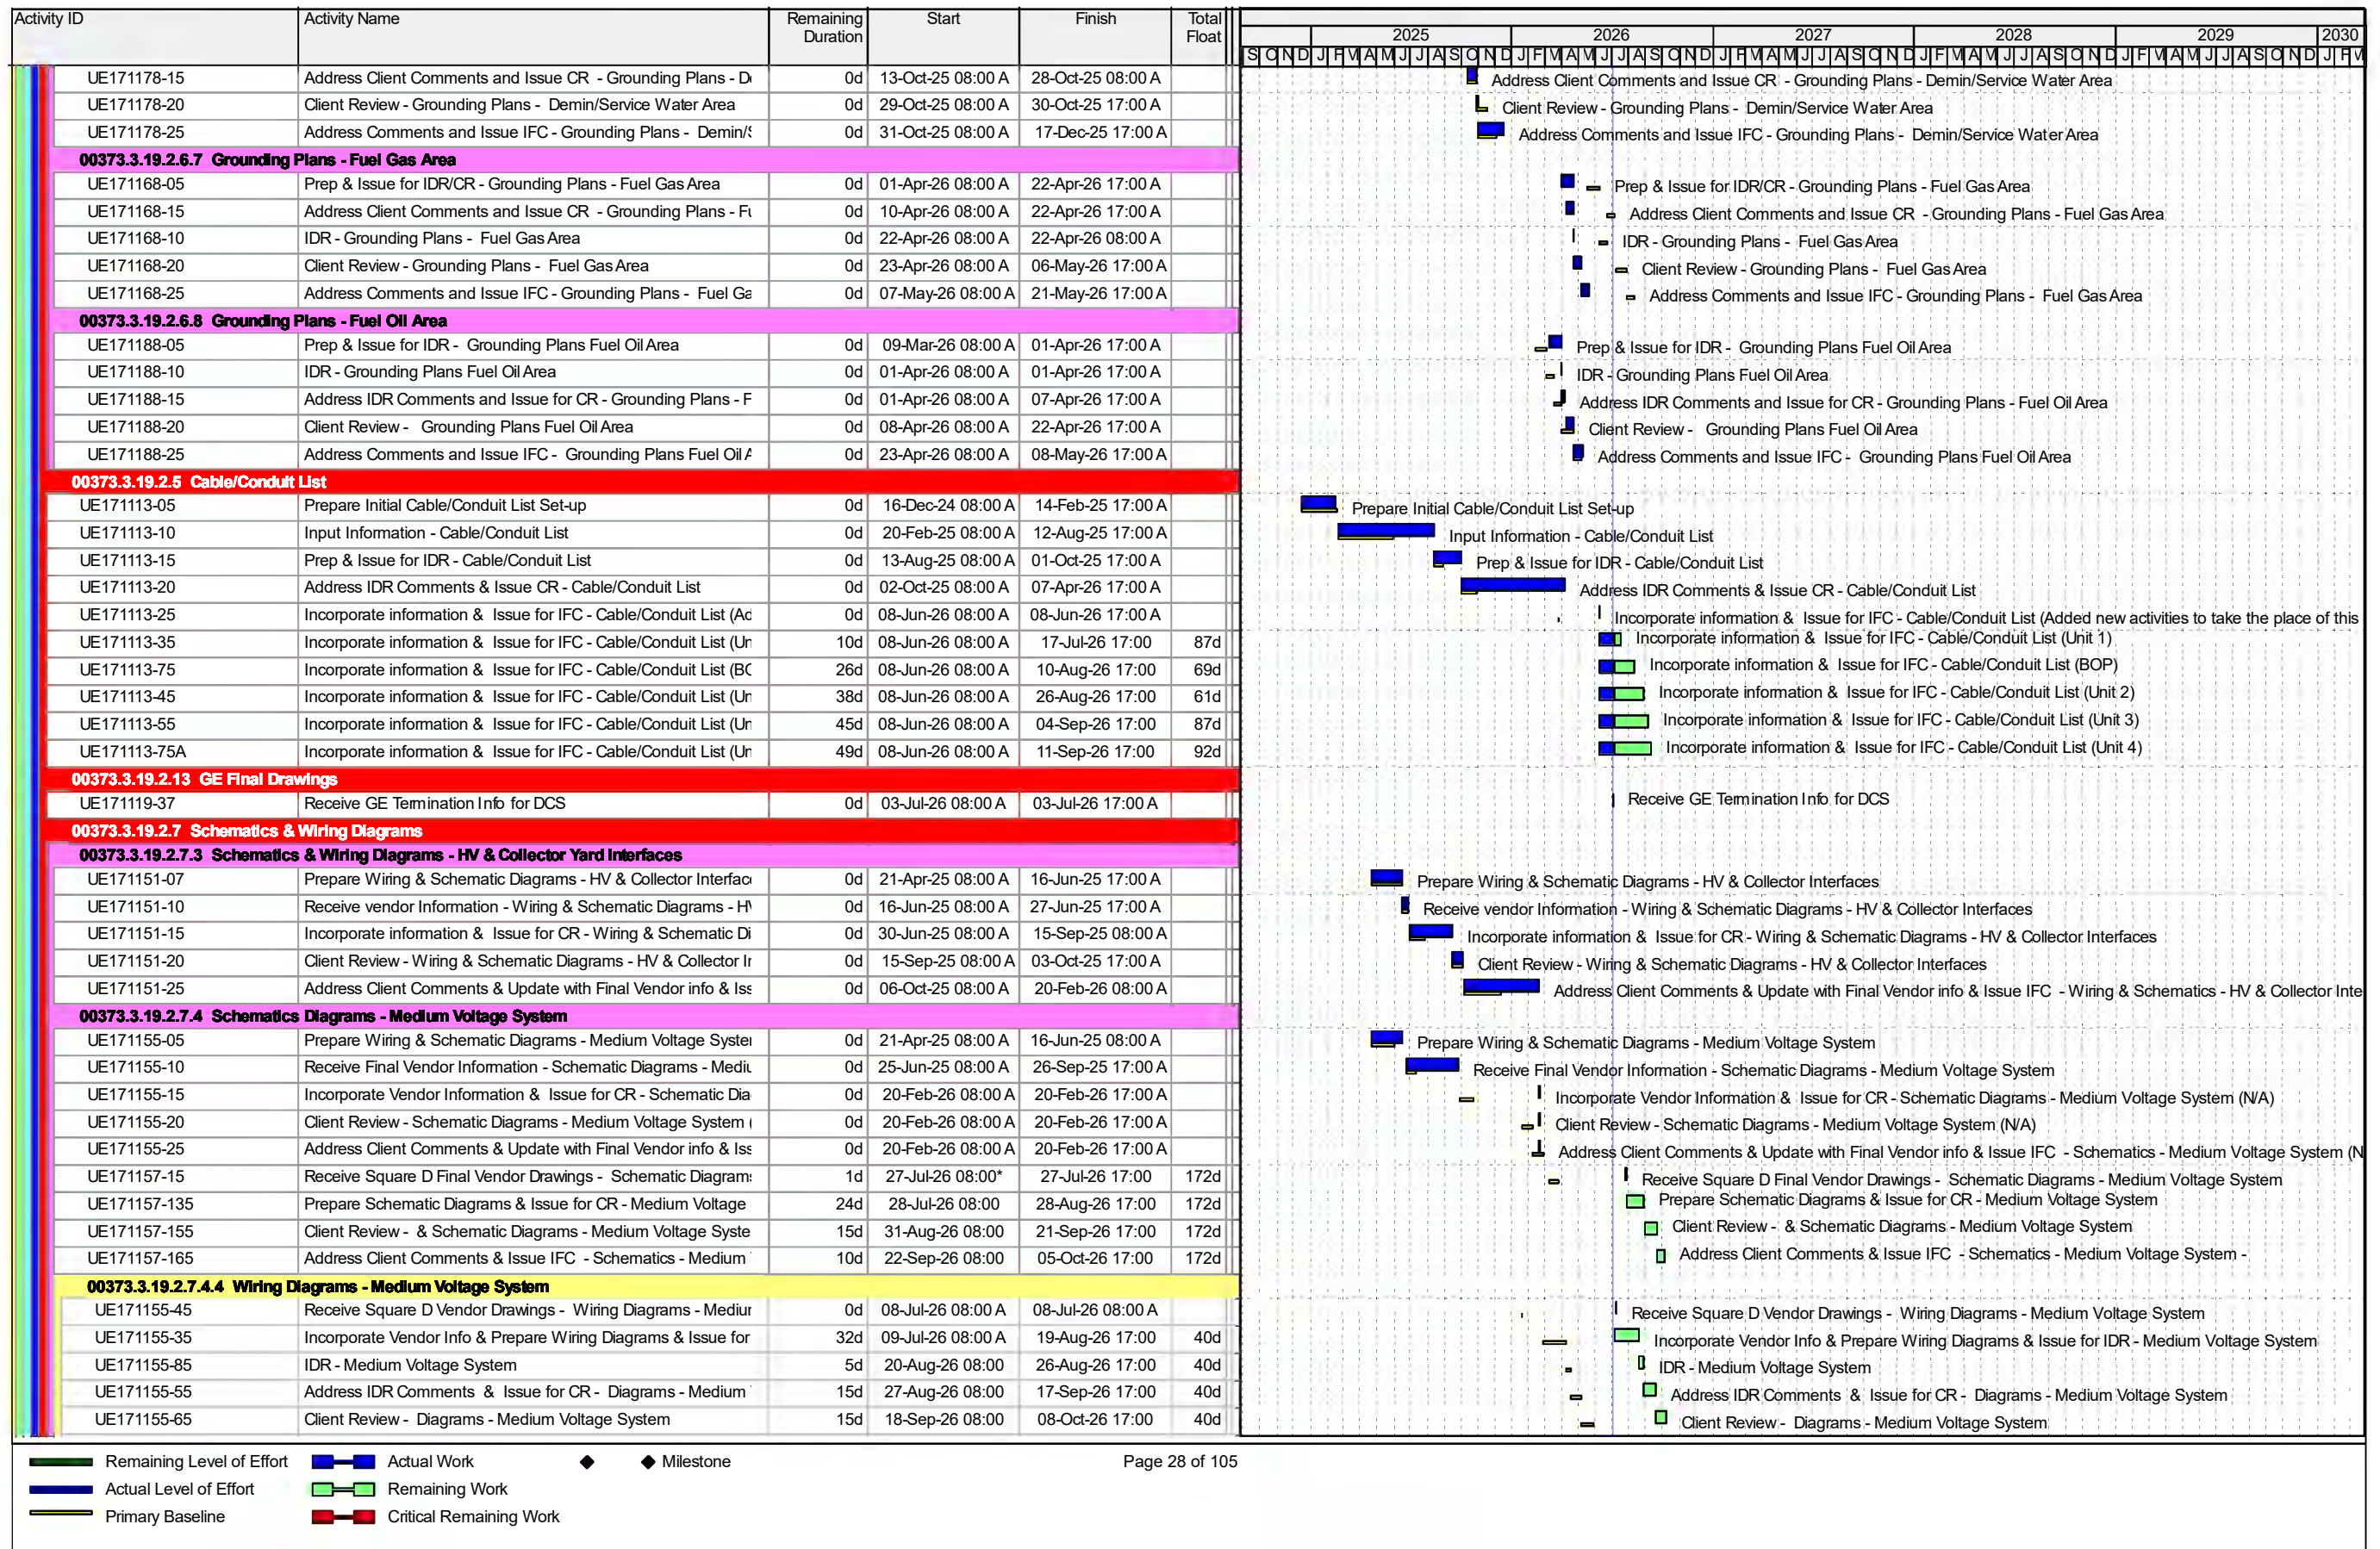


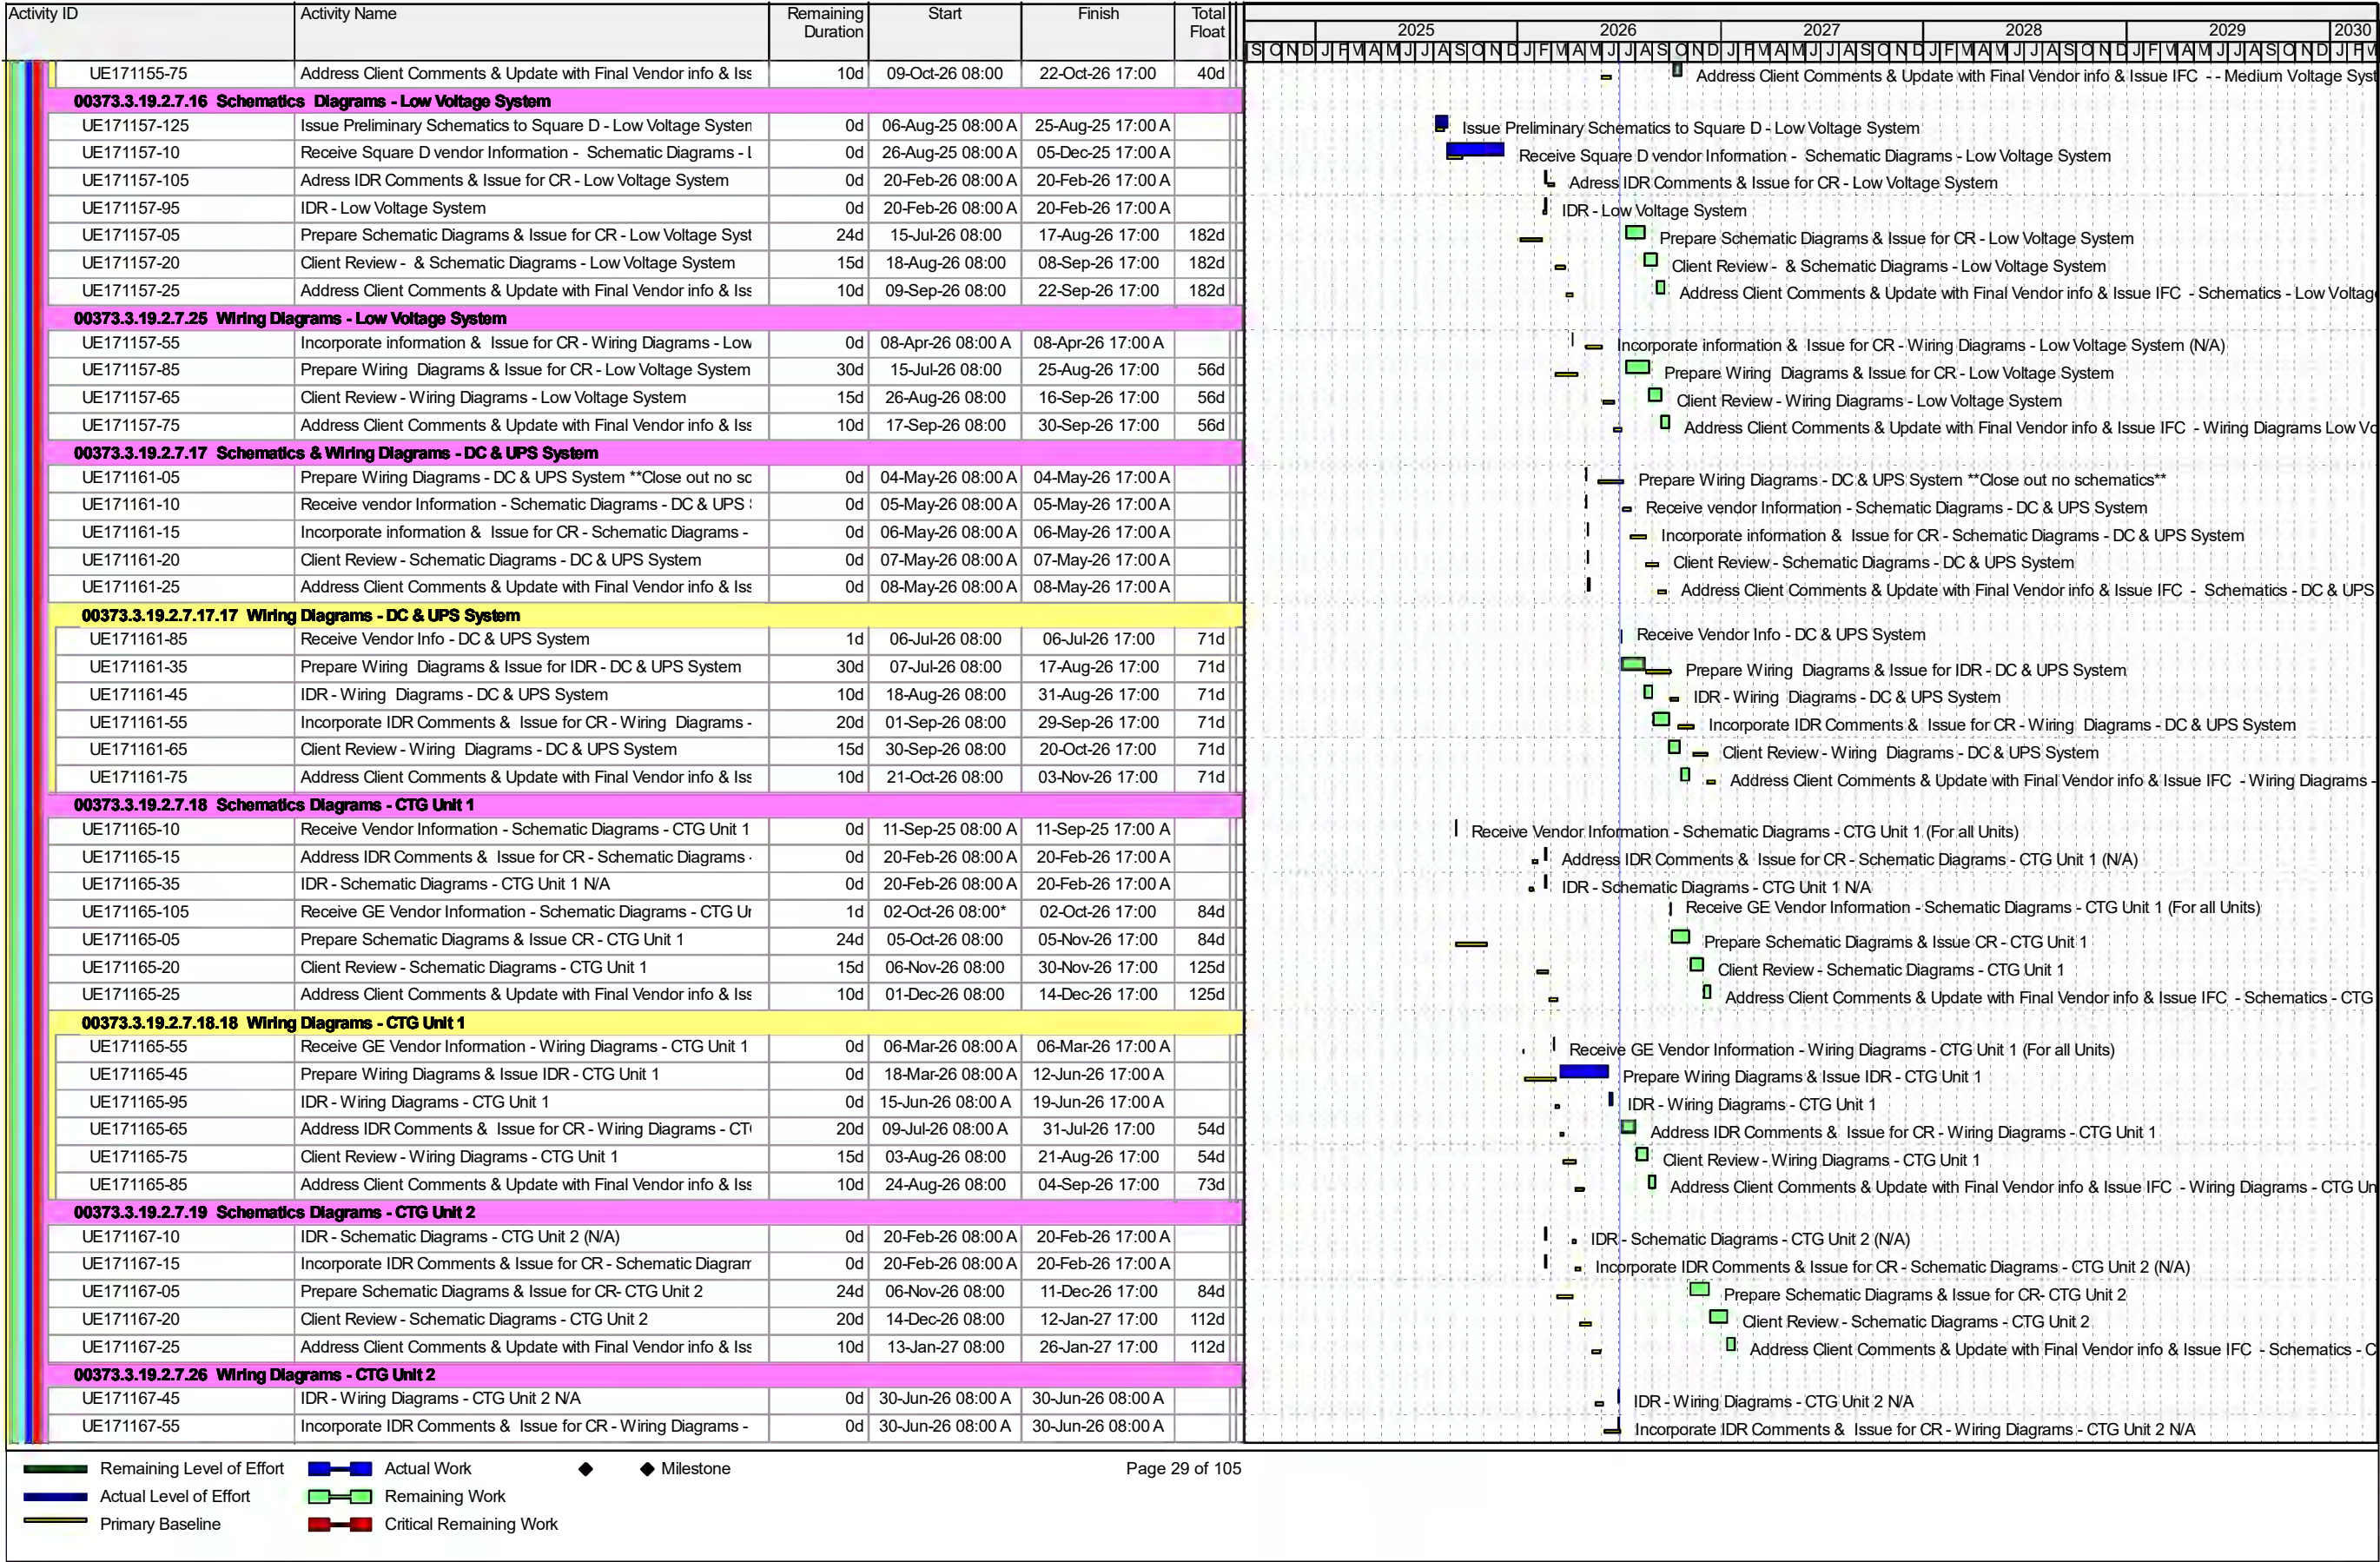 Primary Baseline Milestone

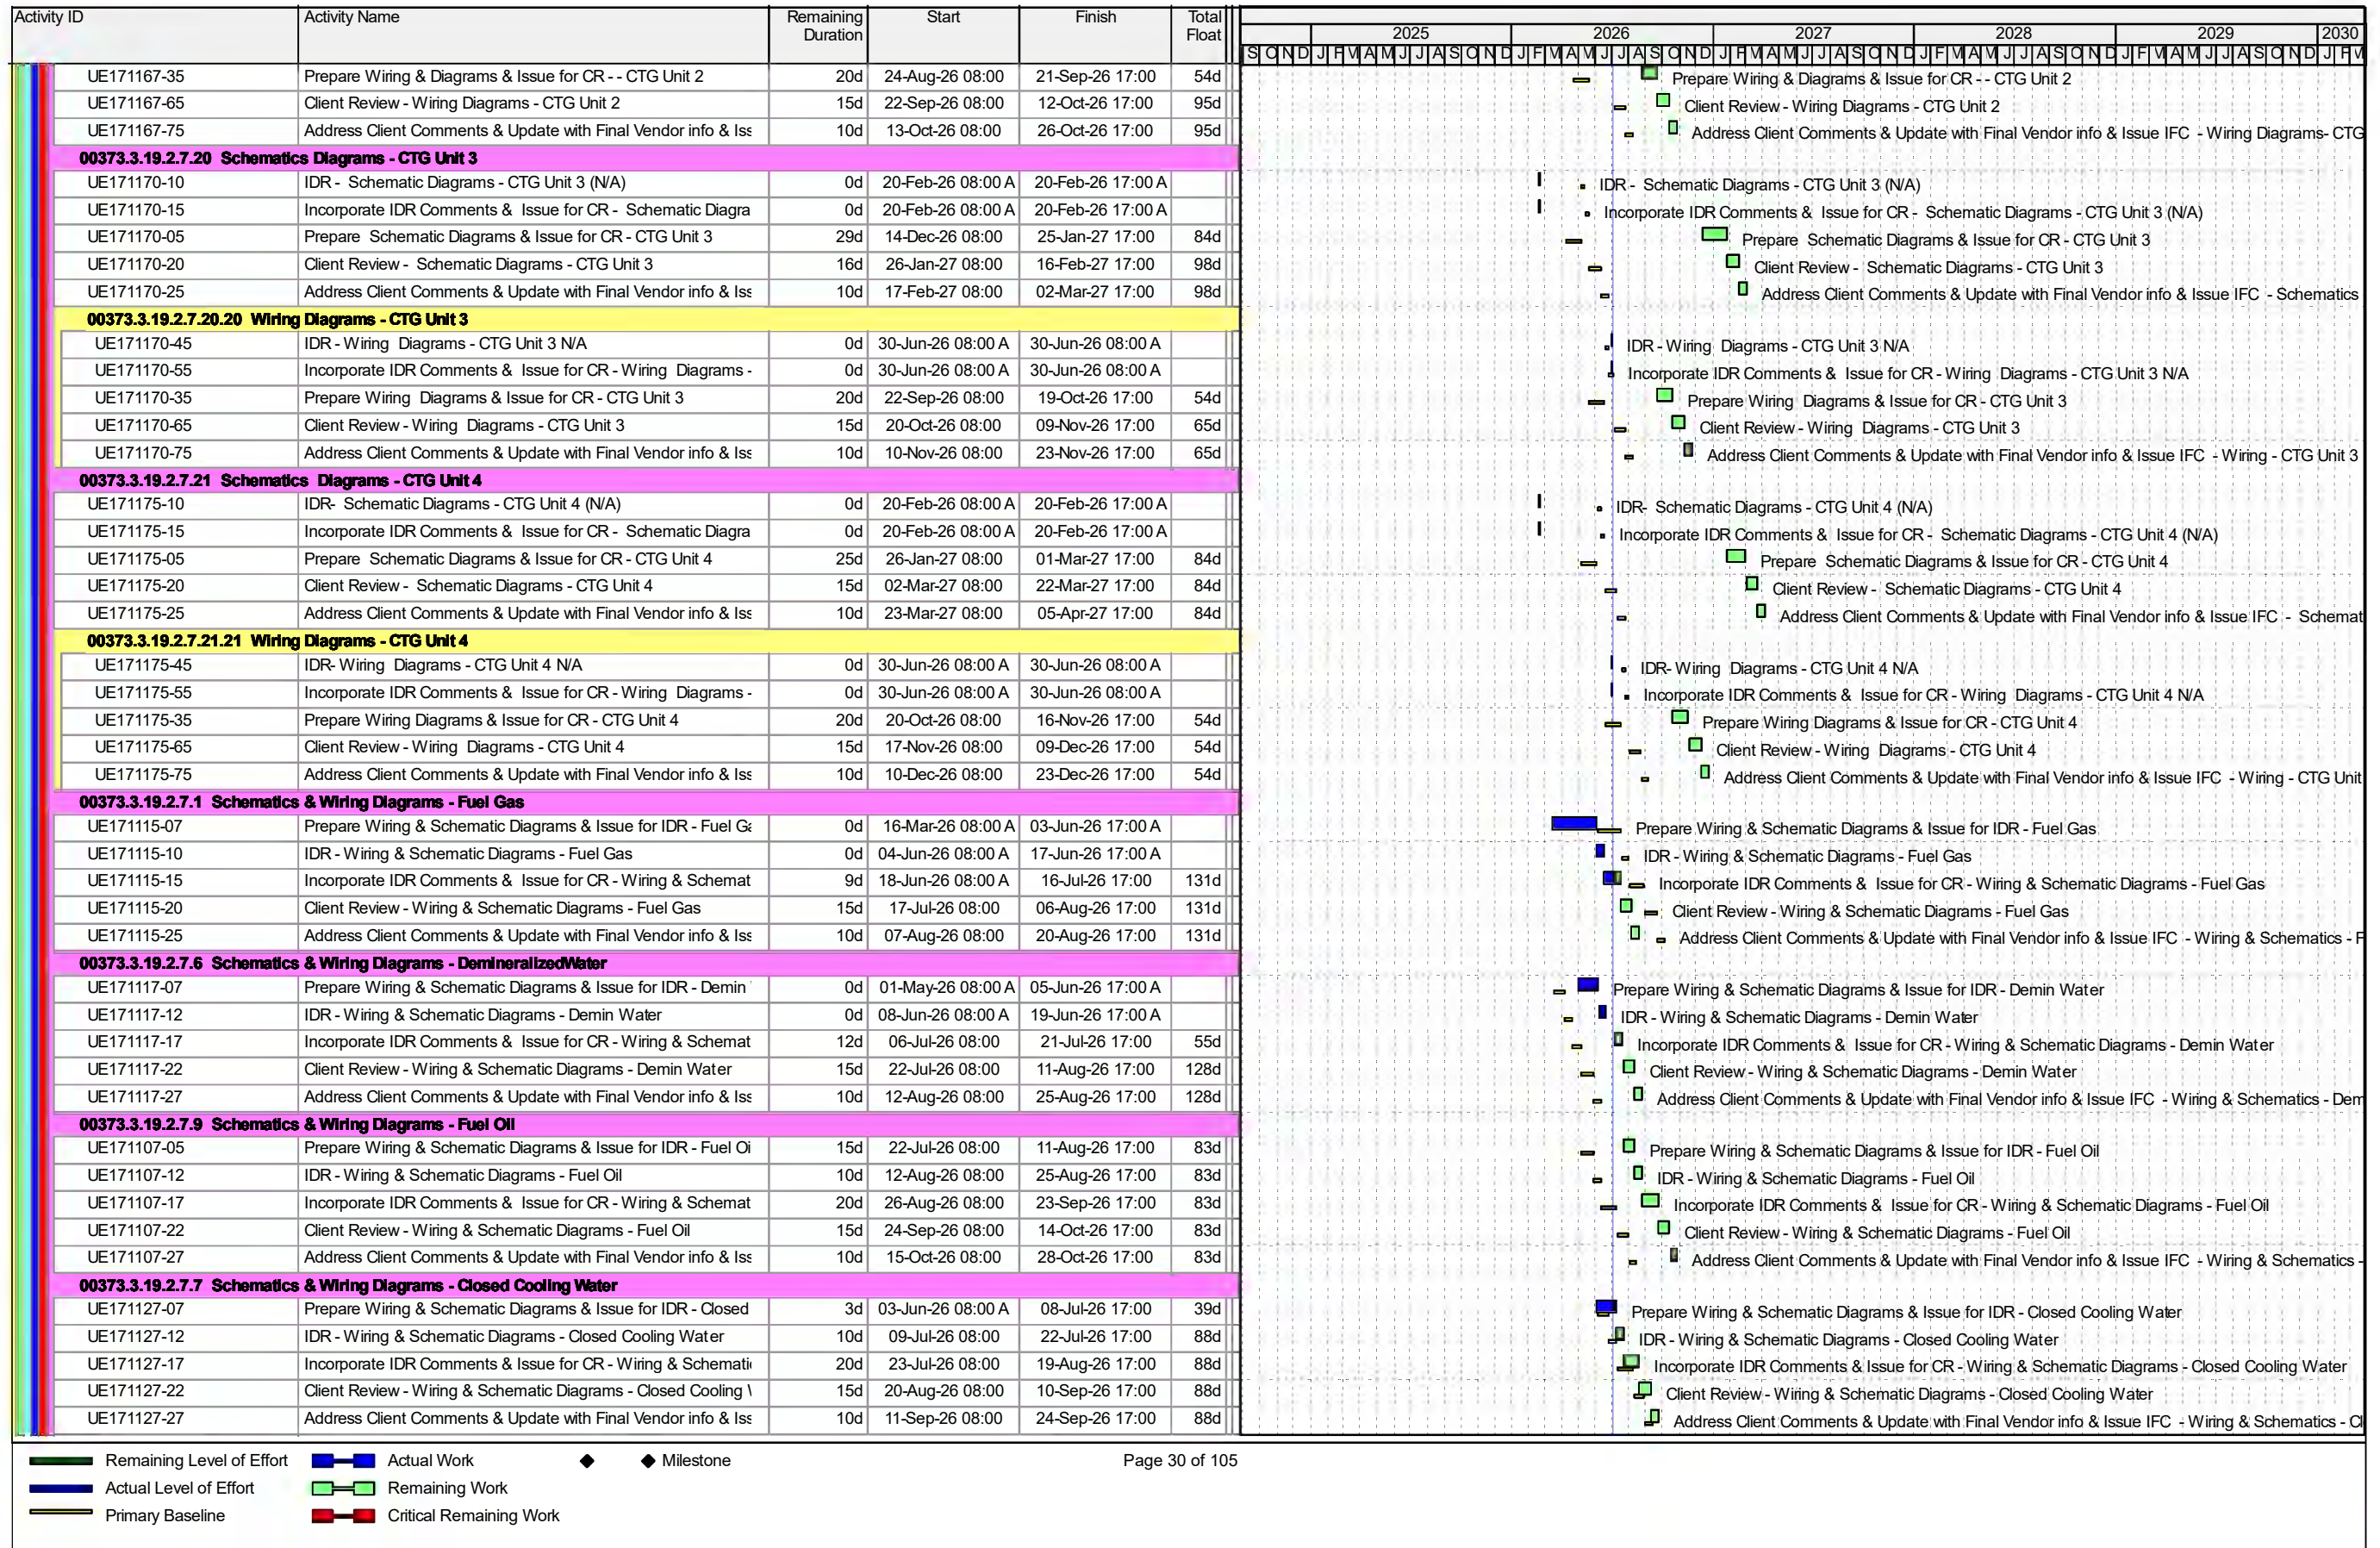


Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2025							2026							2027							2028							2029							2030						
						S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
						Legend: - Remaining Level of Effort - Actual Work - Milestone - Actual Level of Effort - Remaining Work - Primary Baseline - Critical Remaining Work																																									


Page 31 of 105

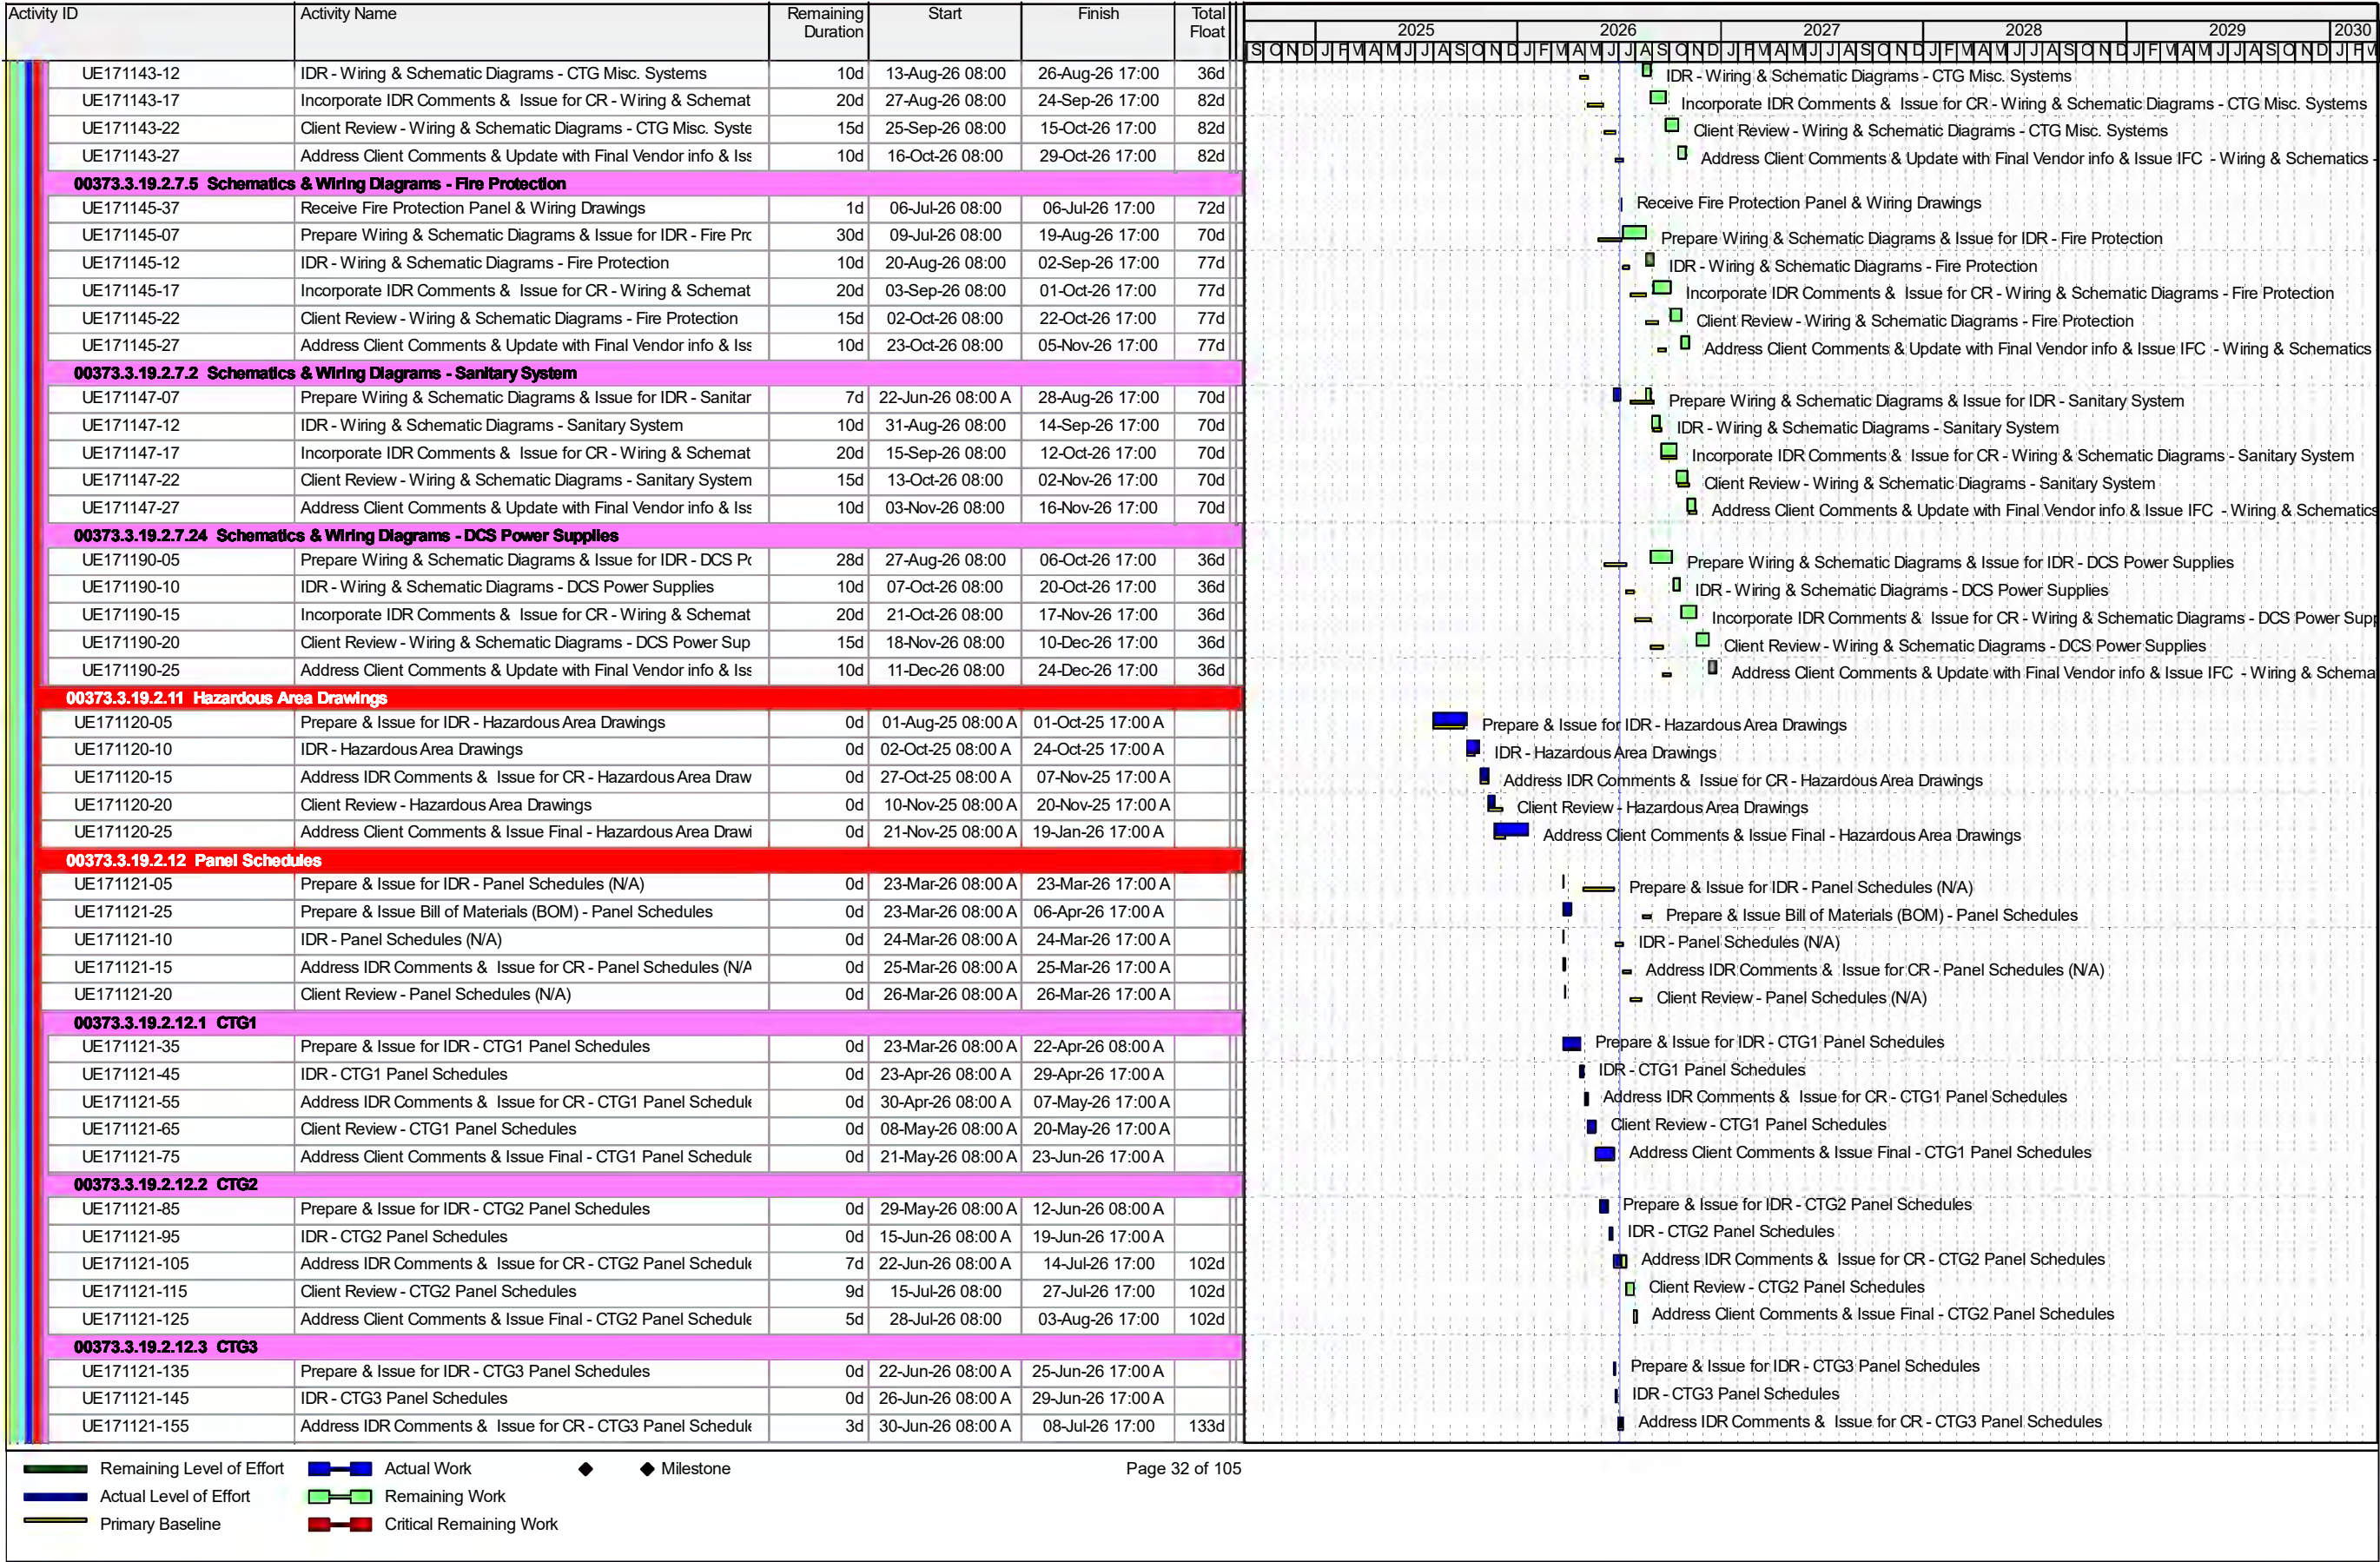



[illegible]

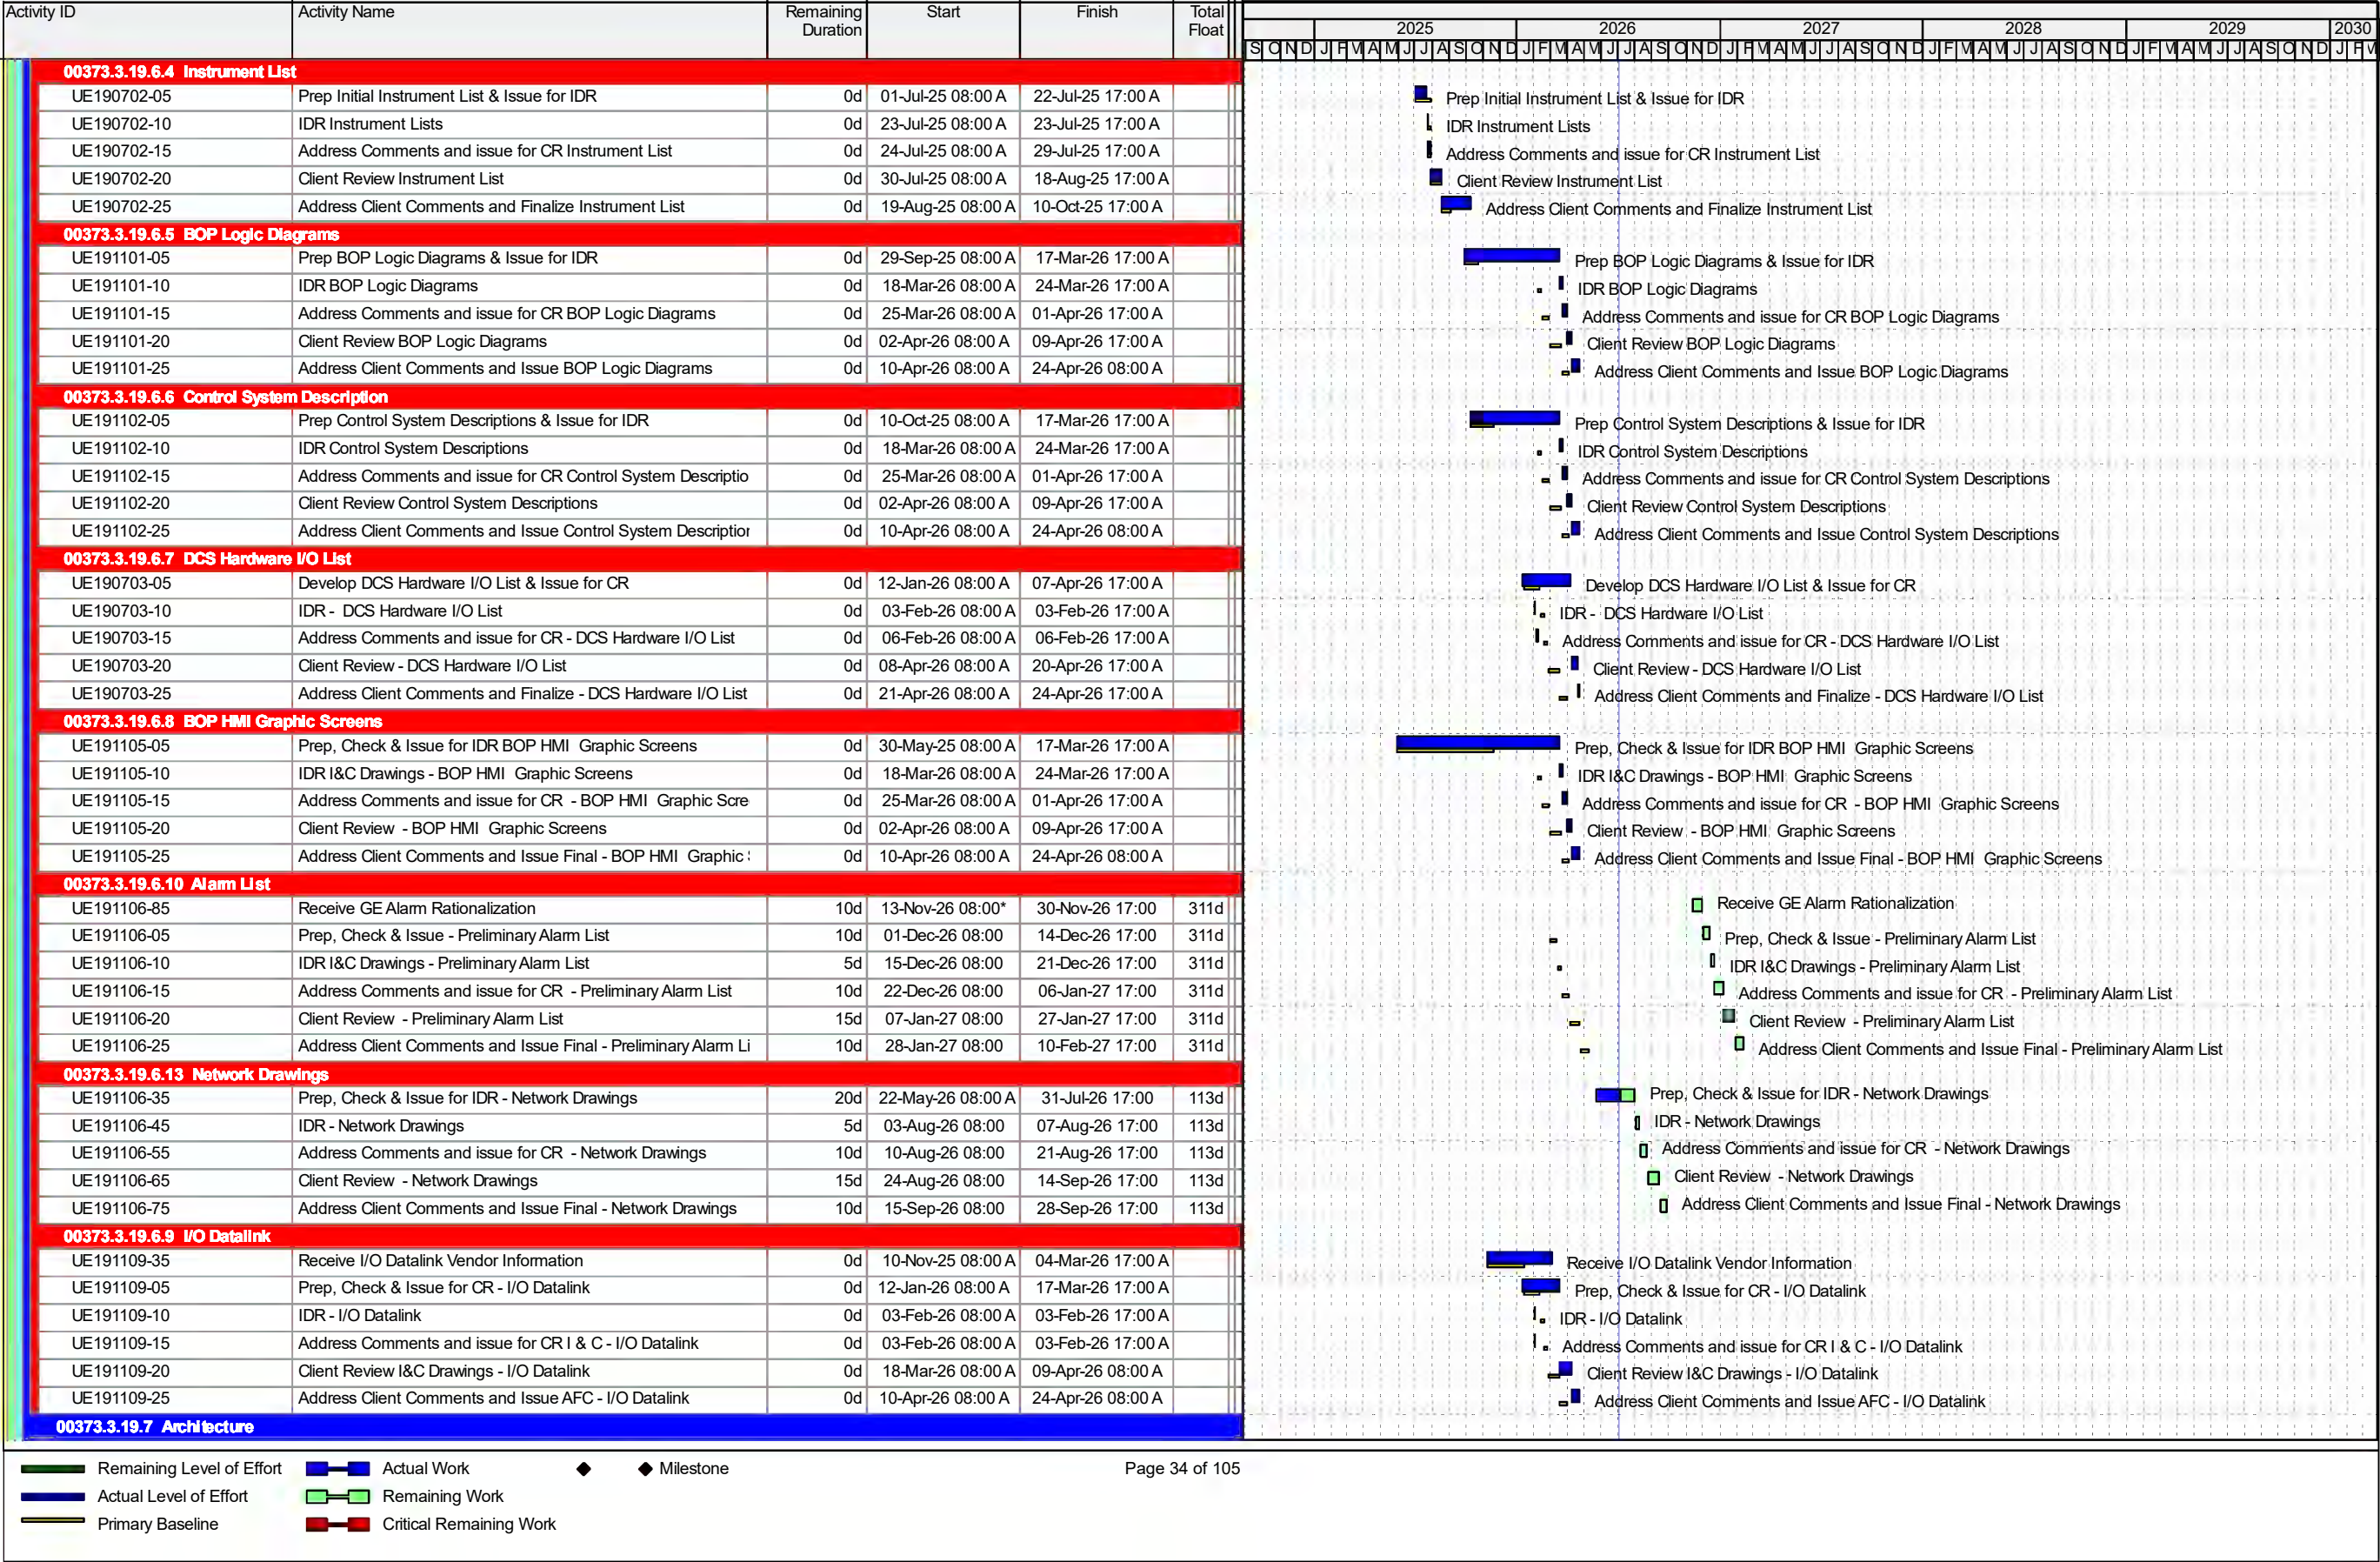


Page 34 of 105

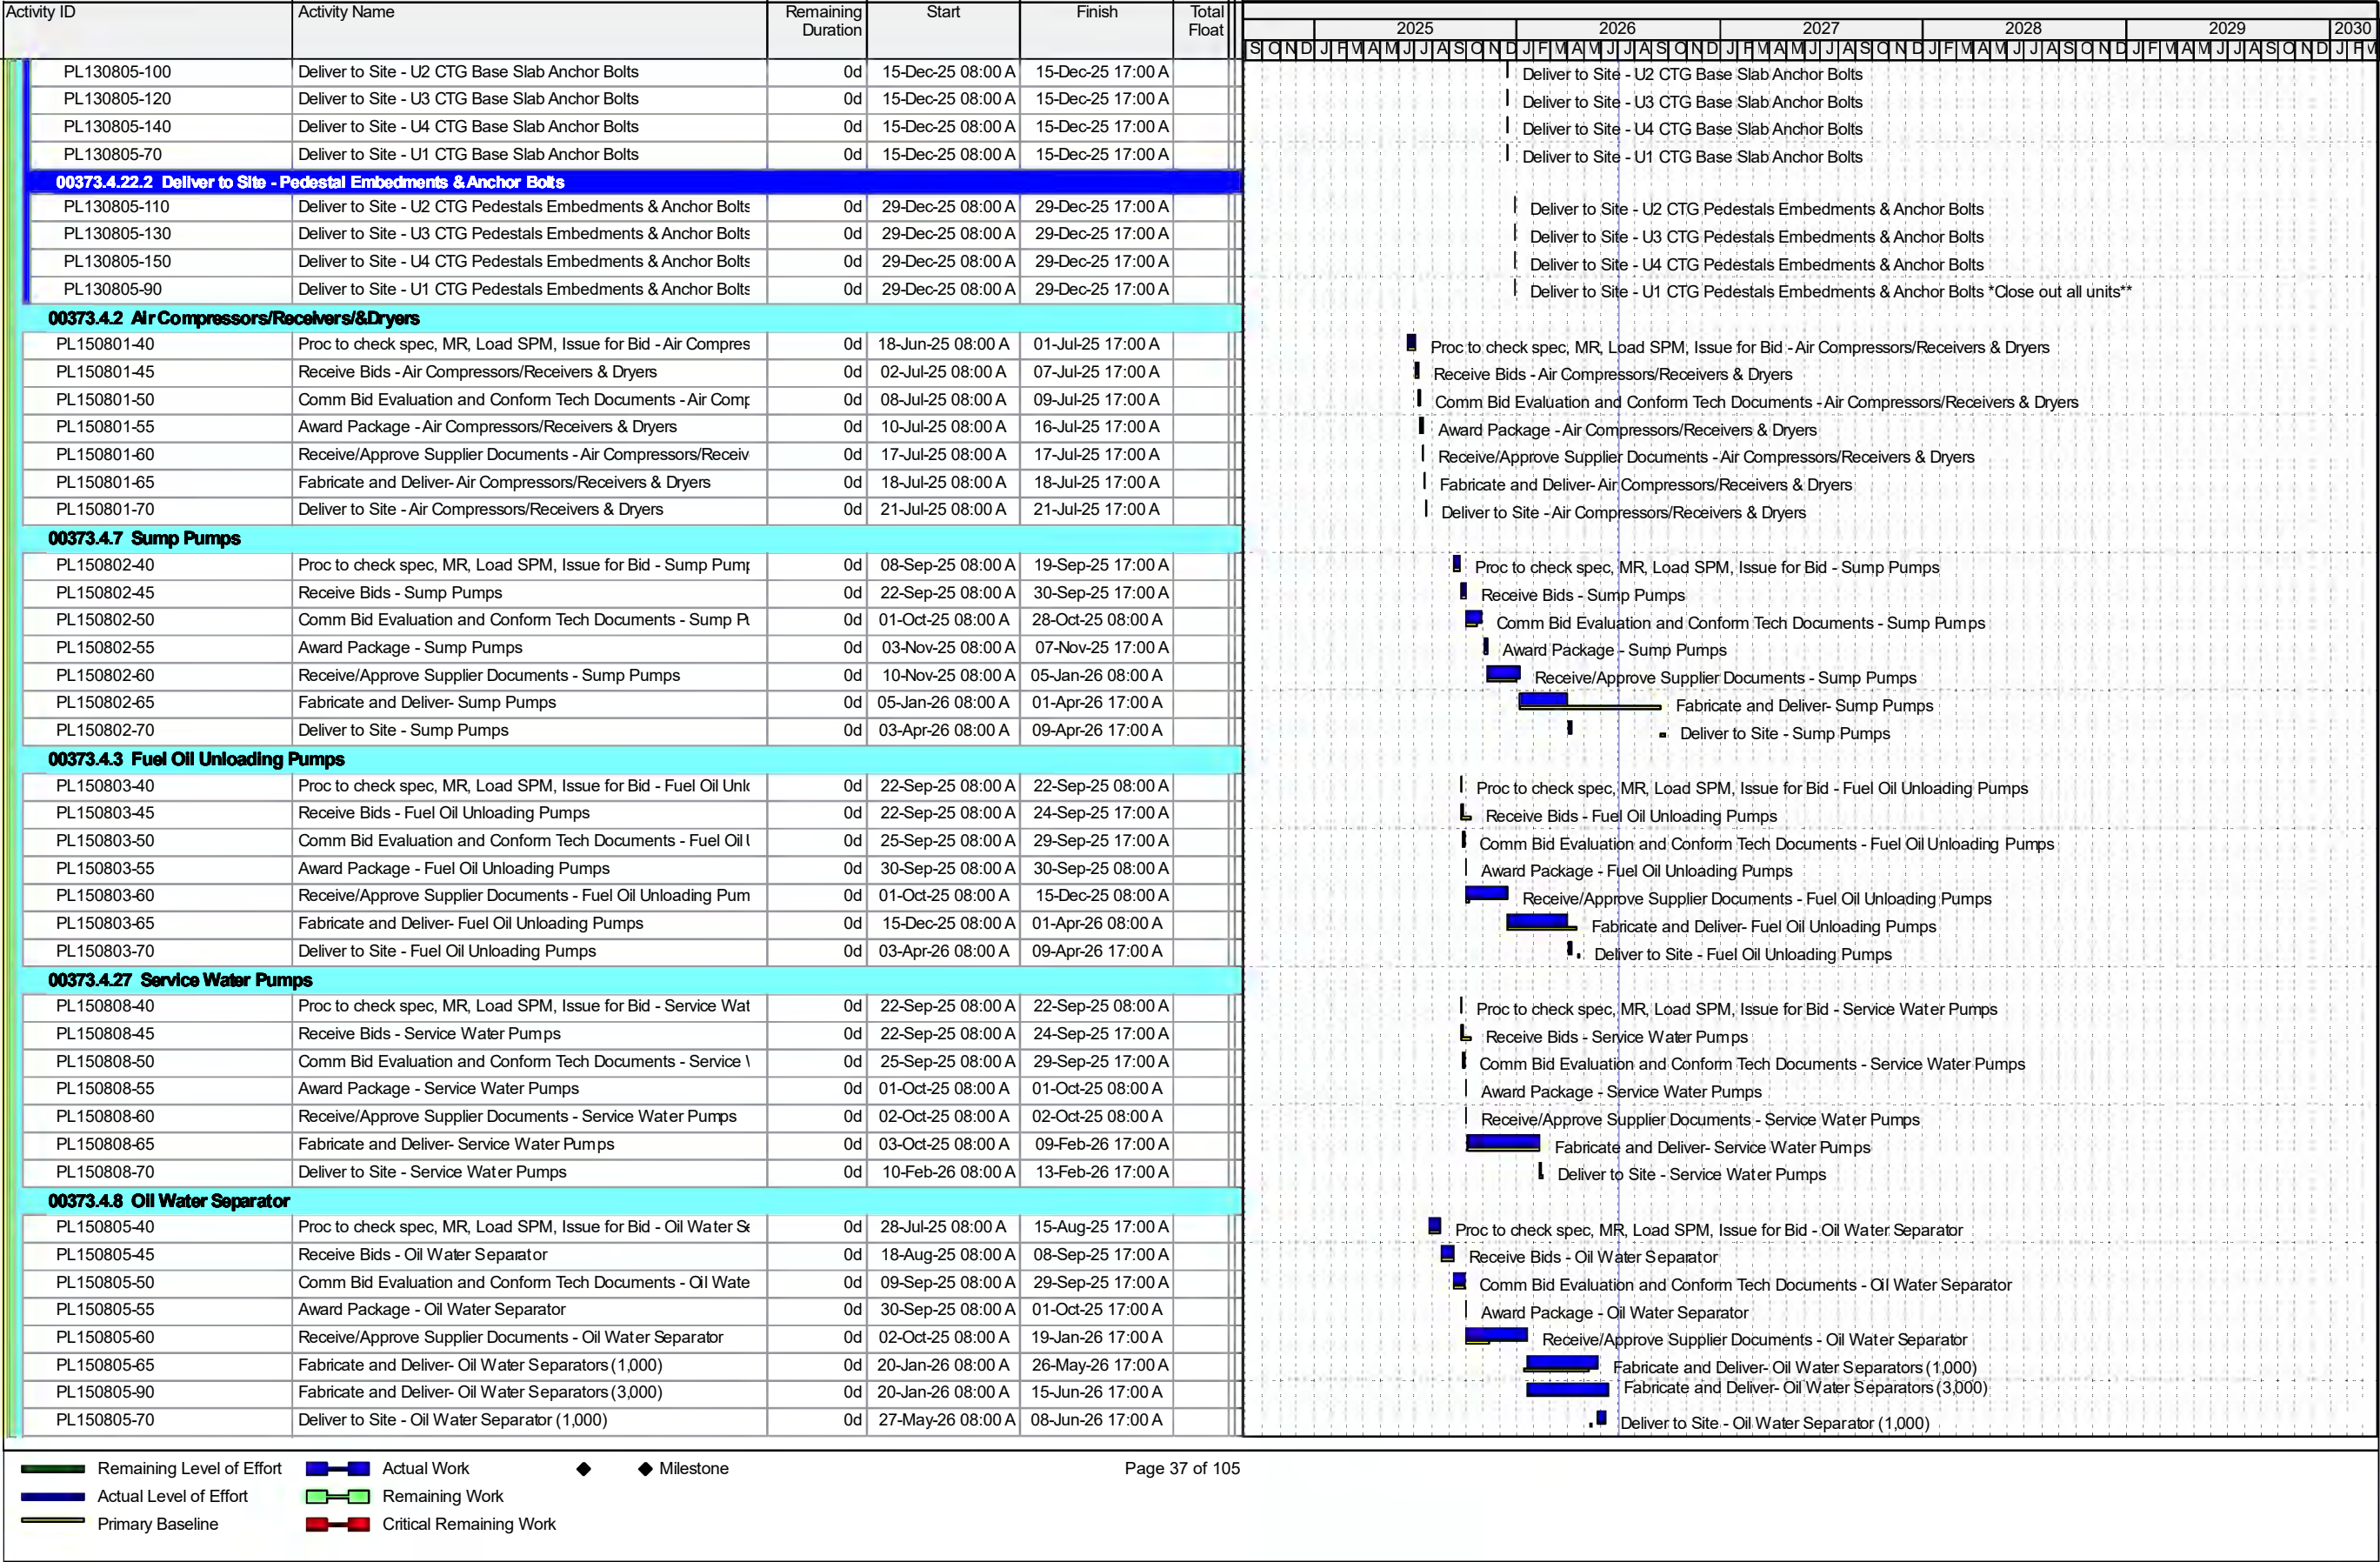


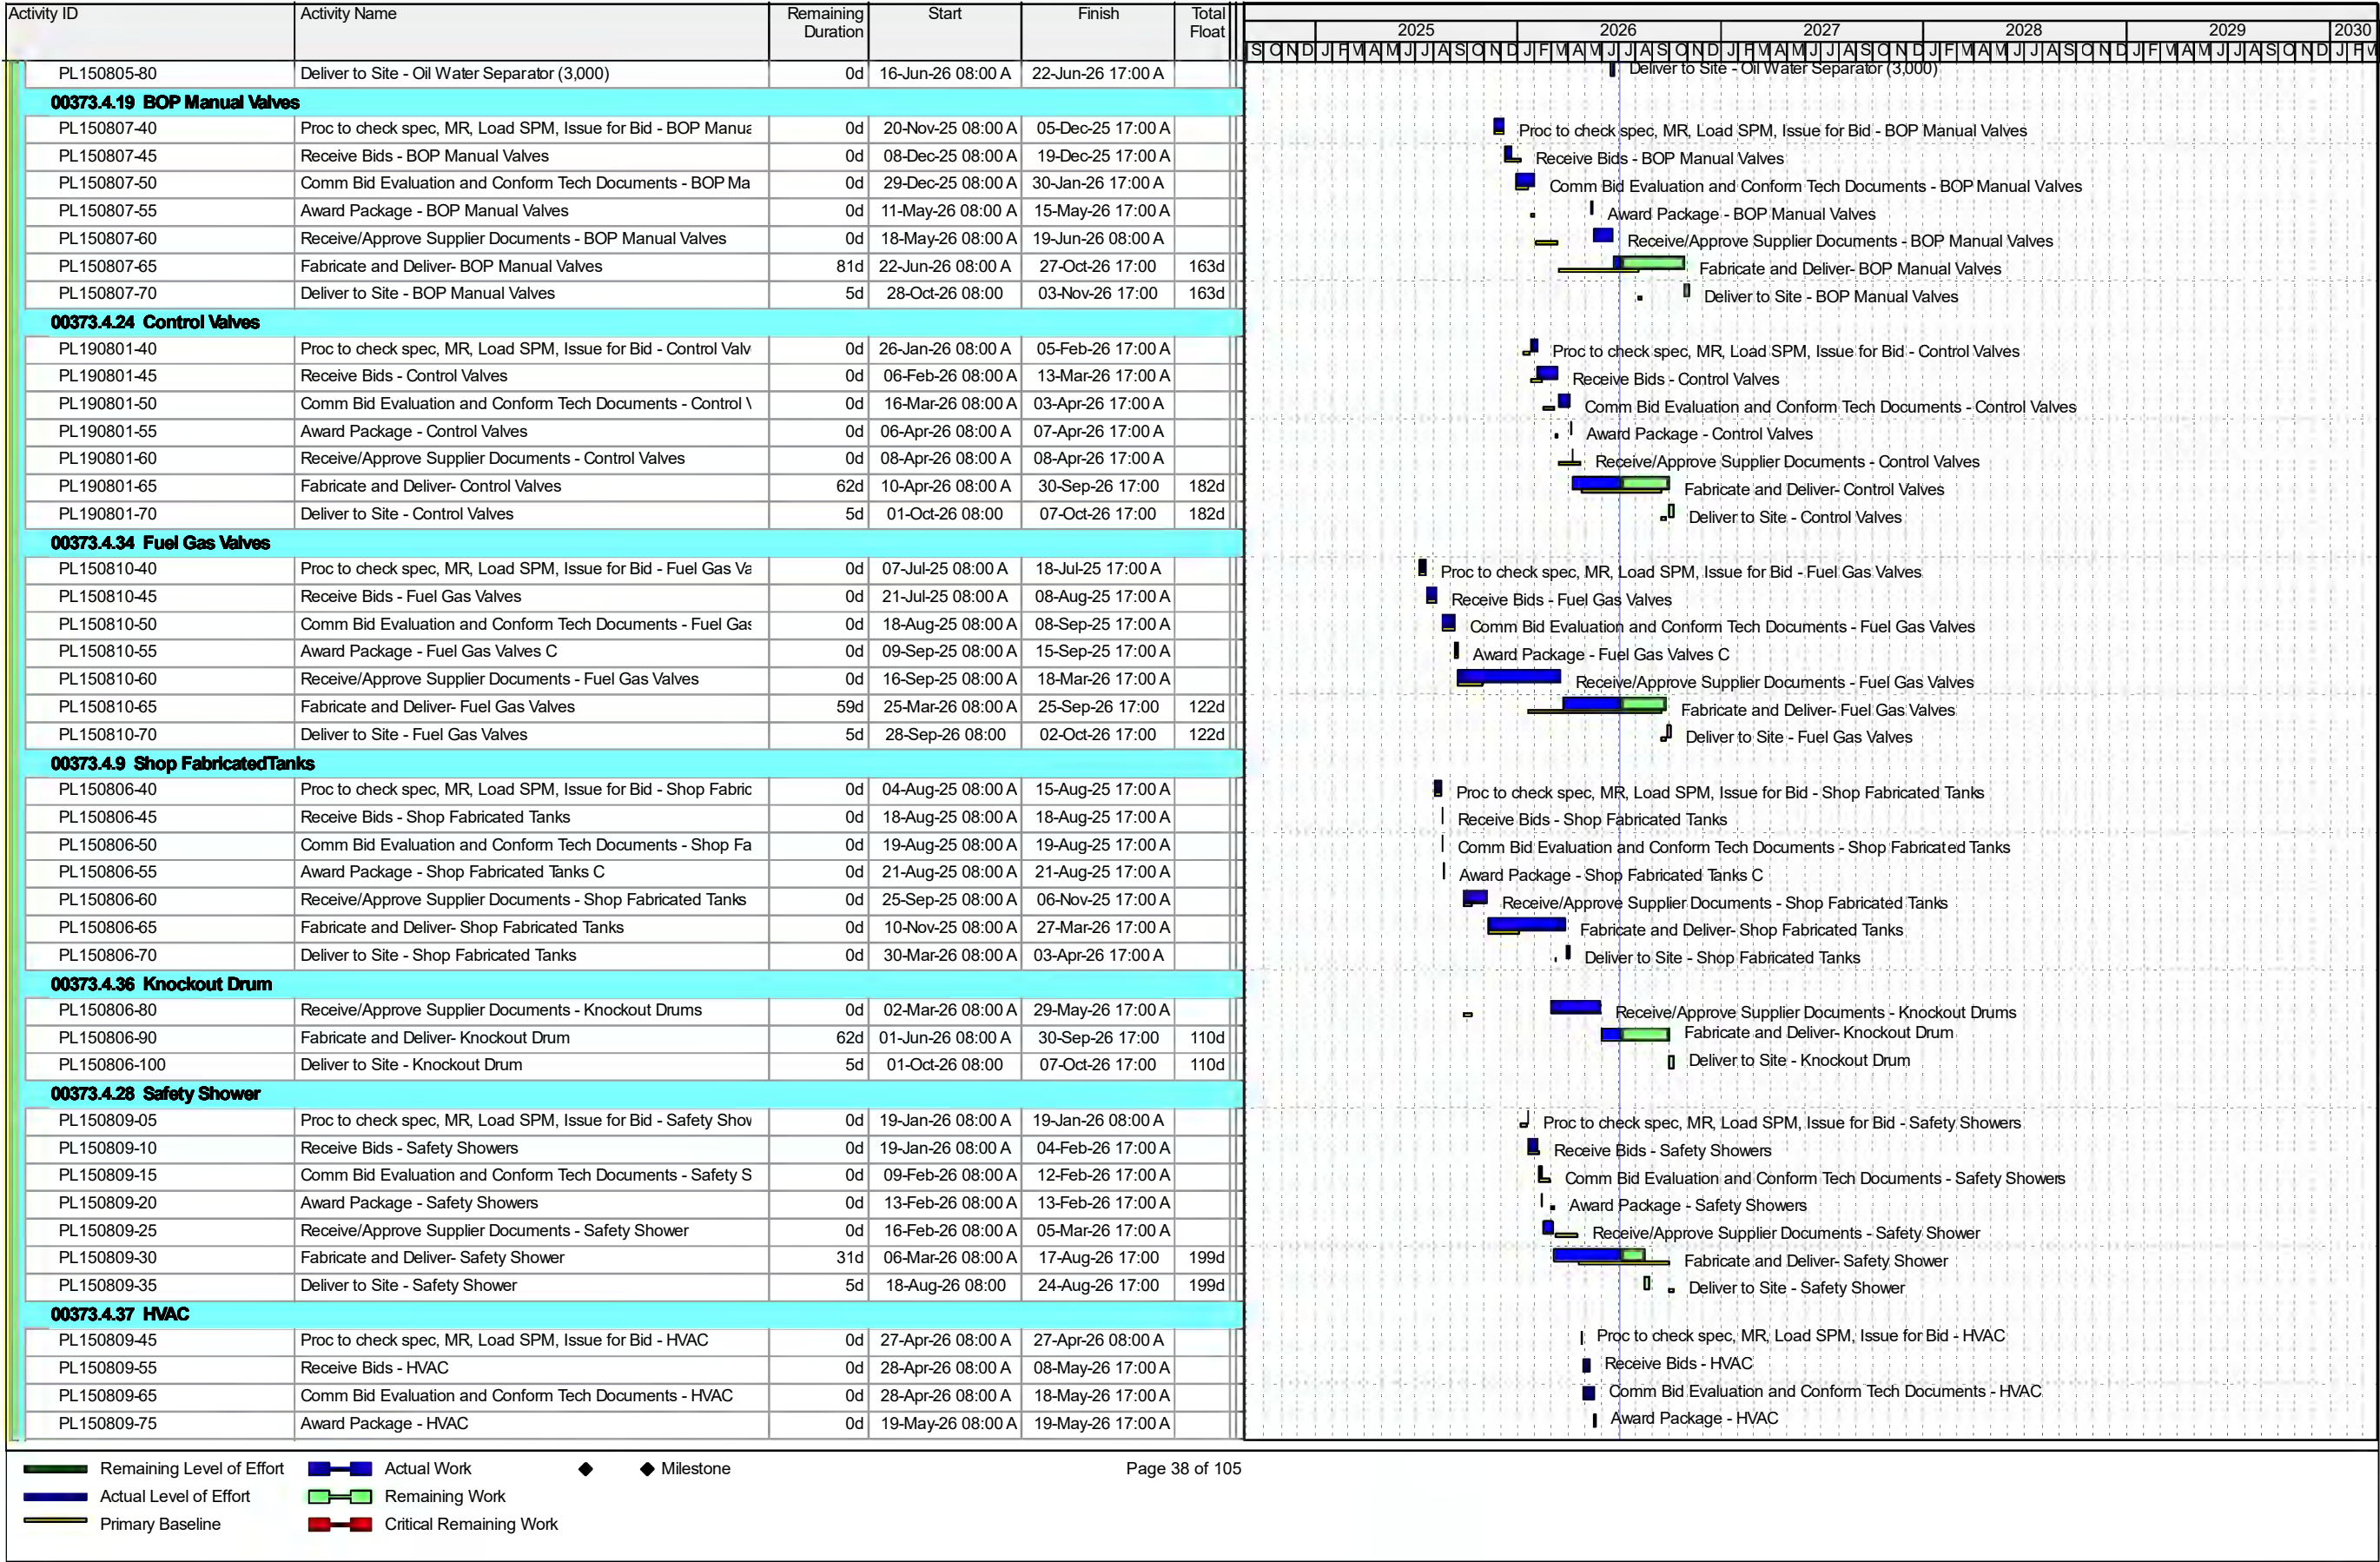


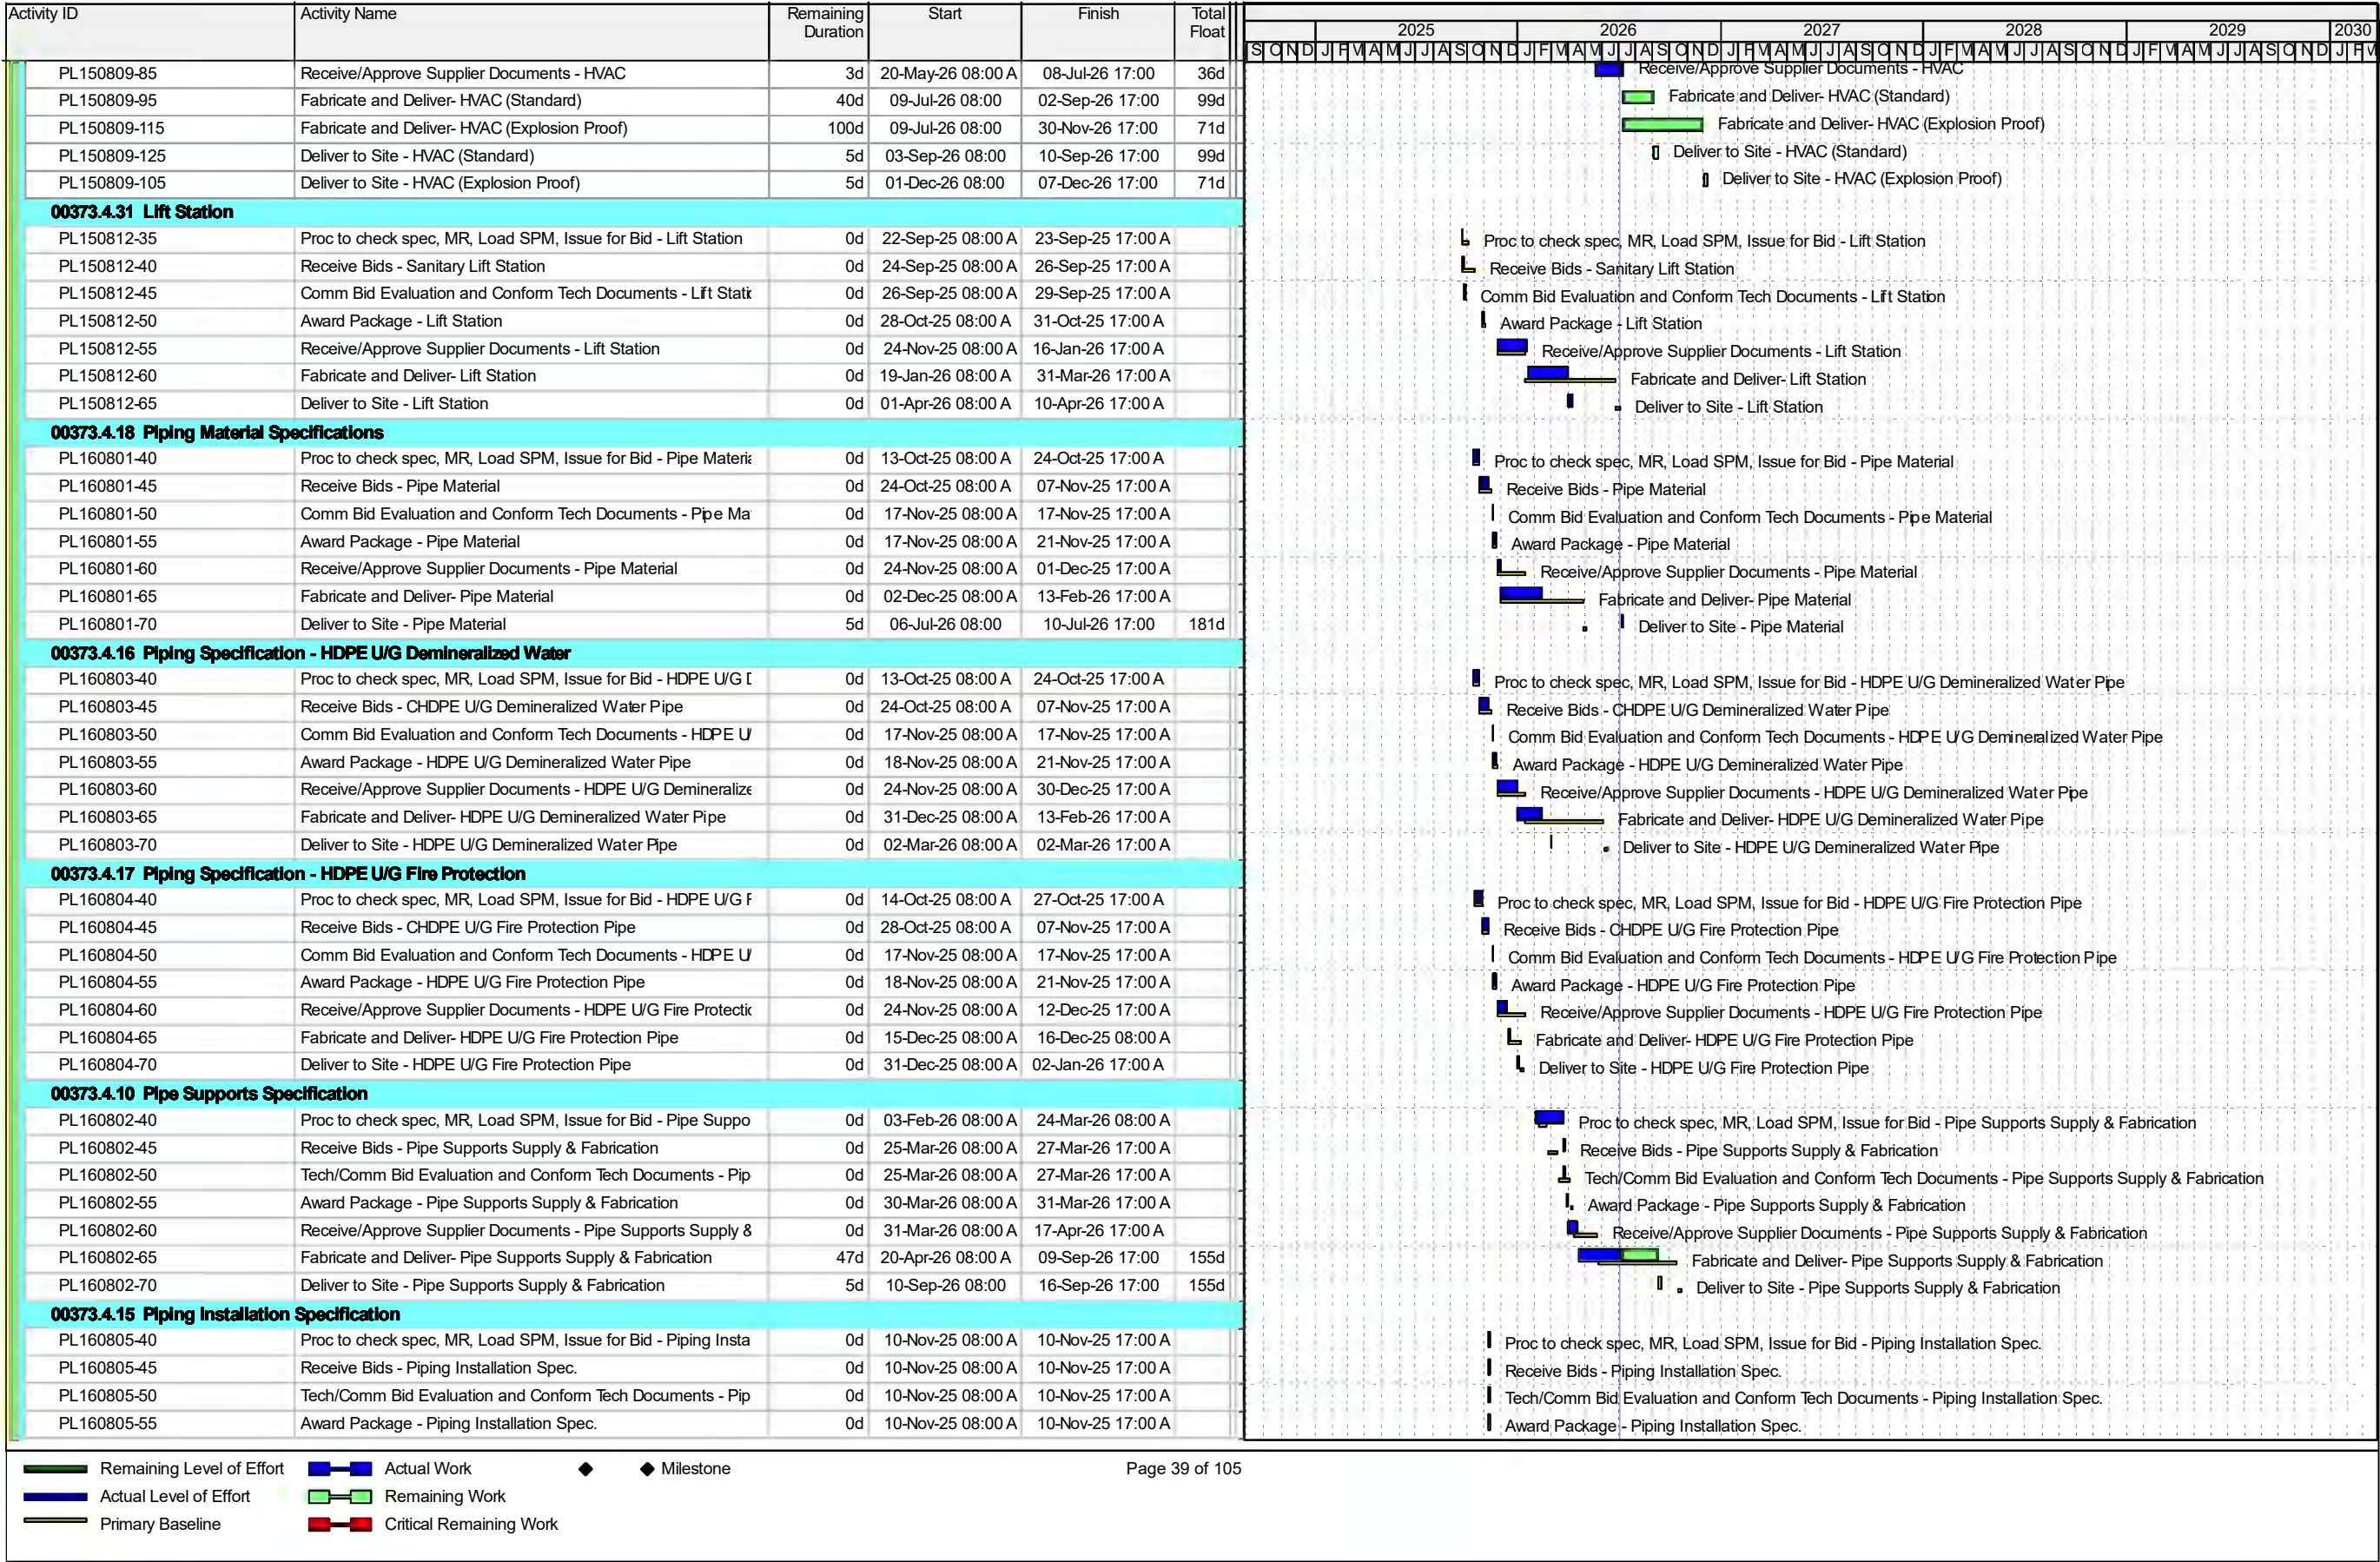

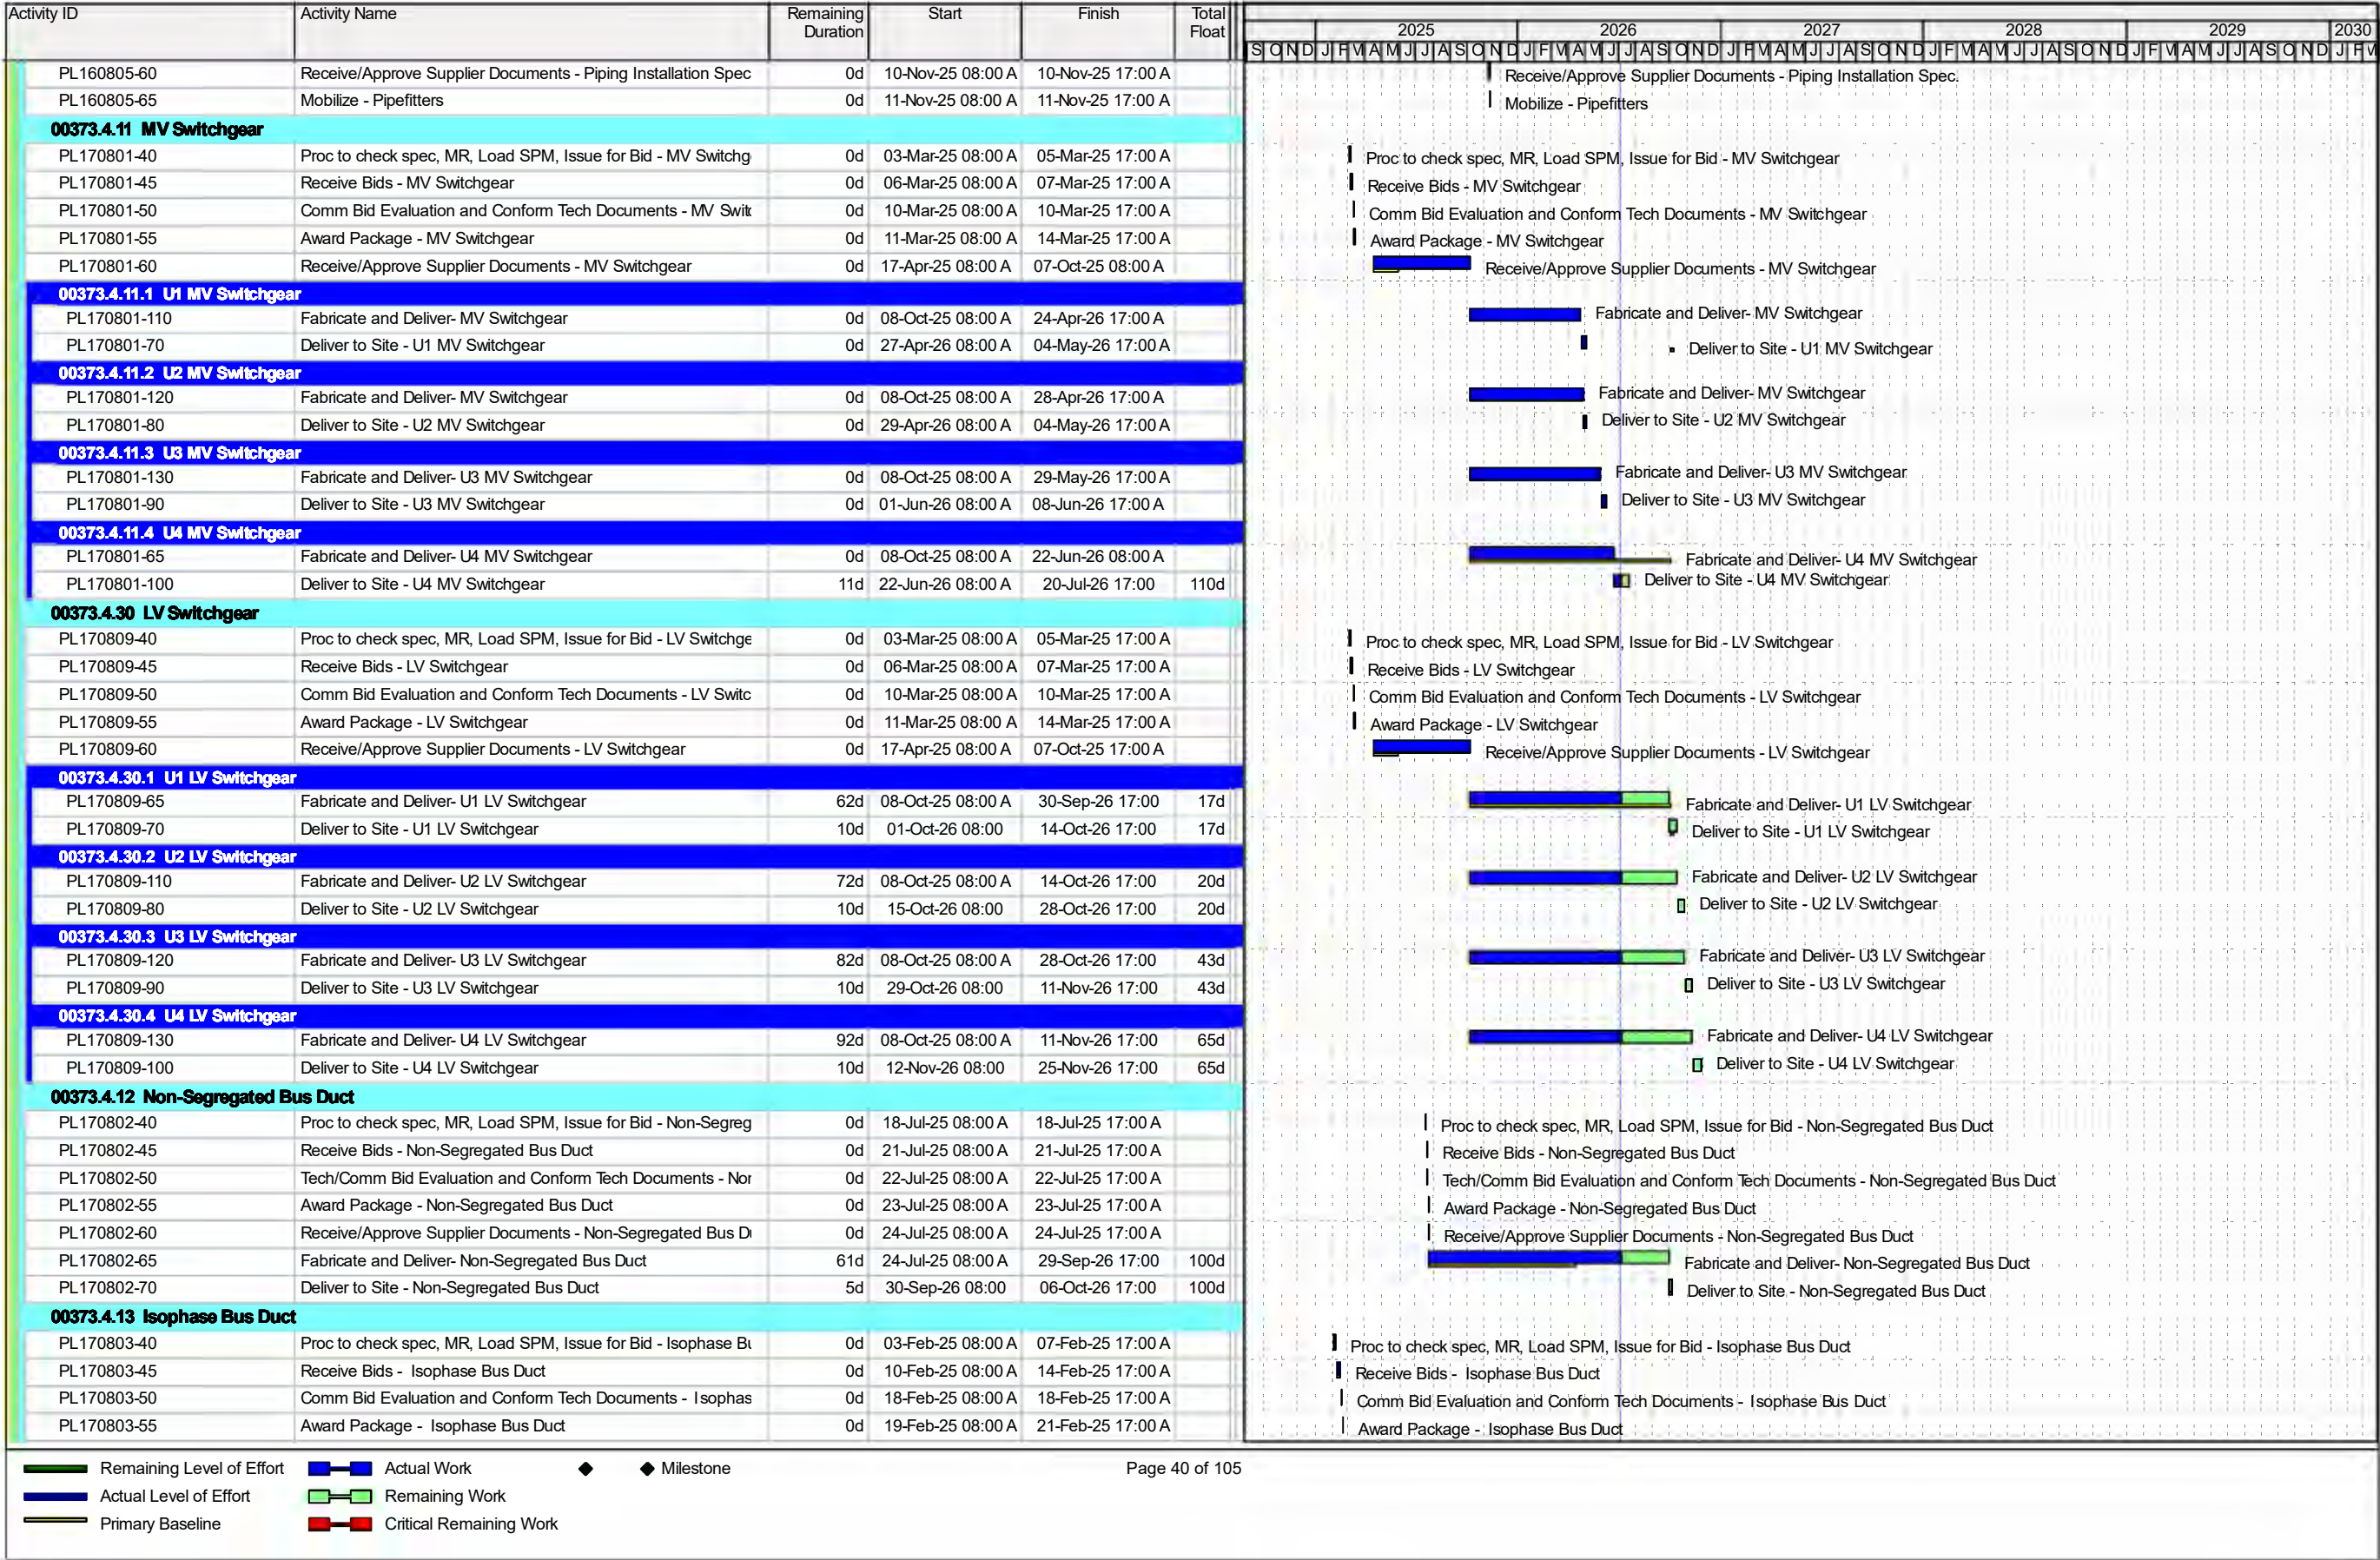



Page 40 of 105

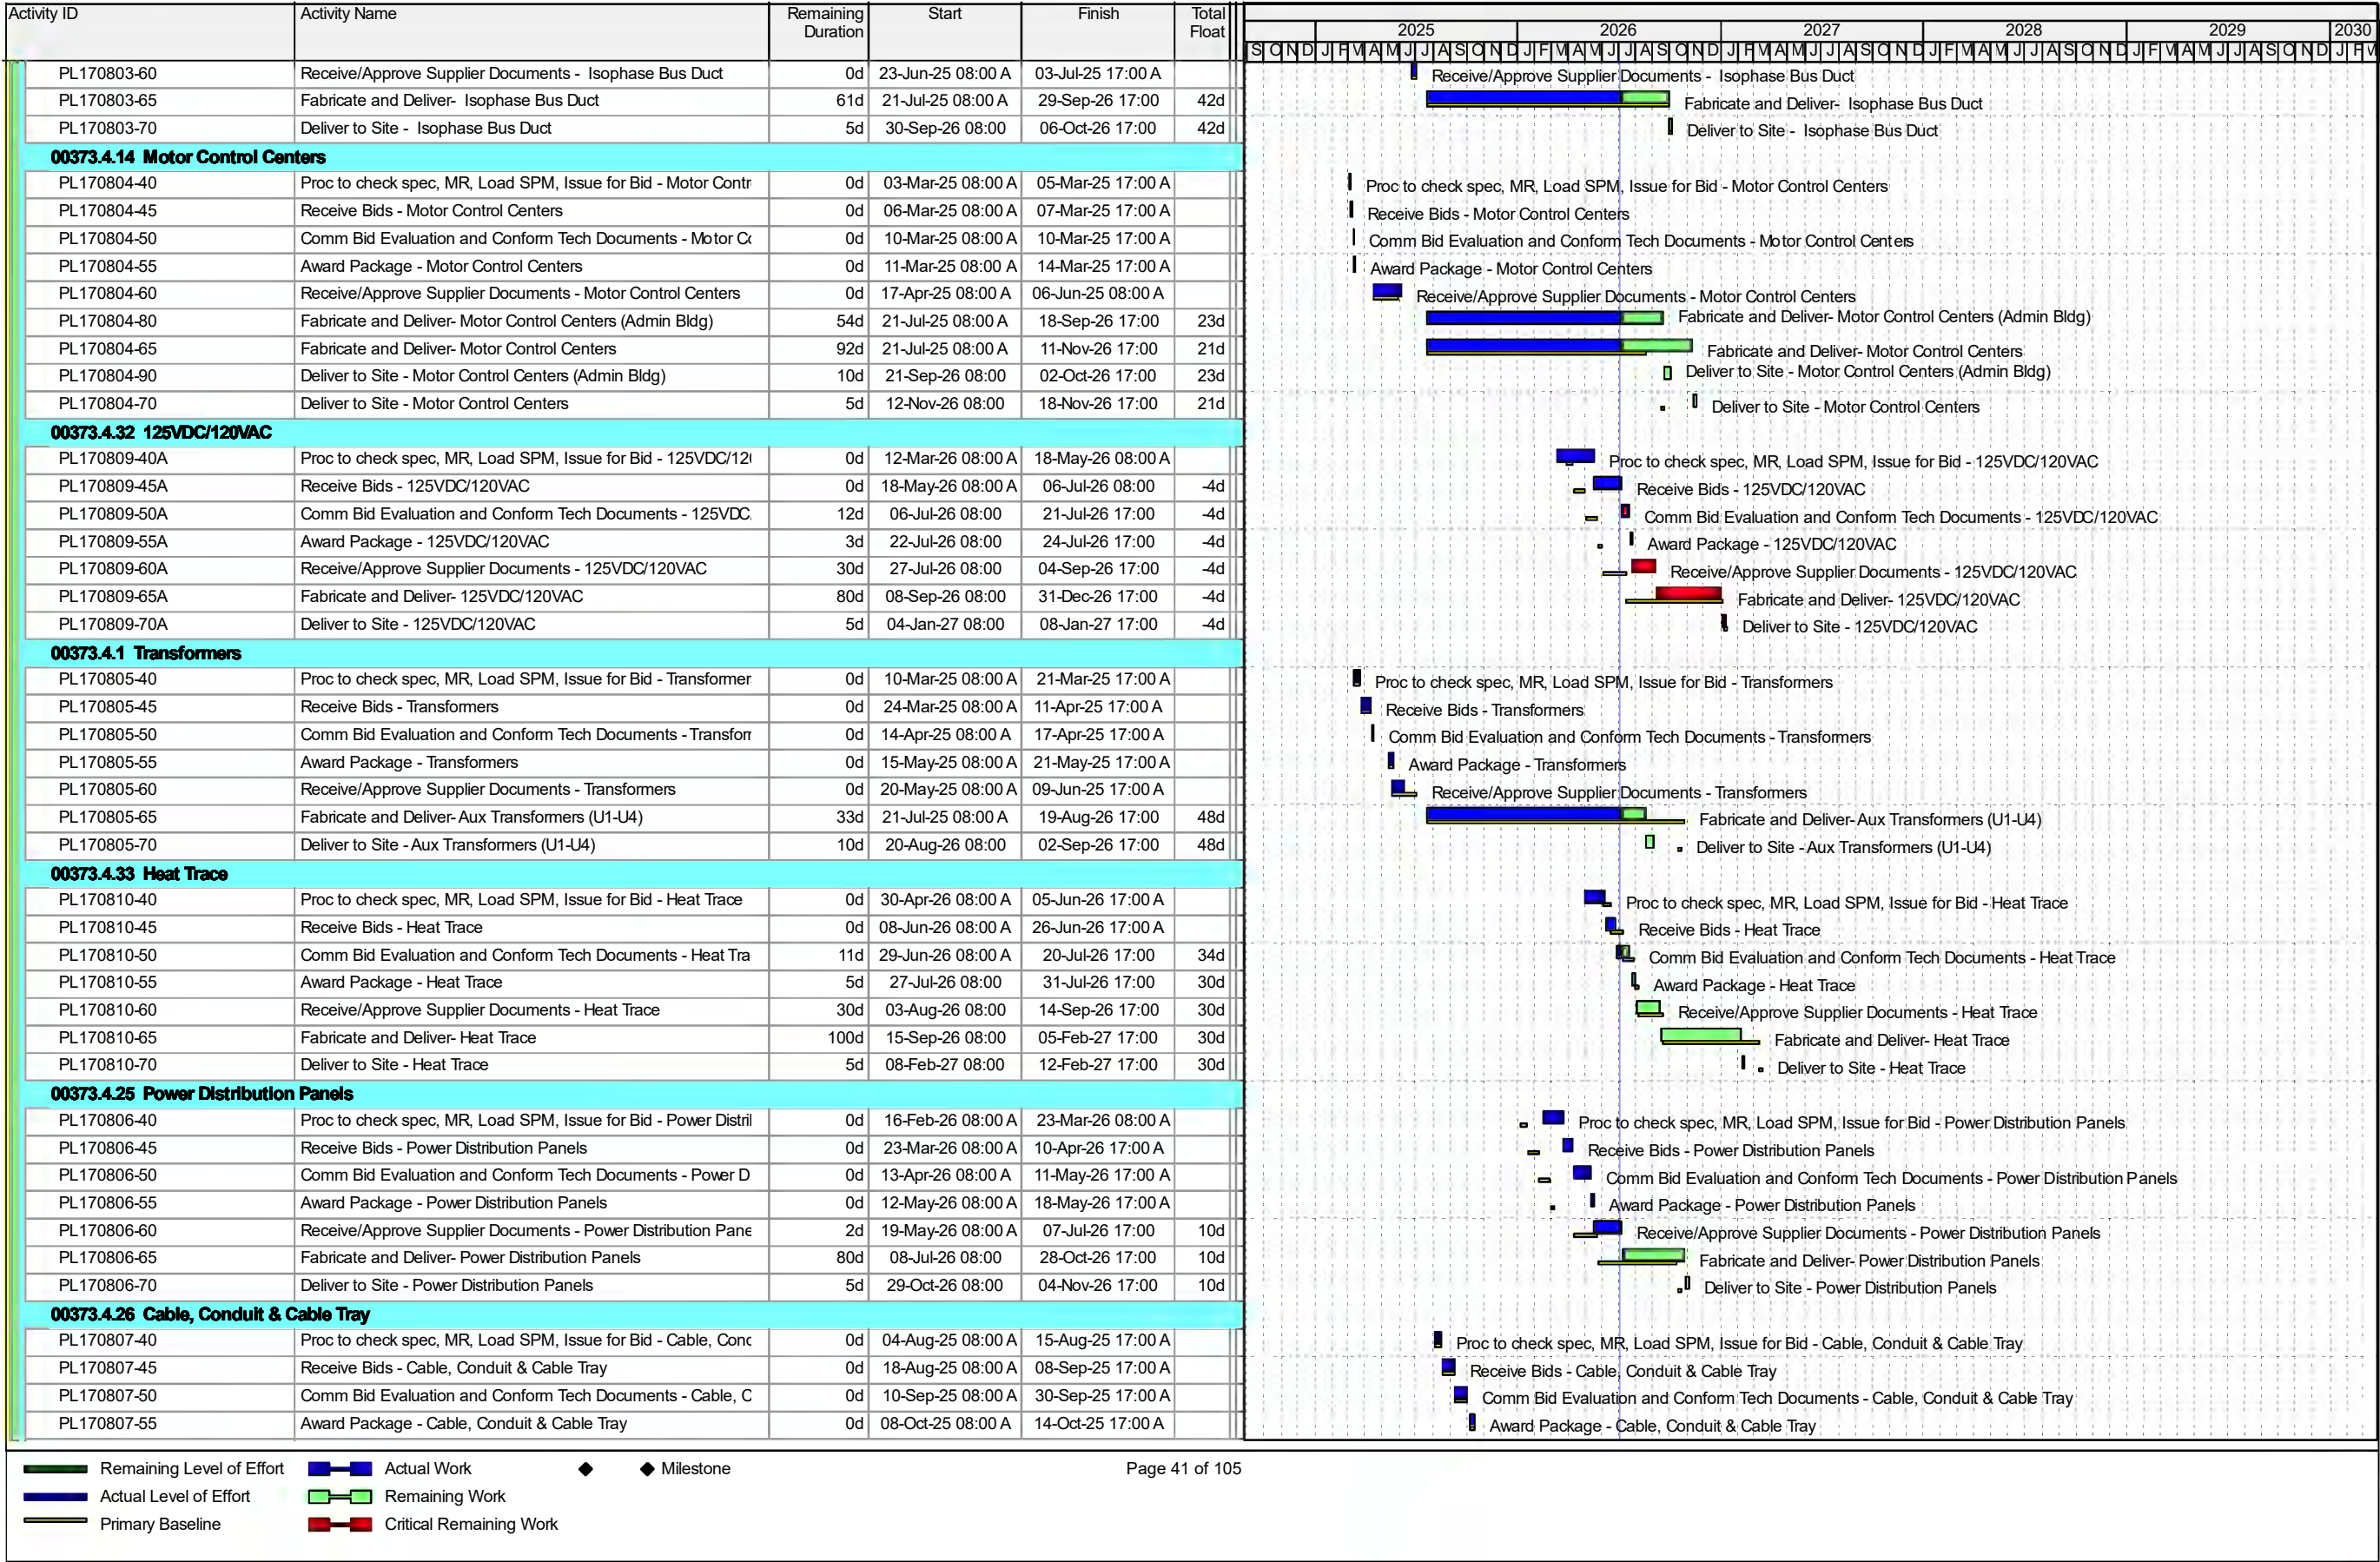


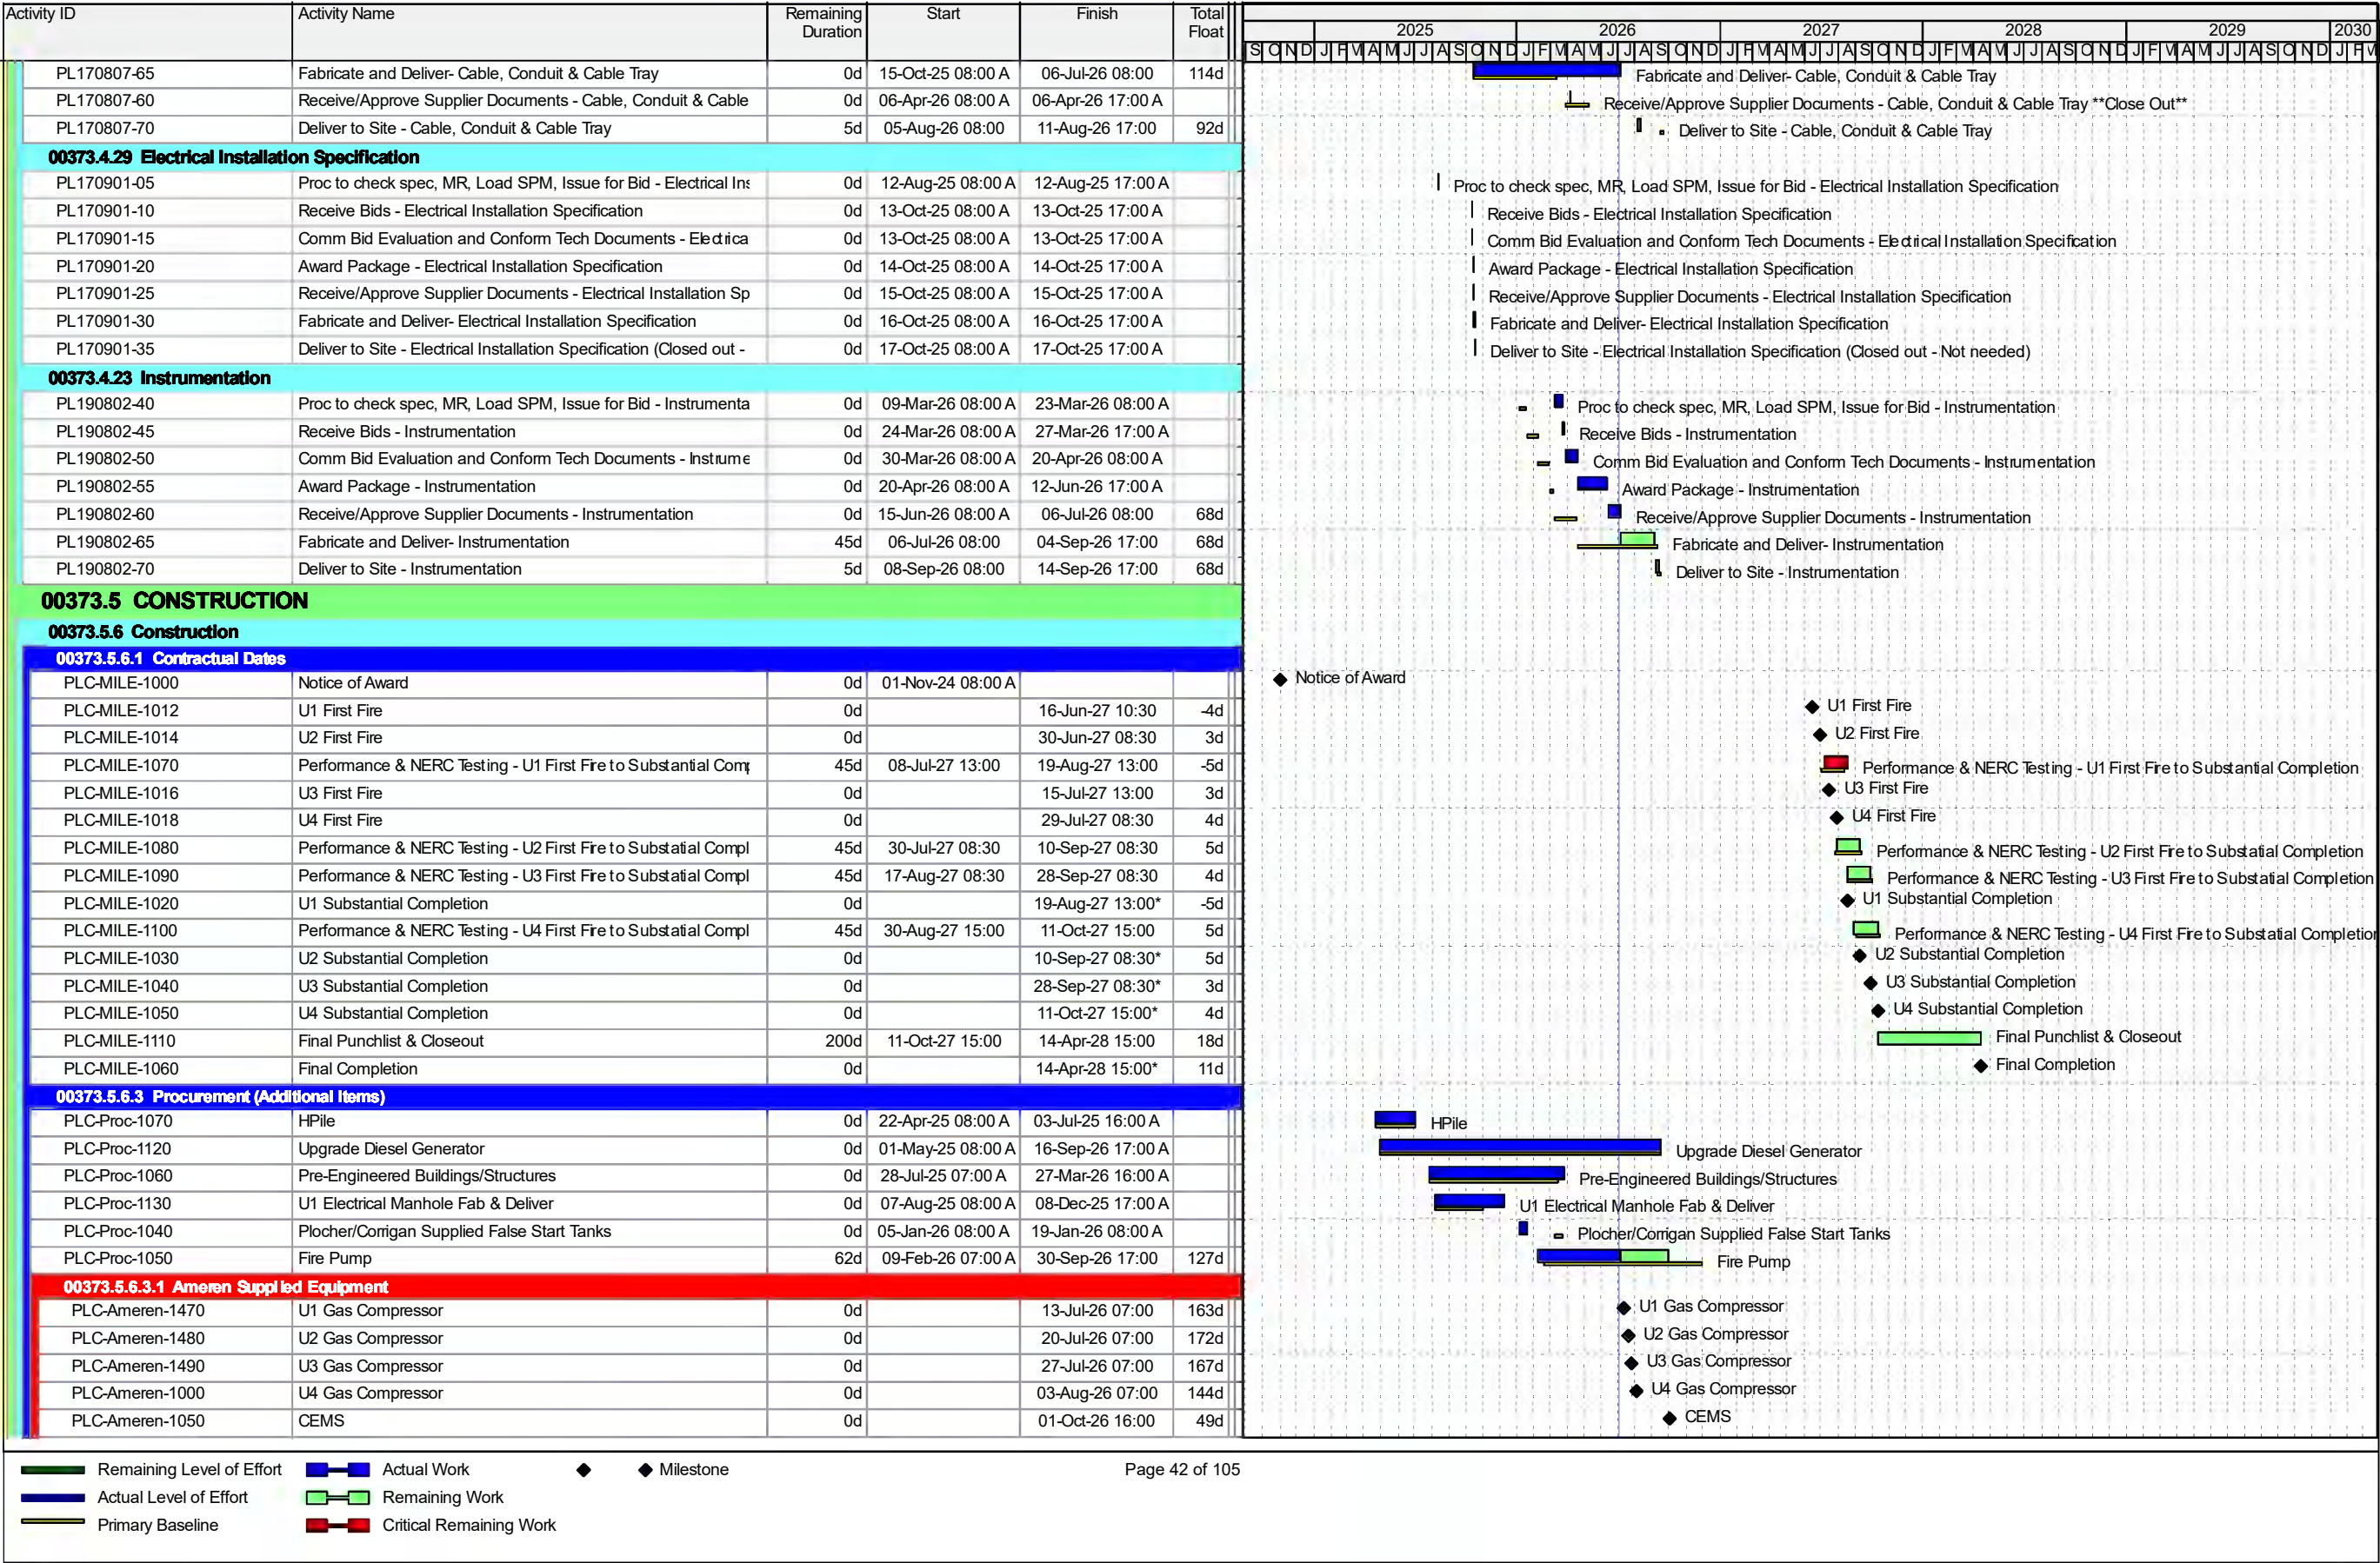



Remaining Level of Effort Actual Work Milestone
Actual Level of Effort Remaining Work
Primary Baseline Critical Remaining Work

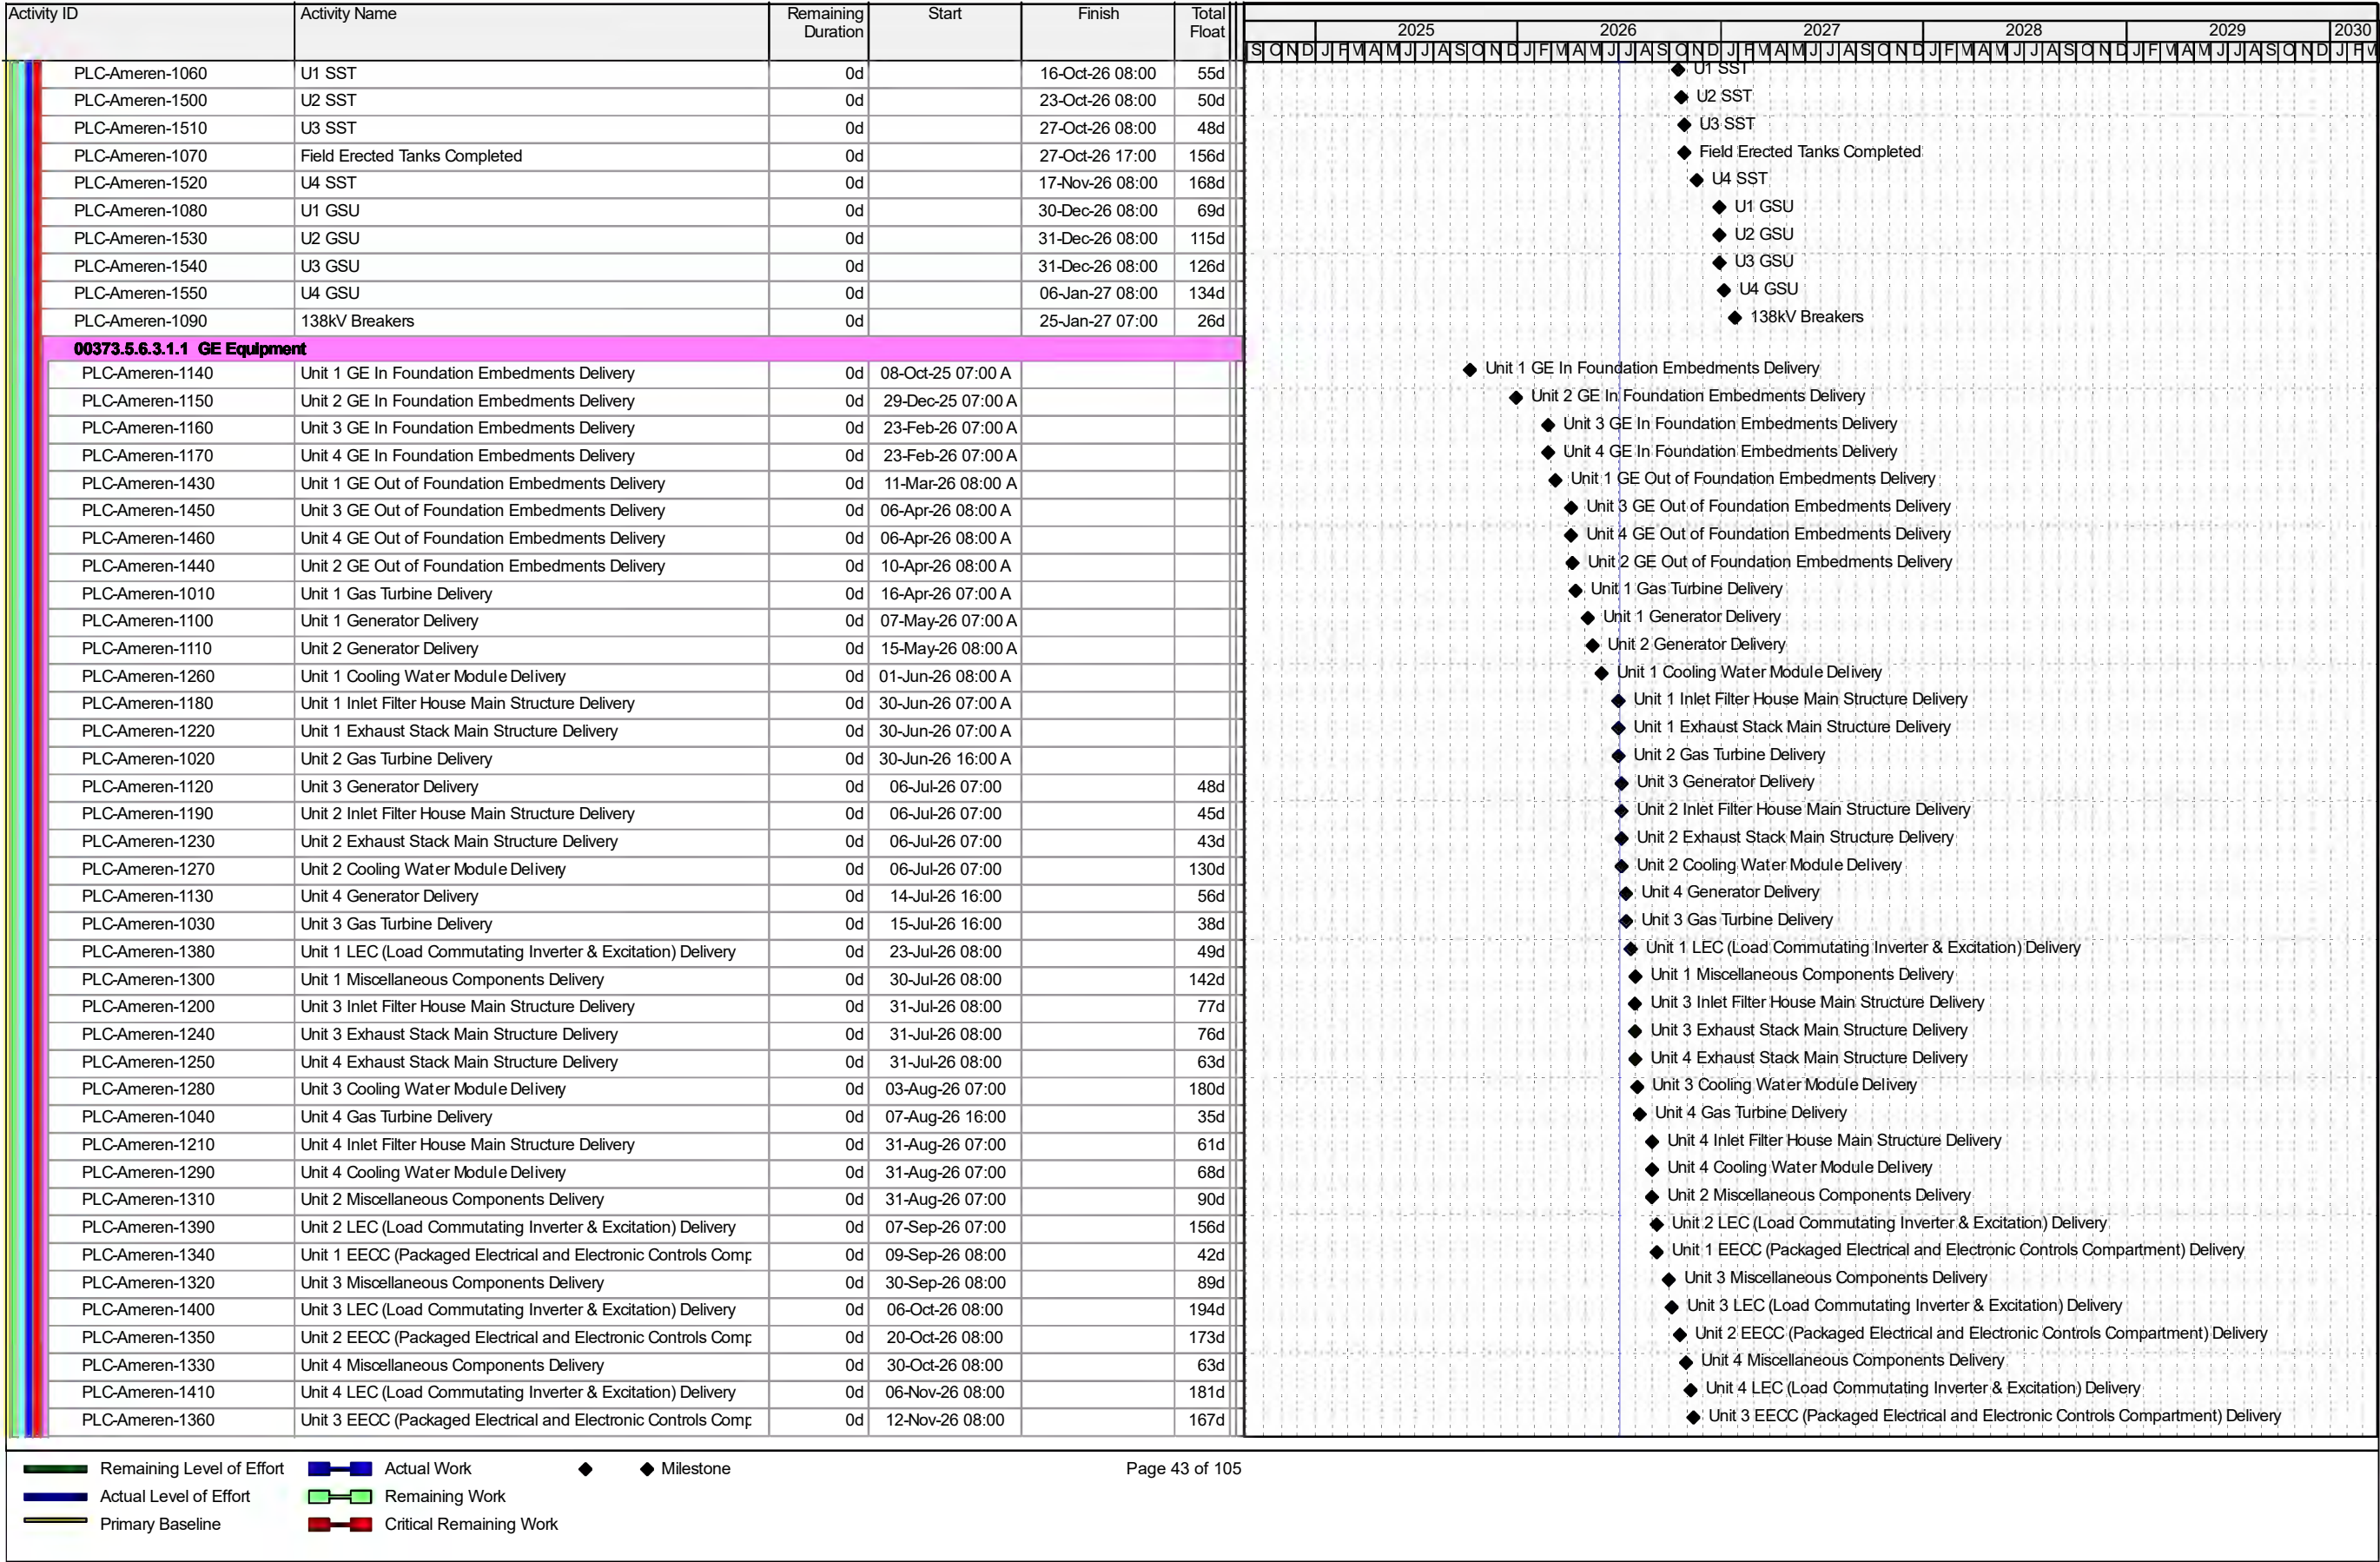


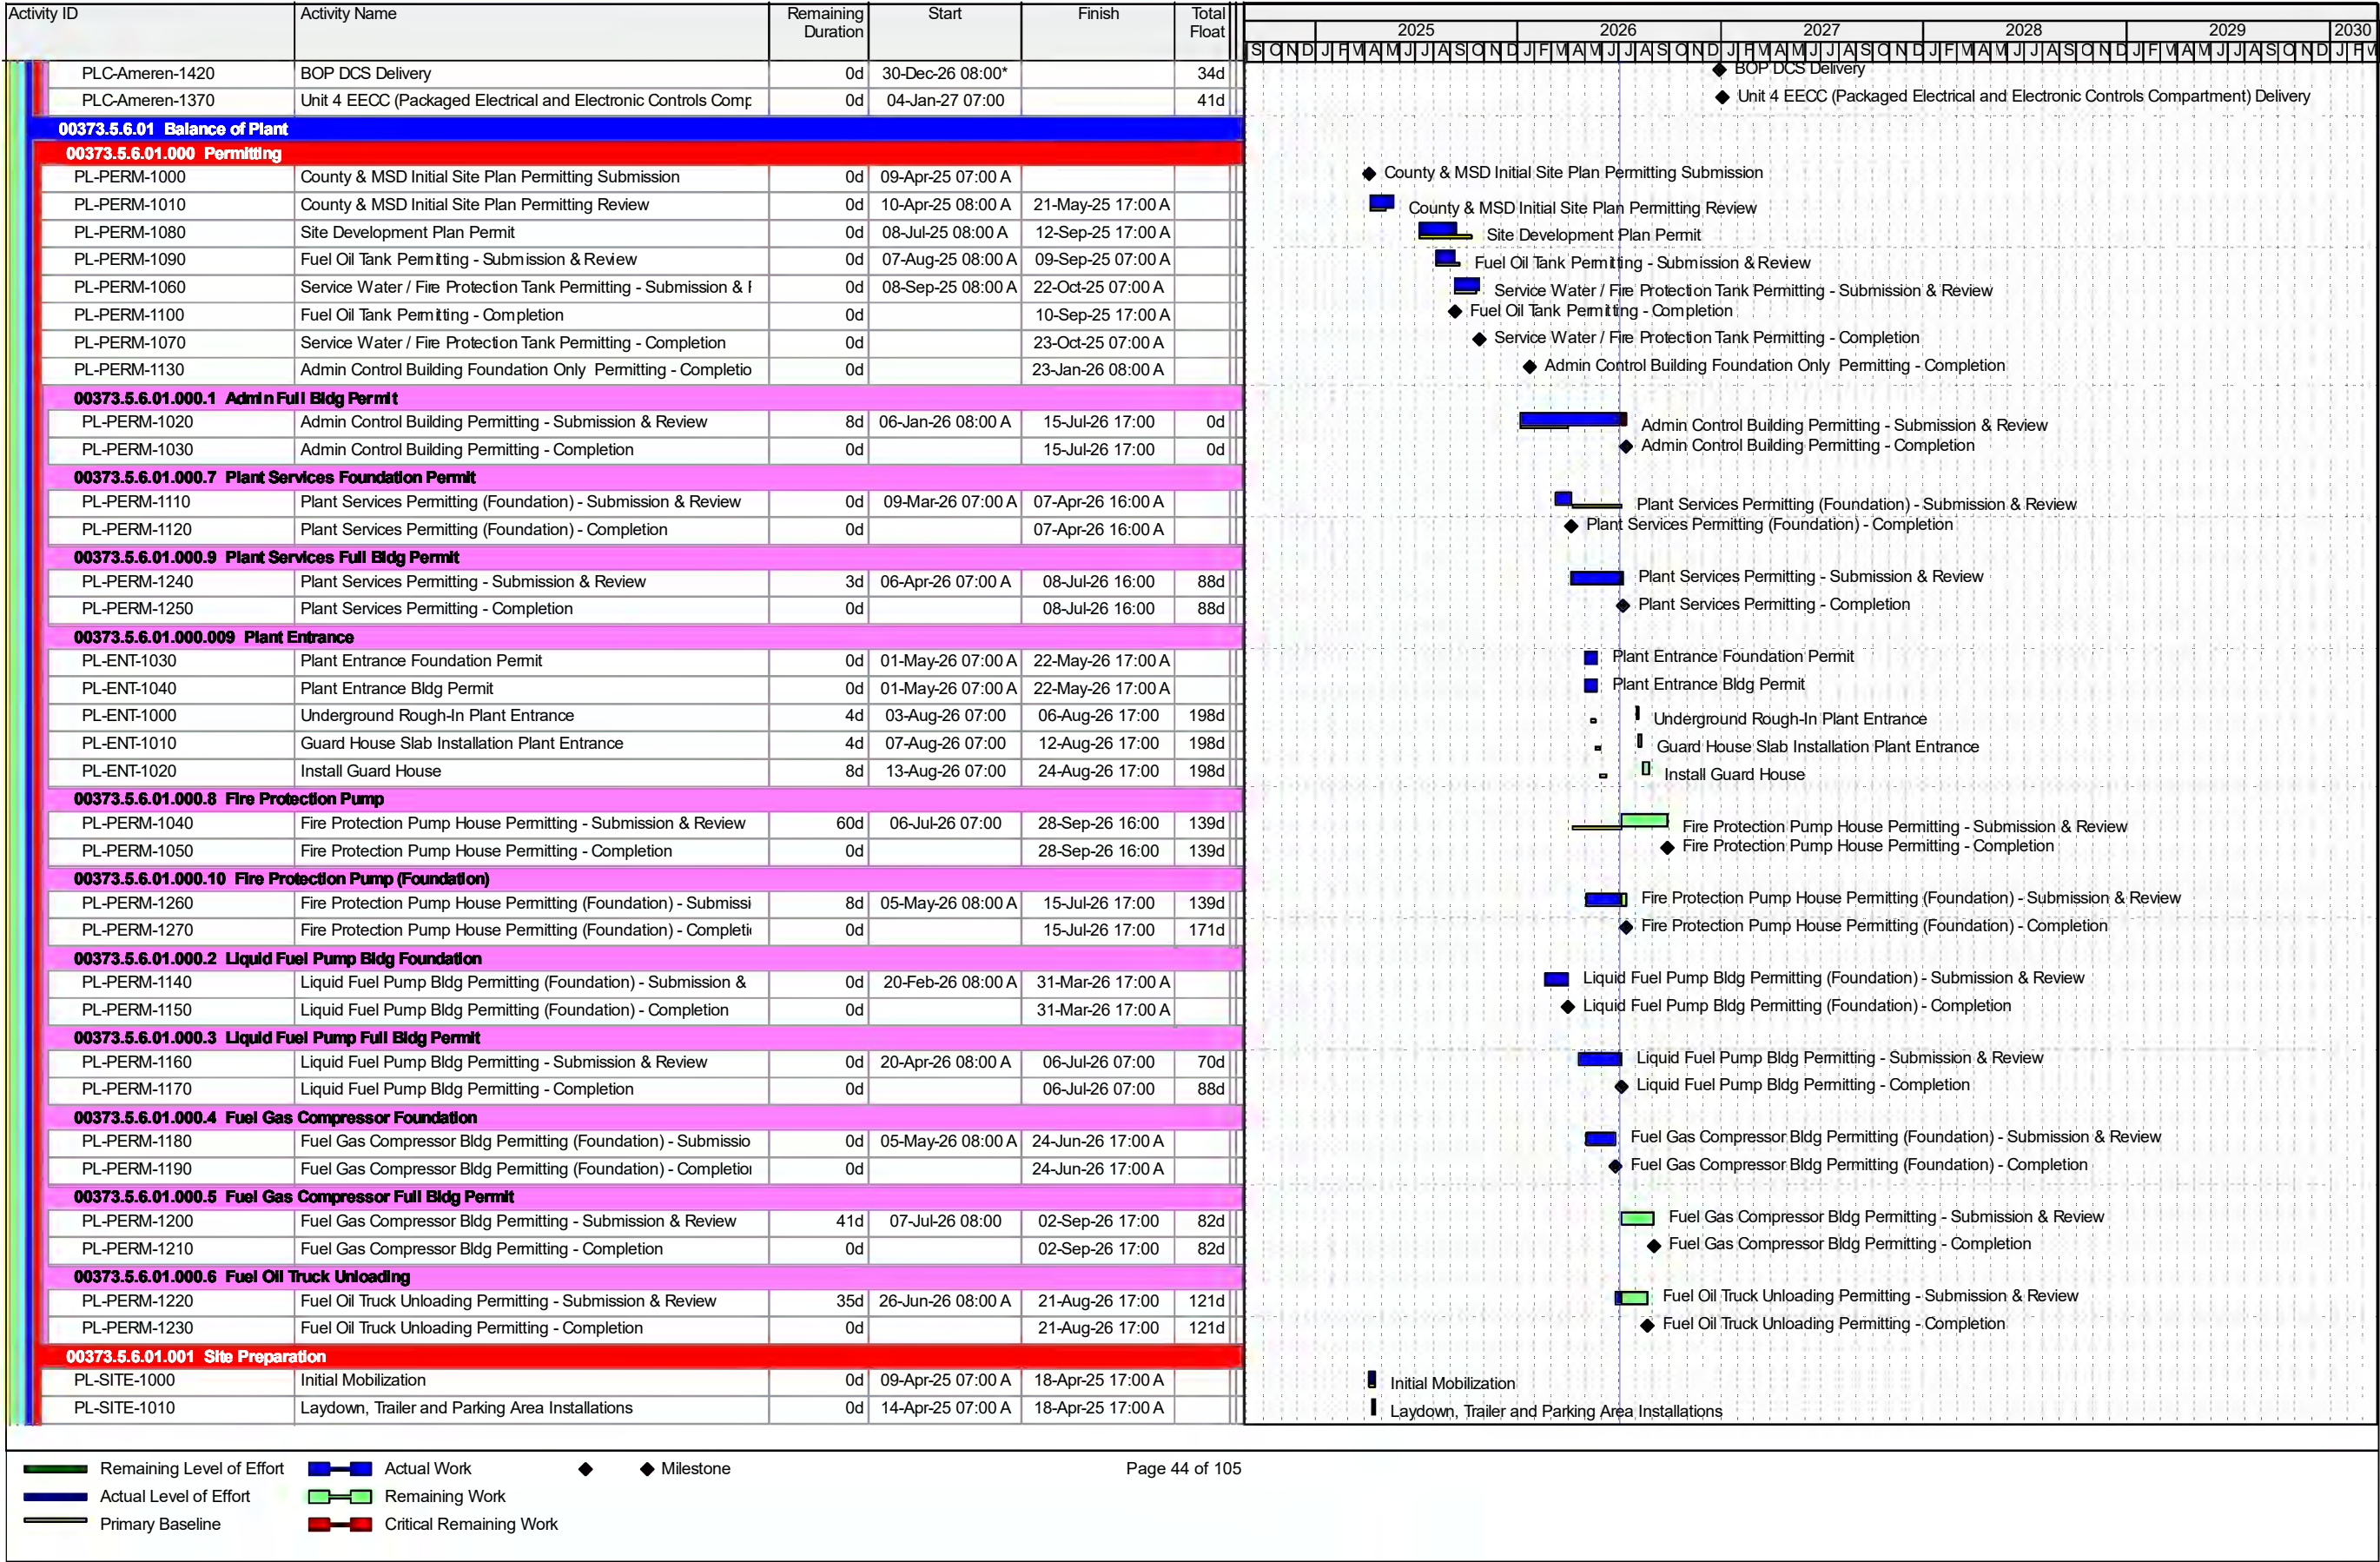

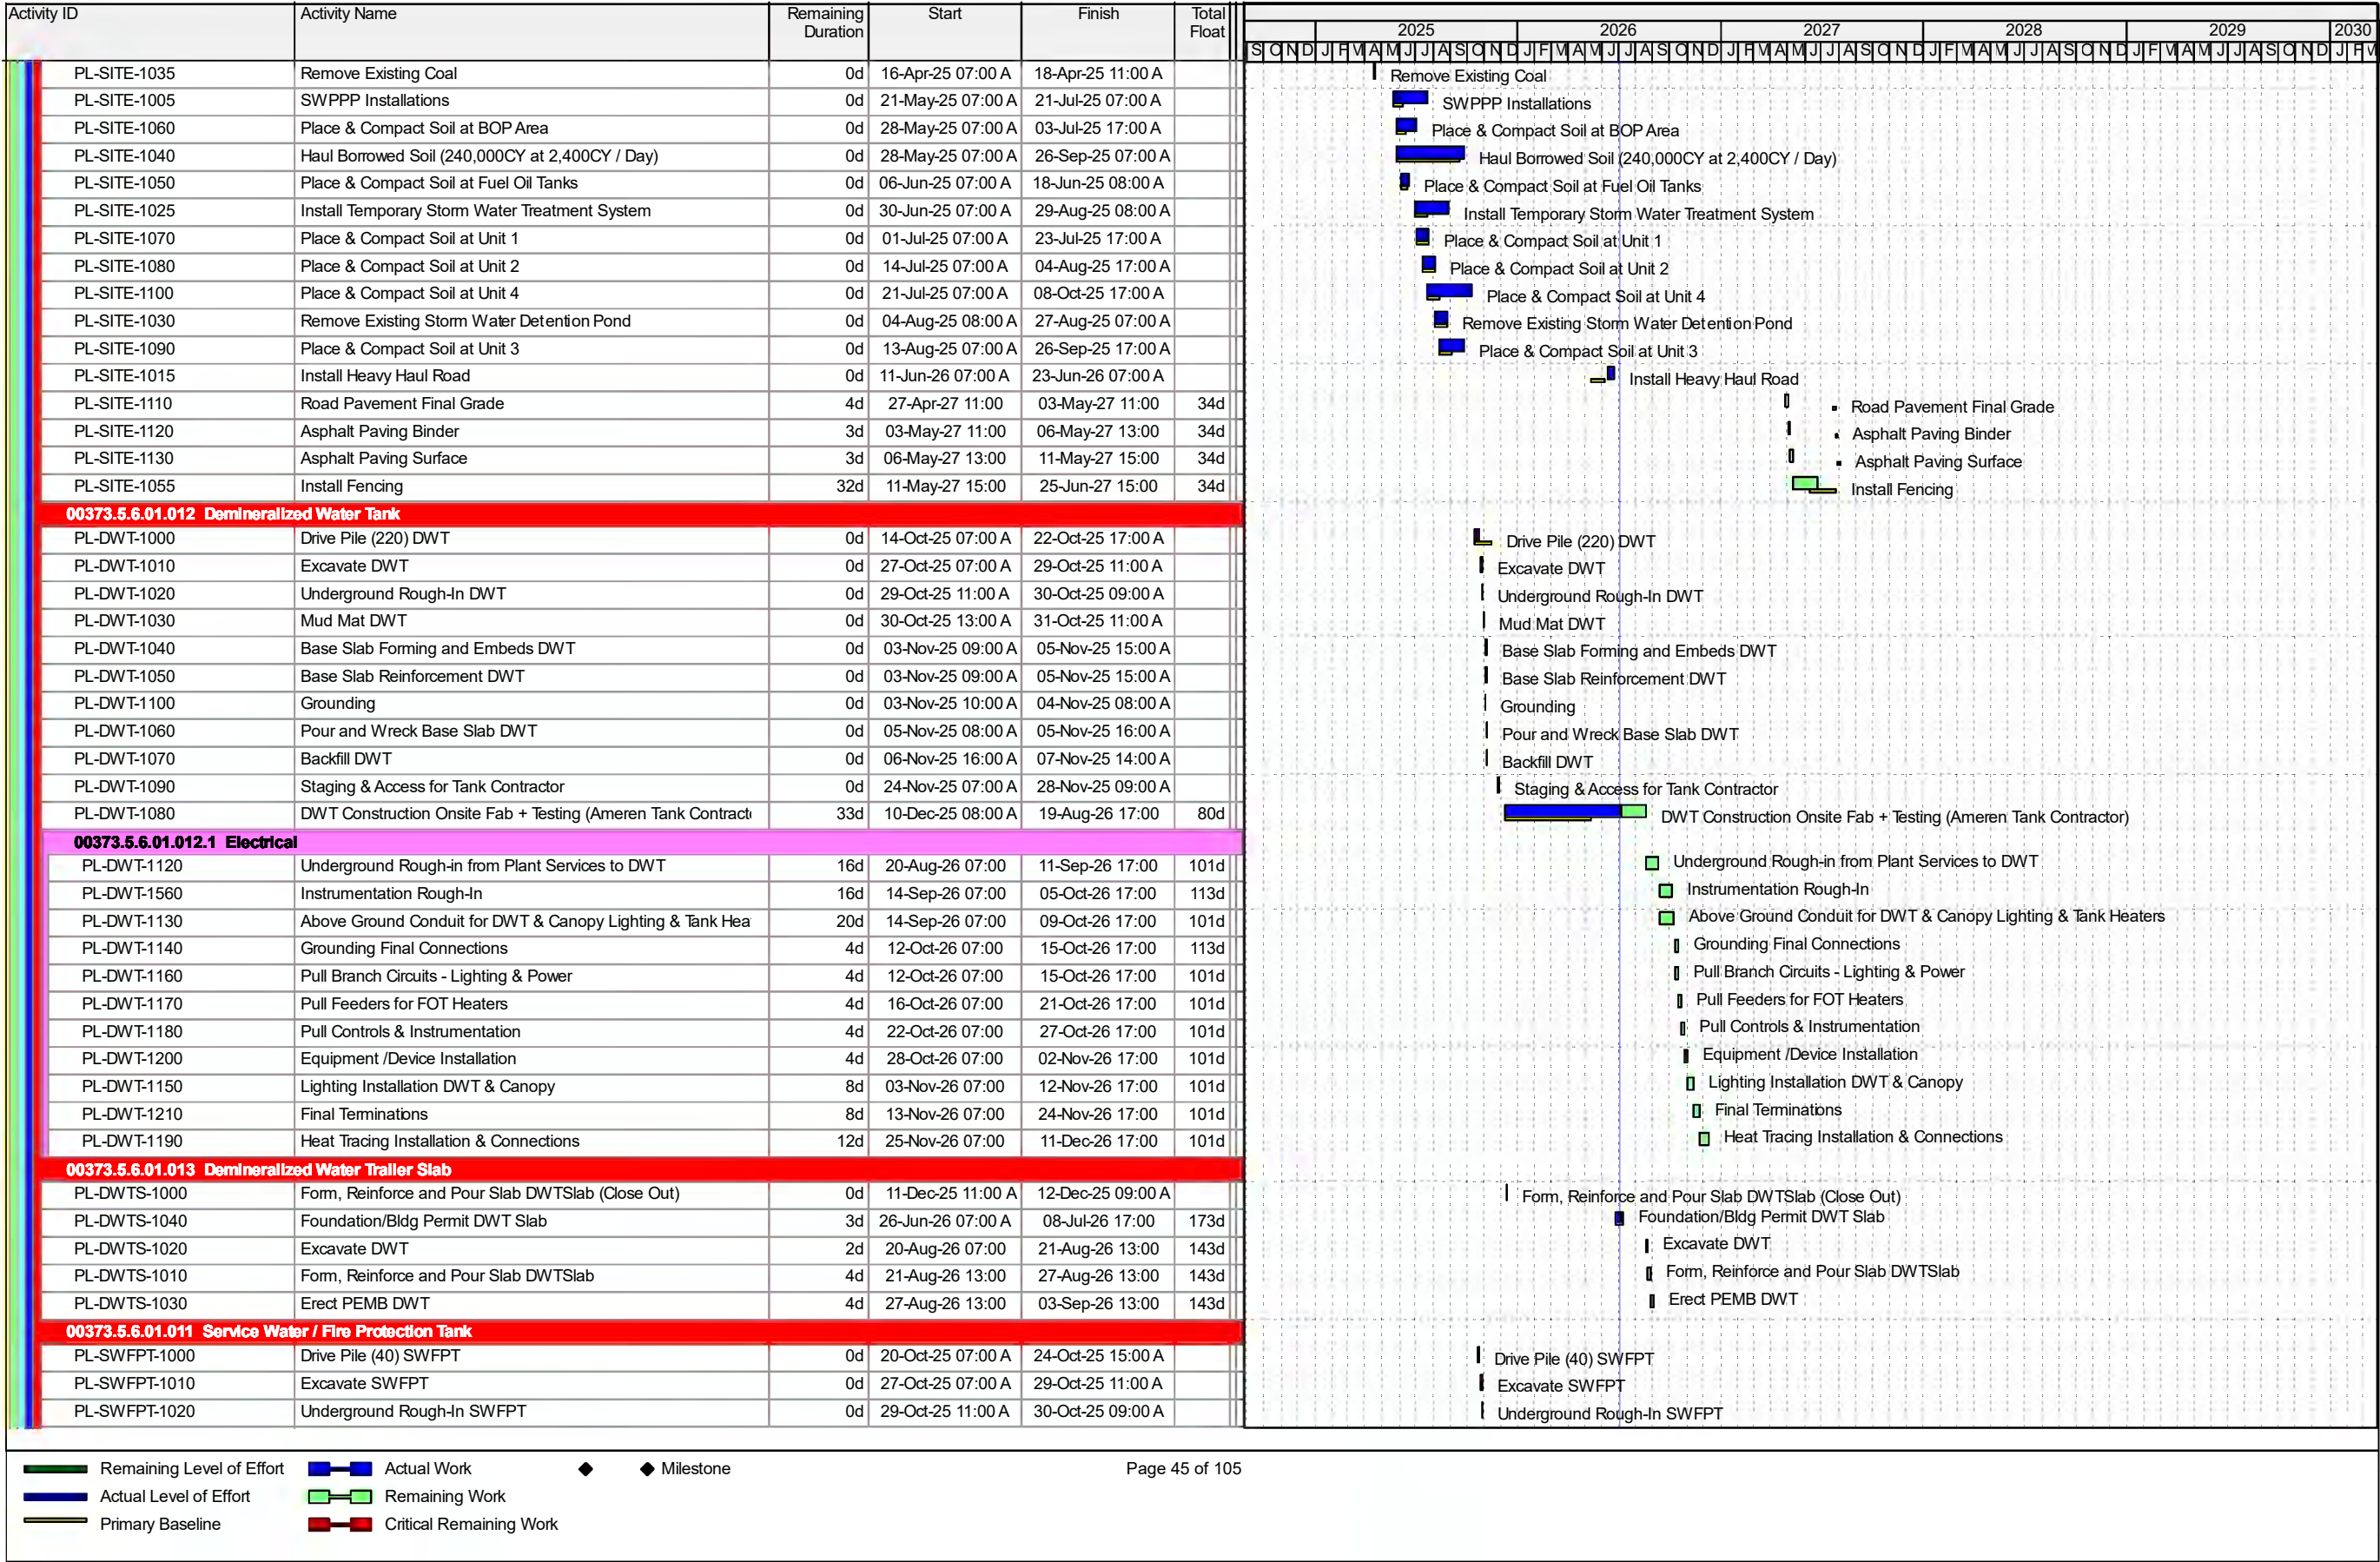

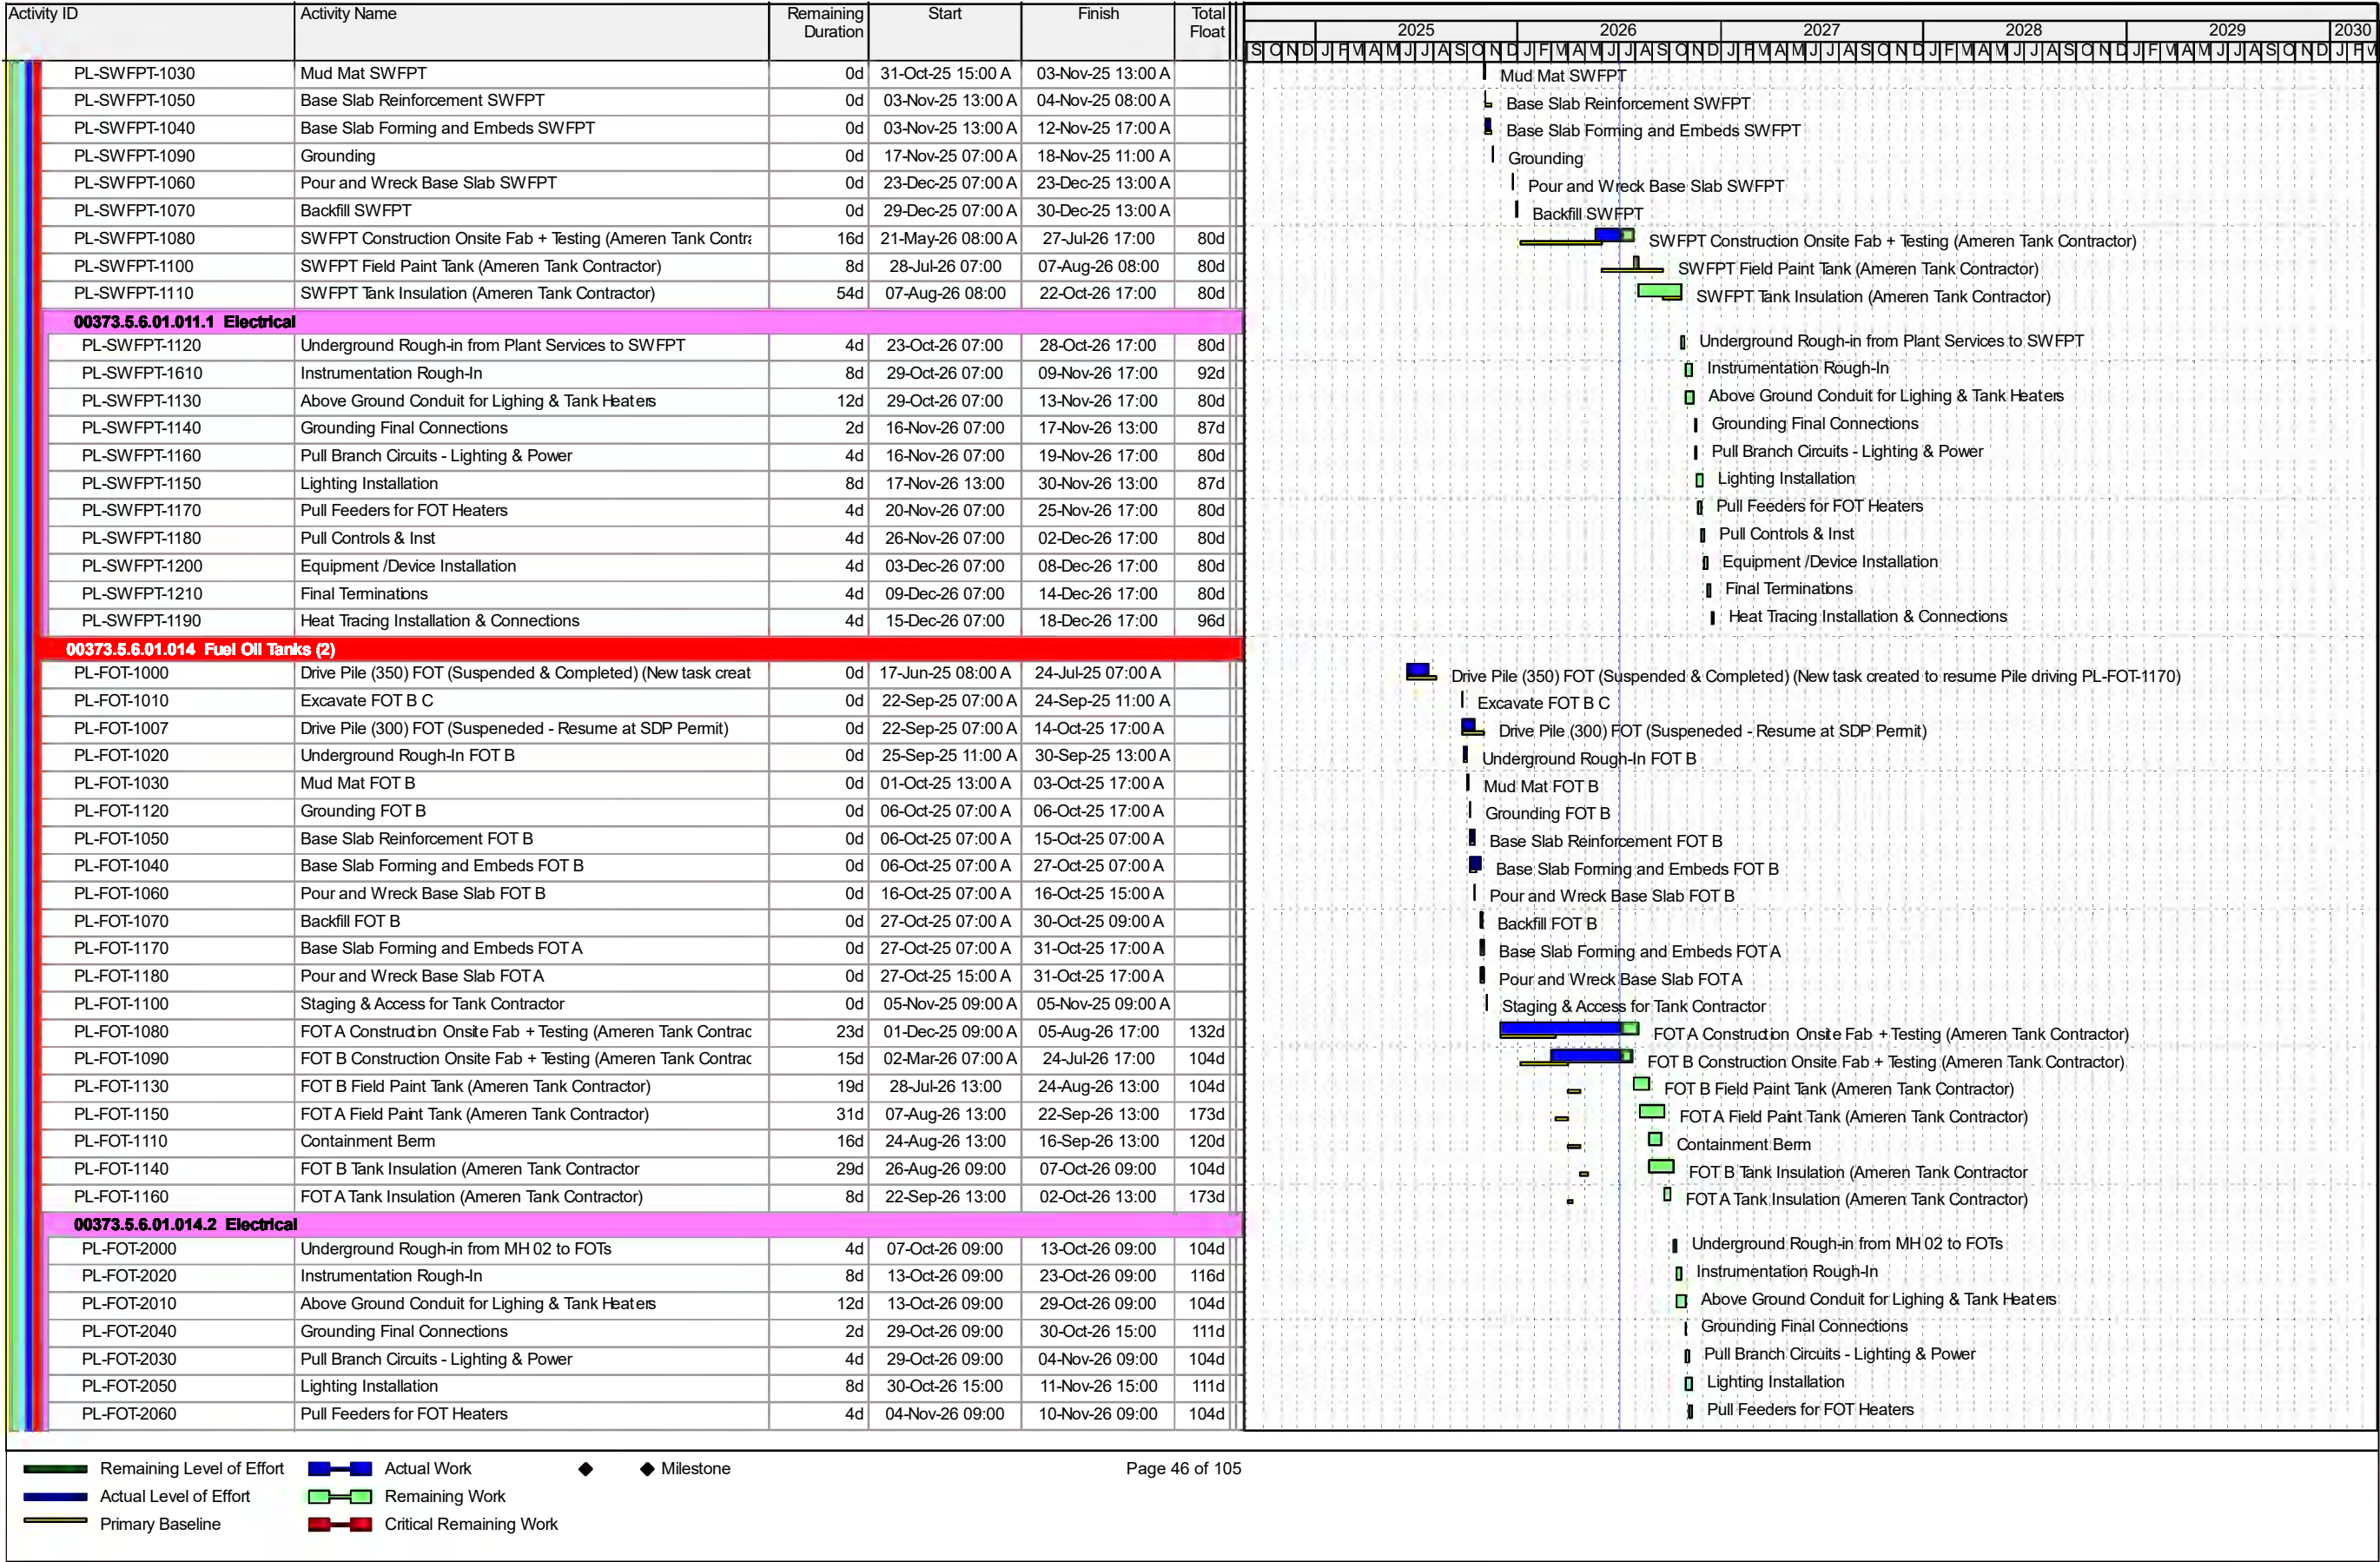

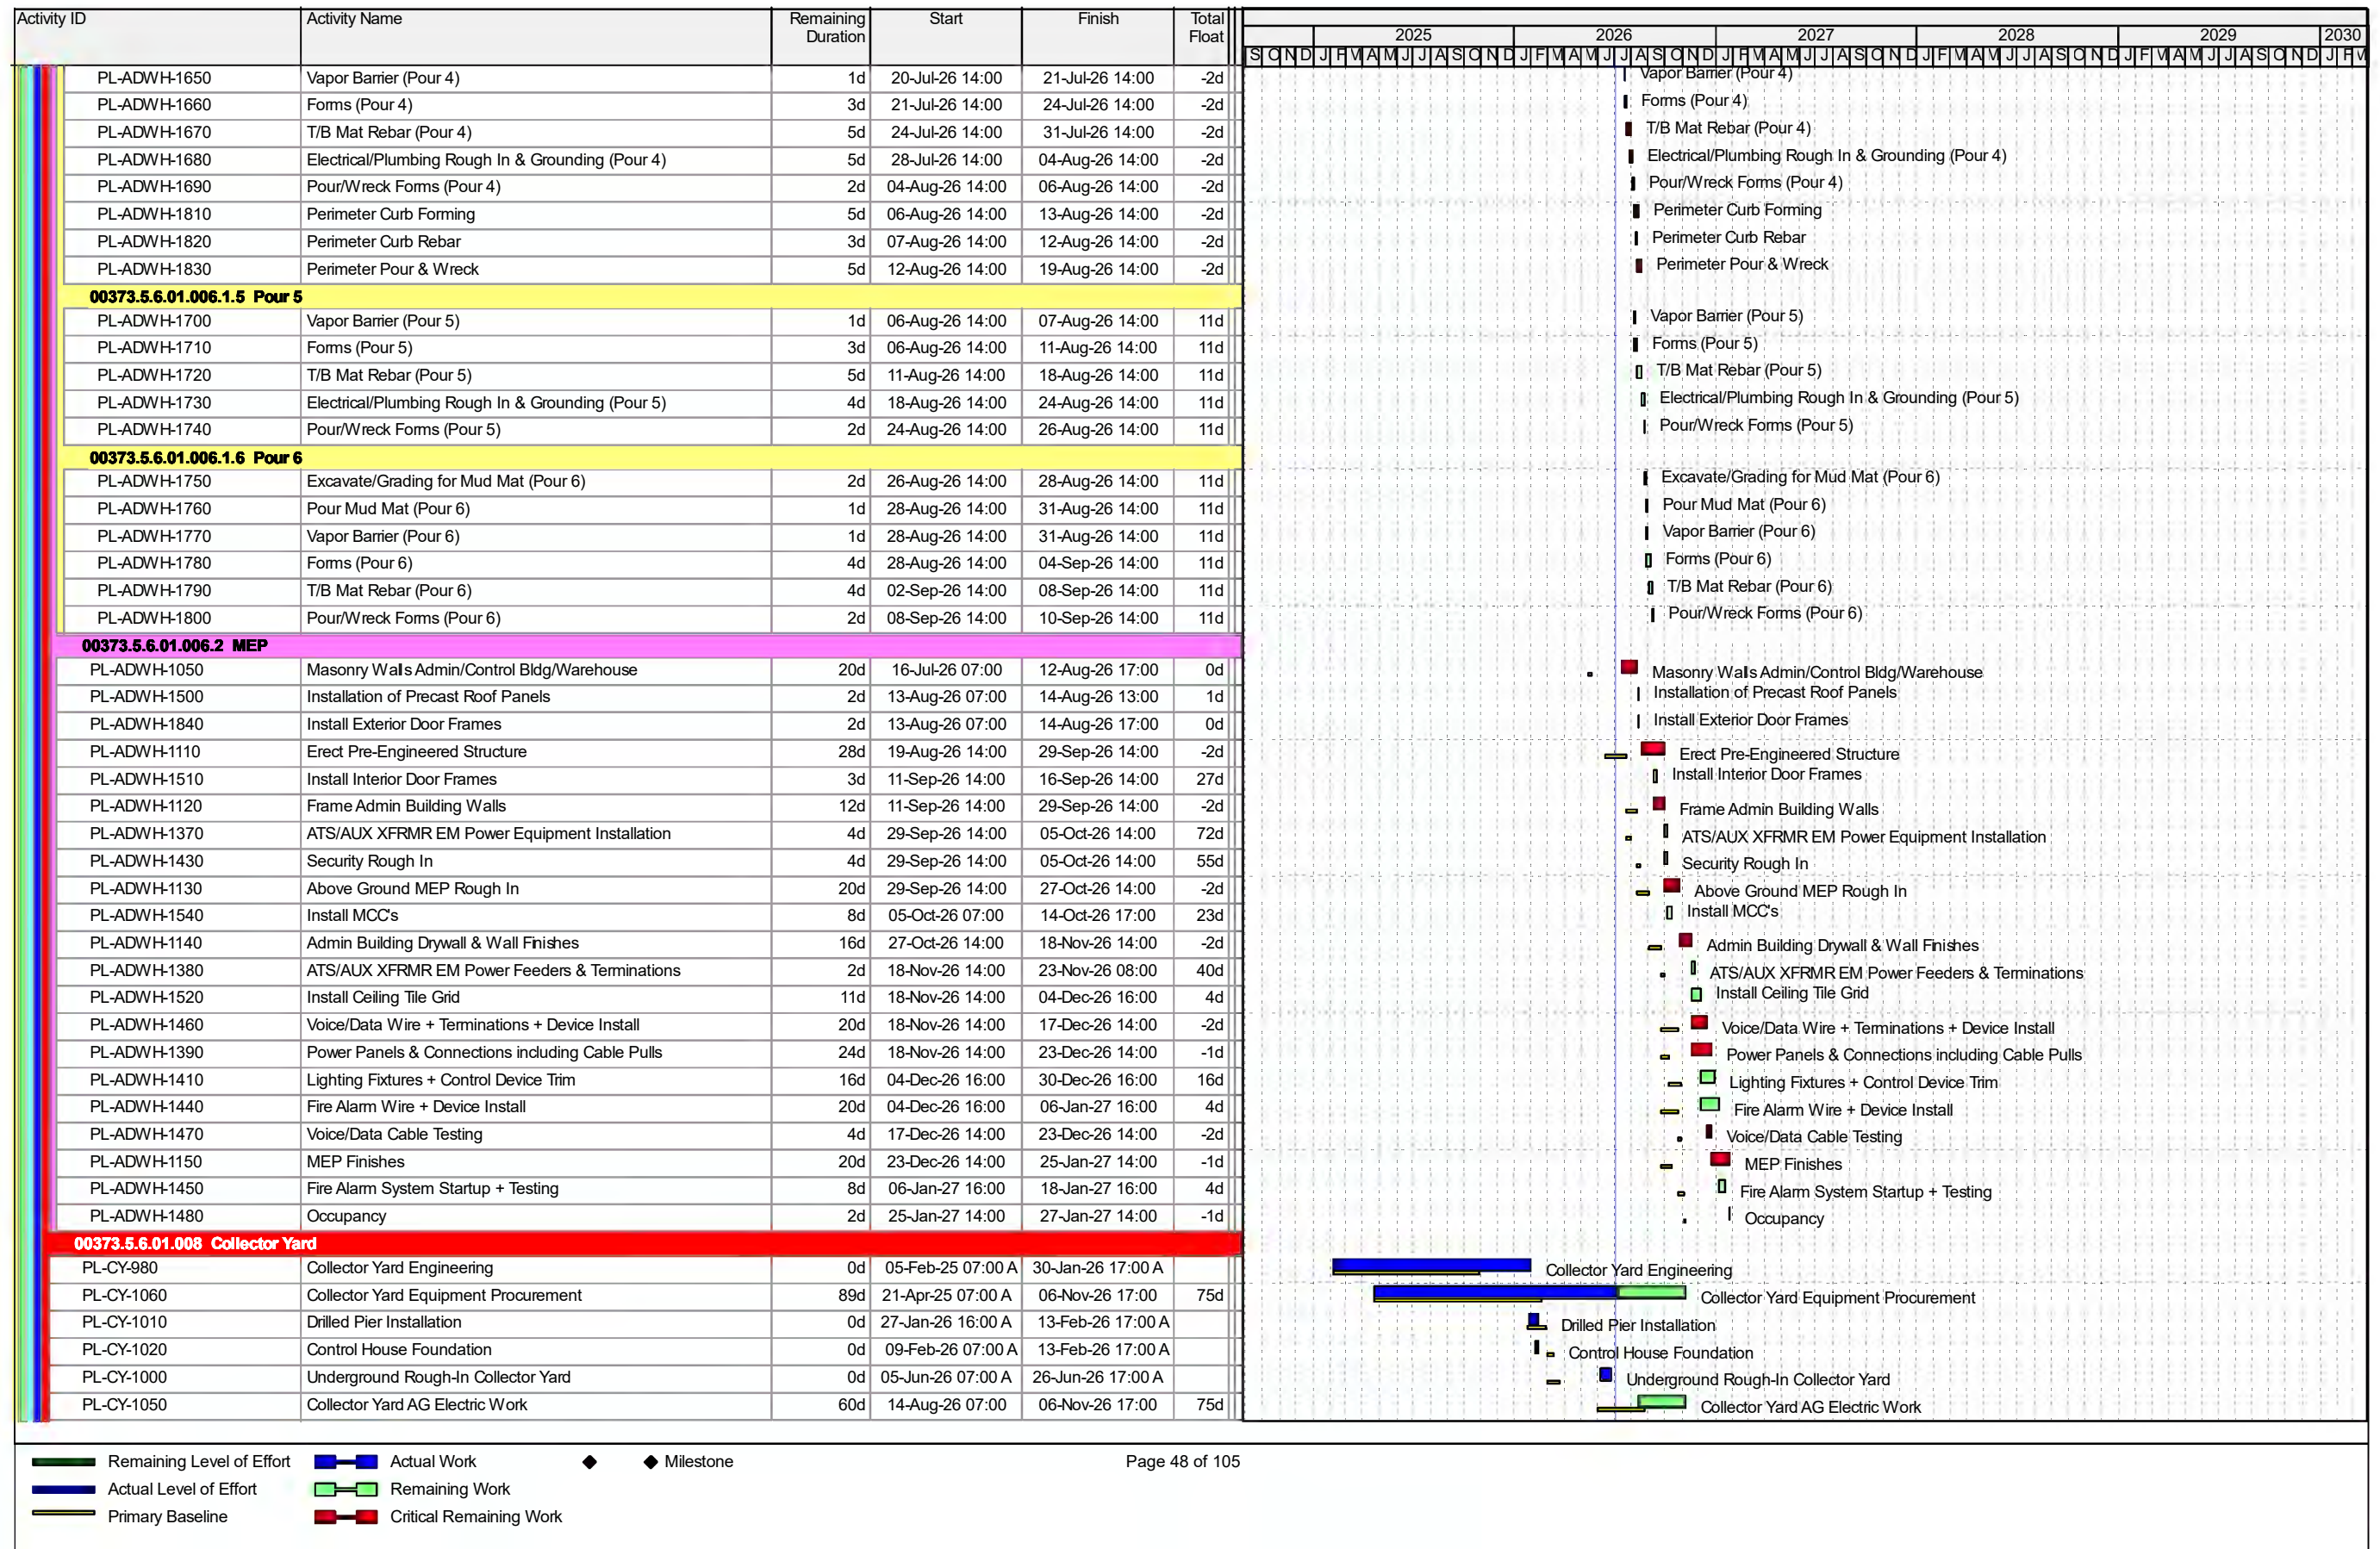


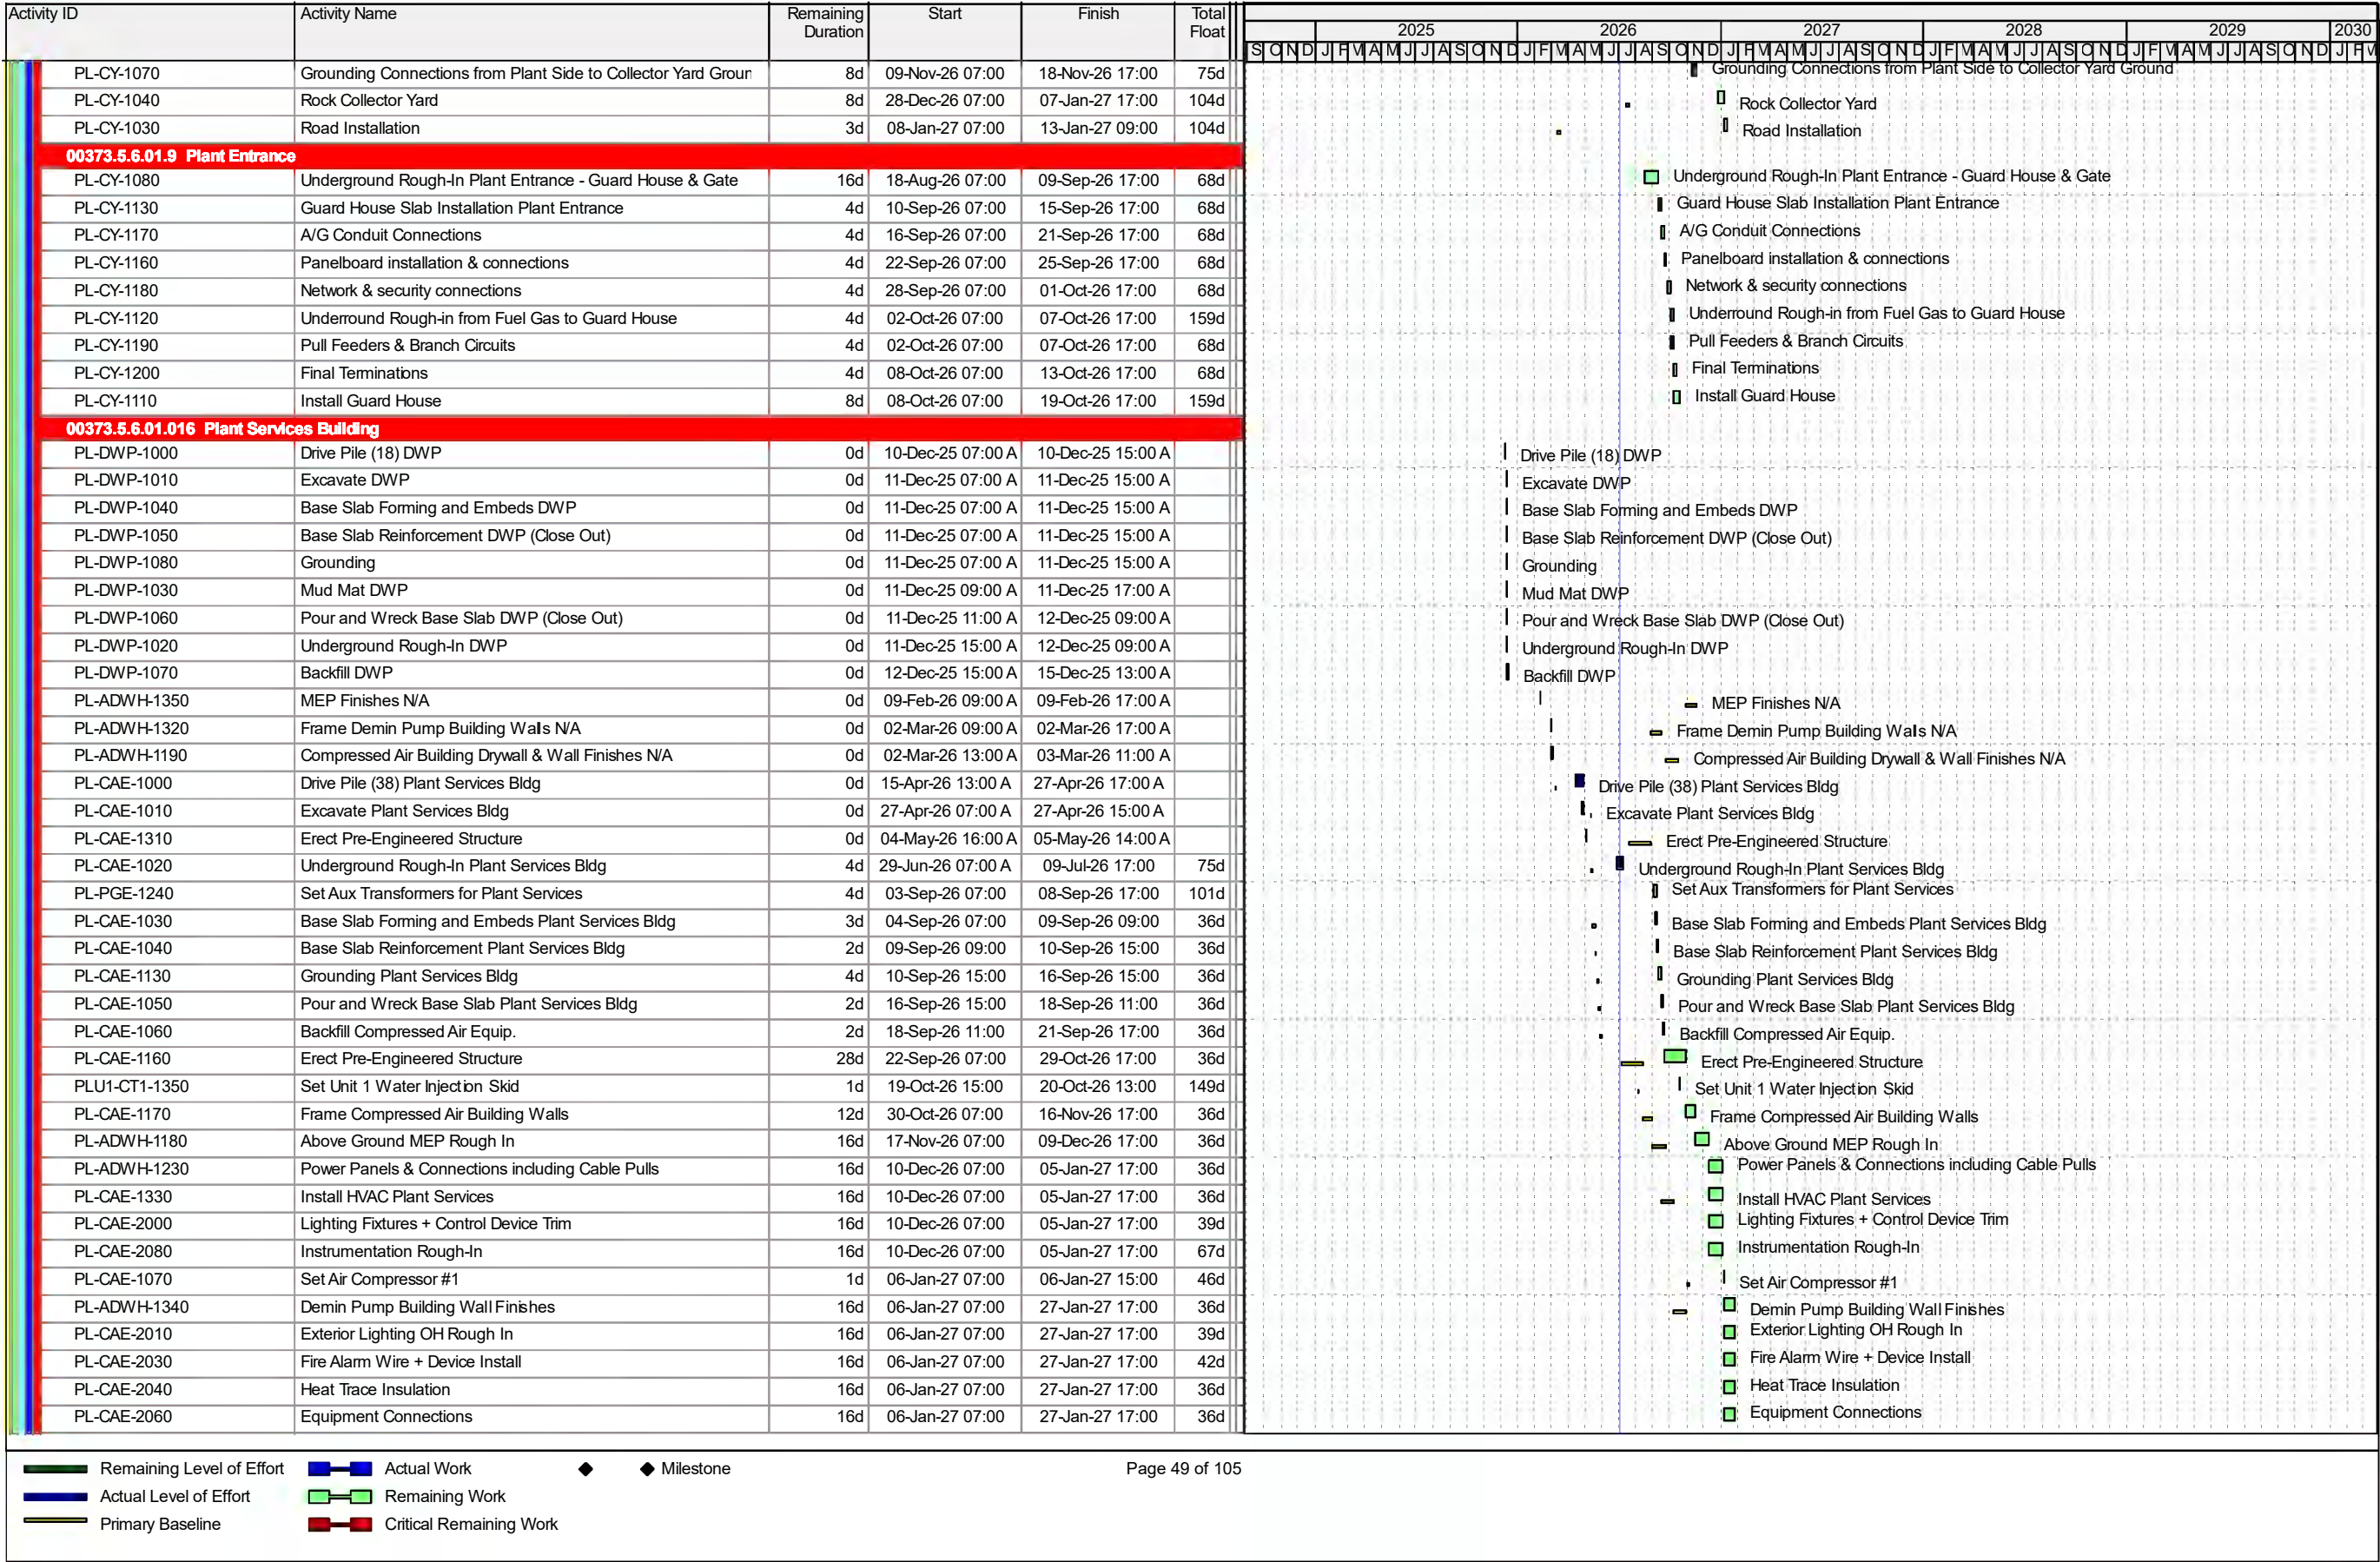


Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float																															
						2025				2026				2027				2028				2029				2030										
						S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
	PL-DG-1010	Excavate DG	1d	22-Jul-26 07:00	22-Jul-26 15:00	118d																														
	PL-DG-1020	Underground Rough-In DG	2d	22-Jul-26 15:00	27-Jul-26 09:00	118d																														
	PL-DG-1030	Mud Mat DG	1d	27-Jul-26 09:00	27-Jul-26 17:00	161d																														
	PL-DG-1040	Base Slab Forming and Embeds DG	4d	28-Jul-26 07:00	31-Jul-26 17:00	161d																														
	PL-DG-1080	Grounding	2d	03-Aug-26 07:00	04-Aug-26 13:00	161d																														
	PL-DG-1050	Base Slab Reinforcement DG	2d	03-Aug-26 07:00	05-Aug-26 11:00	161d																														
	PL-DG-1060	Pour and Wreck Base Slab DG	6d	05-Aug-26 11:00	12-Aug-26 17:00	161d																														
	PL-DG-1070	Backfill DG	2d	13-Aug-26 07:00	14-Aug-26 13:00	161d																														
	00373.5.6.01.044.1 Electrical																																			
		PL-PGE-1160	2000 KW Diesel Generator Receiving/Handling	4d	14-Aug-26 13:00	20-Aug-26 13:00	161d																													
	PL-PGE-1150	2000 KW Diesel Generator Prep & Set	12d	20-Aug-26 13:00	08-Sep-26 13:00	161d																														
	PL-DG-1250	Pull MV Feeder to EDG from Unit 1 Elect Enclosure	2d	08-Sep-26 13:00	10-Sep-26 17:00	161d																														
	PL-PGE-1170	Diesel Generator Remote Annunciator Install	2d	08-Sep-26 13:00	10-Sep-26 17:00	169d																														
	PL-DG-1260	Pull Communication & Controls to EDG	2d	11-Sep-26 07:00	14-Sep-26 13:00	161d																														
	PL-DG-1270	Pull Branch UPS circuits from Unit 1 Elect Enclosure	2d	14-Sep-26 13:00	16-Sep-26 09:00	161d																														
	PL-DG-1280	Terminate all Feeders, Communication & controls at EDG	4d	16-Sep-26 09:00	22-Sep-26 09:00	161d																														
	PL-DG-1290	Factory Startup & Load Testing	2d	22-Sep-26 09:00	23-Sep-26 15:00	161d																														
00373.5.6.01.010 Fire Protection Pump House																																				
	PL-FPPH-1000	Drive Pile (6) Fire Pump House (N/A)	0d	01-Apr-26 07:00 A	02-Apr-26 13:00 A																															
	PL-FPPH-1010	Excavate Fire Pump House	1d	28-Jul-26 07:00	28-Jul-26 15:00	163d																														
	PL-FPPH-1020	Underground Rough-In Fire Pump House	2d	28-Jul-26 15:00	31-Jul-26 09:00	163d																														
	PL-FPPH-1030	Base Slab Forming and Embeds Fire Pump House	2d	31-Jul-26 09:00	04-Aug-26 13:00	163d																														
	PL-FPPH-1040	Base Slab Reinforcement Fire Pump House	2d	04-Aug-26 13:00	06-Aug-26 09:00	163d																														
	PL-FPPH-1070	Grounding	2d	04-Aug-26 13:00	06-Aug-26 17:00	163d																														
	PL-FPPH-1050	Pour and Wreck Base Slab Fire Pump House	2d	07-Aug-26 07:00	10-Aug-26 13:00	163d																														
	PL-FPPH-1060	Backfill Fire Pump House	2d	01-Oct-26 07:00	02-Oct-26 13:00	127d																														
00373.5.6.01.010.1 Electrical																																				
	PL-FPPH-1300	Fire Alarm Wire & Device Install	4d	02-Oct-26 13:00	08-Oct-26 13:00	127d																														
	PL-FPPH-1310	Pull 600v Feeder to Electrical Fire Pump	4d	08-Oct-26 13:00	14-Oct-26 13:00	127d																														
	PL-FPPH-1320	Terminate all Feeders, Communication & Controls	2d	06-Nov-26 07:00	10-Nov-26 11:00	110d																														
00373.5.6.01.043 Hydrogen Trailers																																				
	PL-HT-1350	Underground ductbank from MH01 to Hydrogen Trailer location	2d	13-Aug-26 07:00	17-Aug-26 11:00	184d																														
	PL-HT-1360	Above Ground Conduit	2d	17-Aug-26 11:00	19-Aug-26 15:00	184d																														
	PL-HT-1000	Form, Reinforce and Pour Slab Hydrogen Trailers	4d	08-Sep-26 11:00	14-Sep-26 11:00	167d																														
	PL-HT-1340	Misc Wire Pulls & Final Terminations	2d	16-Oct-26 07:00	20-Oct-26 11:00	144d																														
00373.5.6.01.019 Fuel Gas Metering Yard Area																																				
	PL-FGMY-1000	Place Holder for Gas Metering Yard	62d	01-Dec-25 11:00 A	30-Sep-26 17:00	126d																														

[illegible]

[illegible]

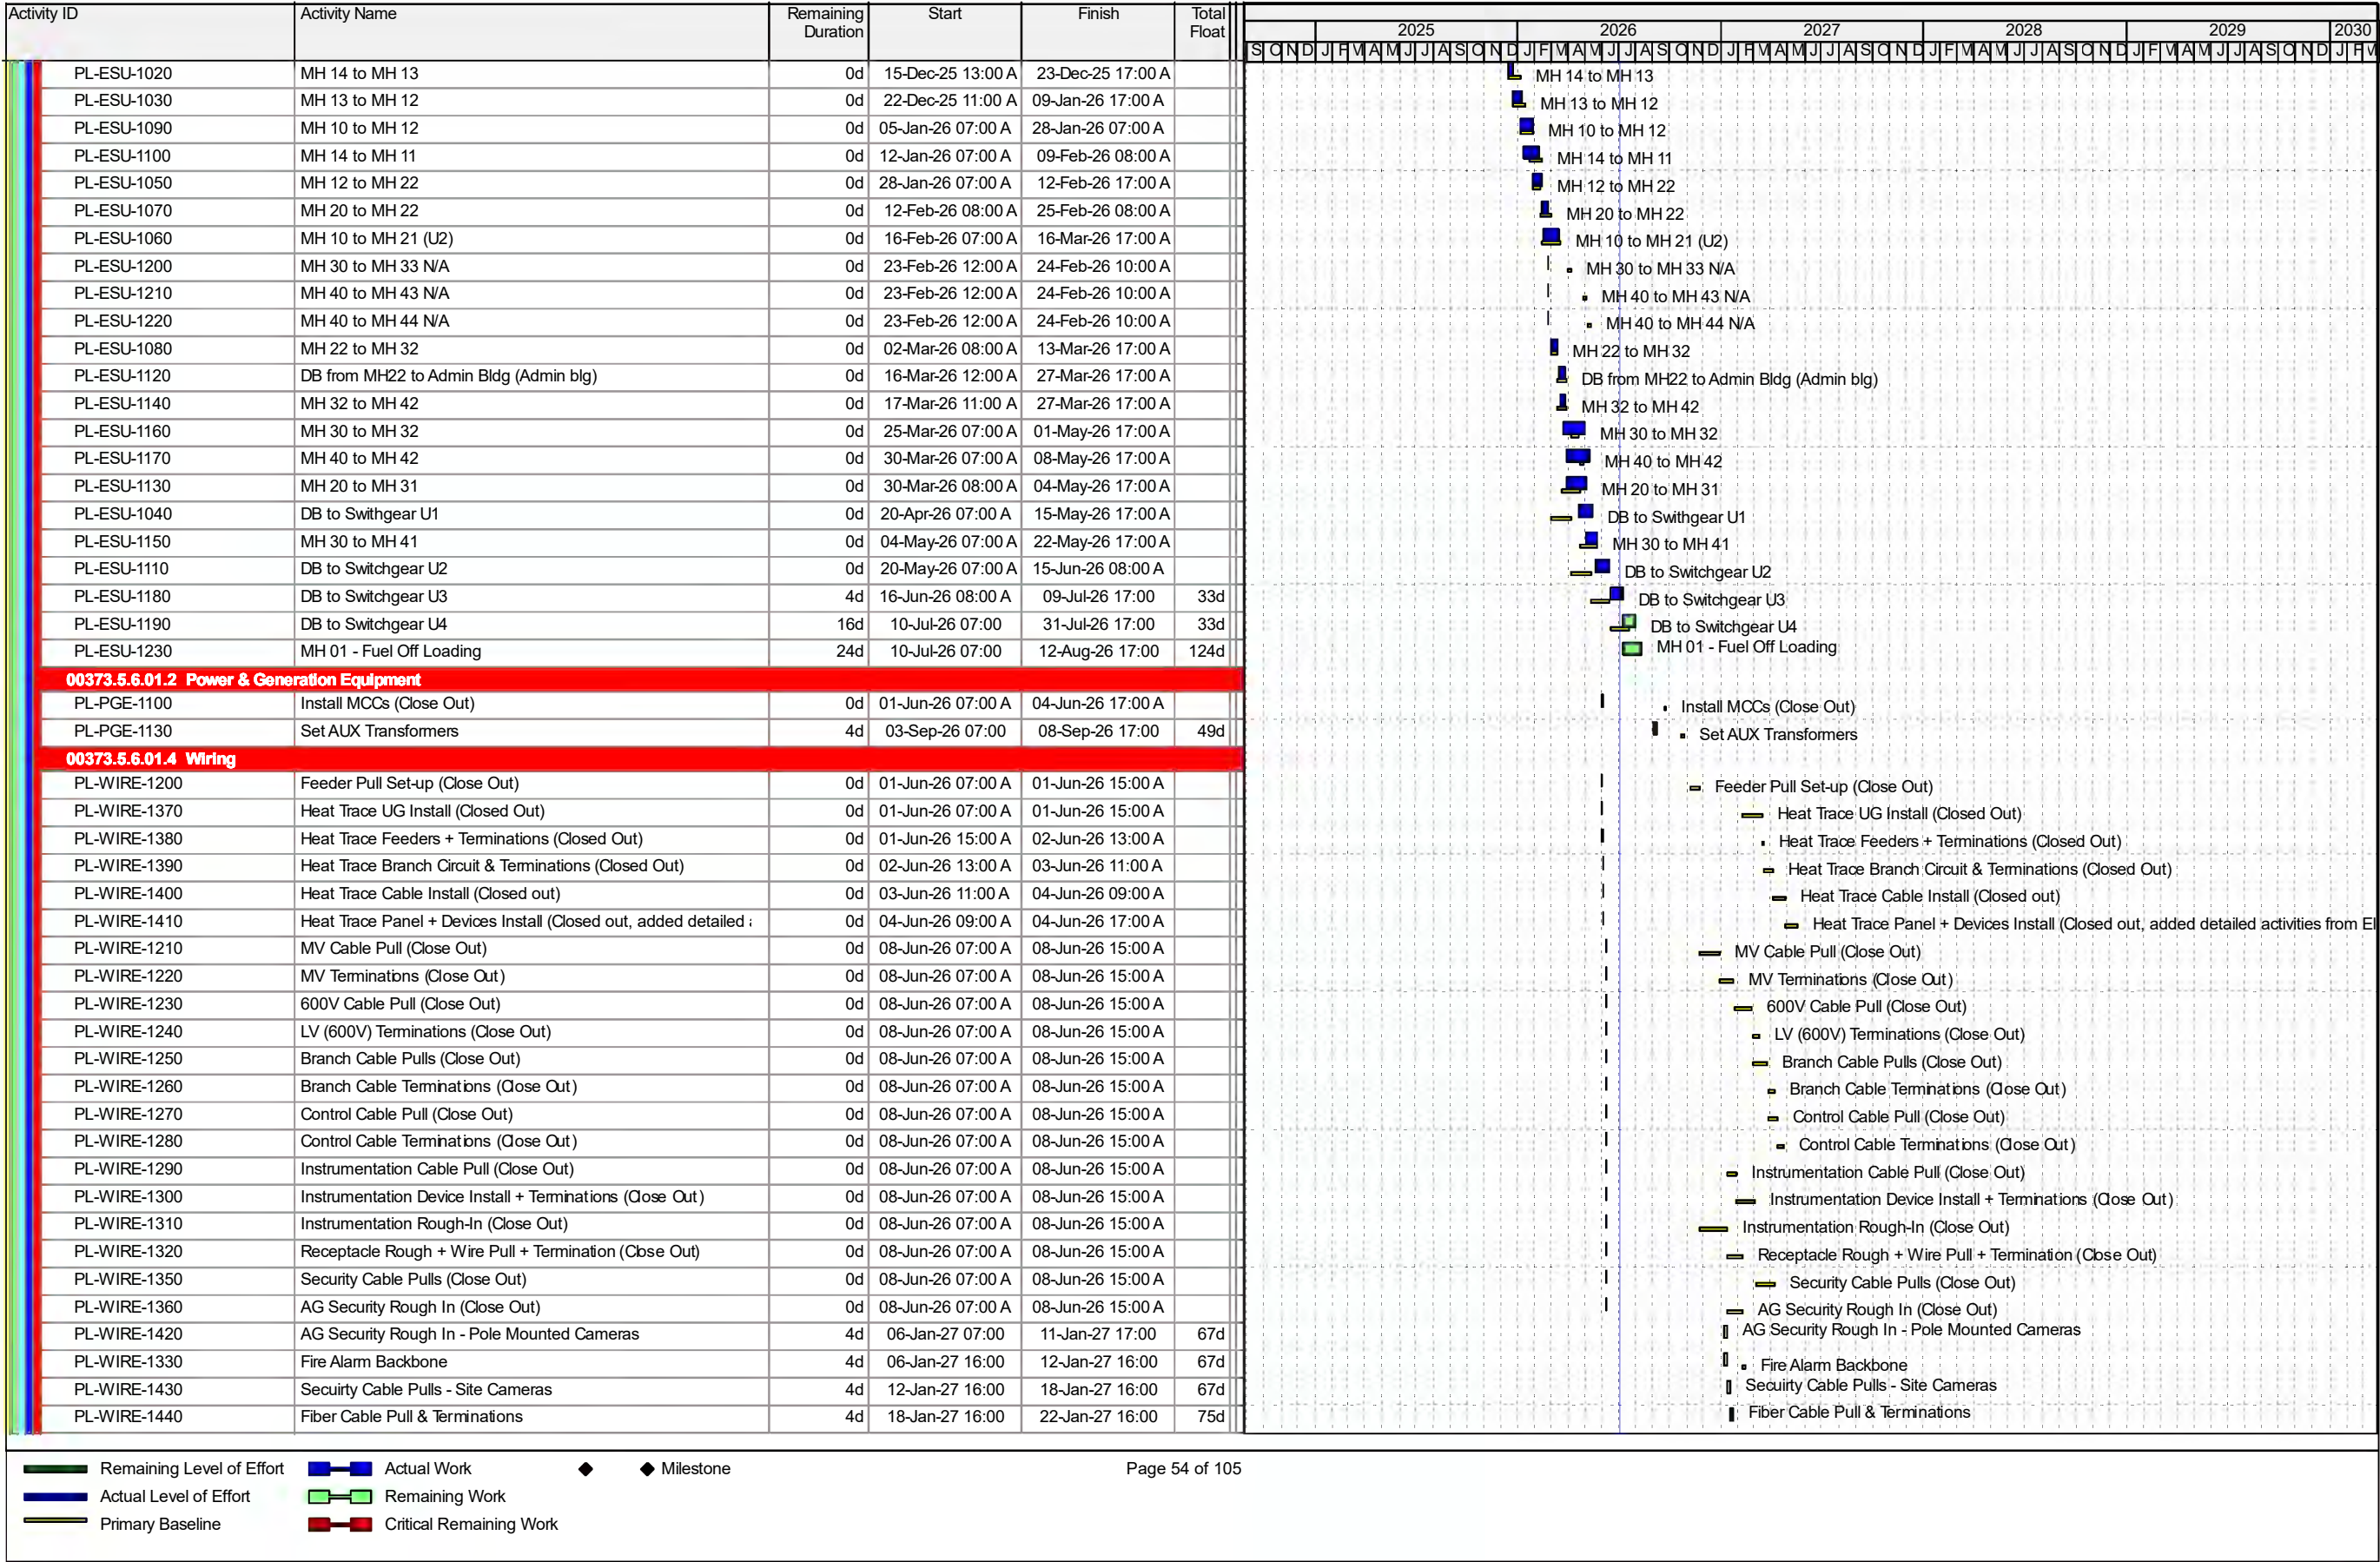

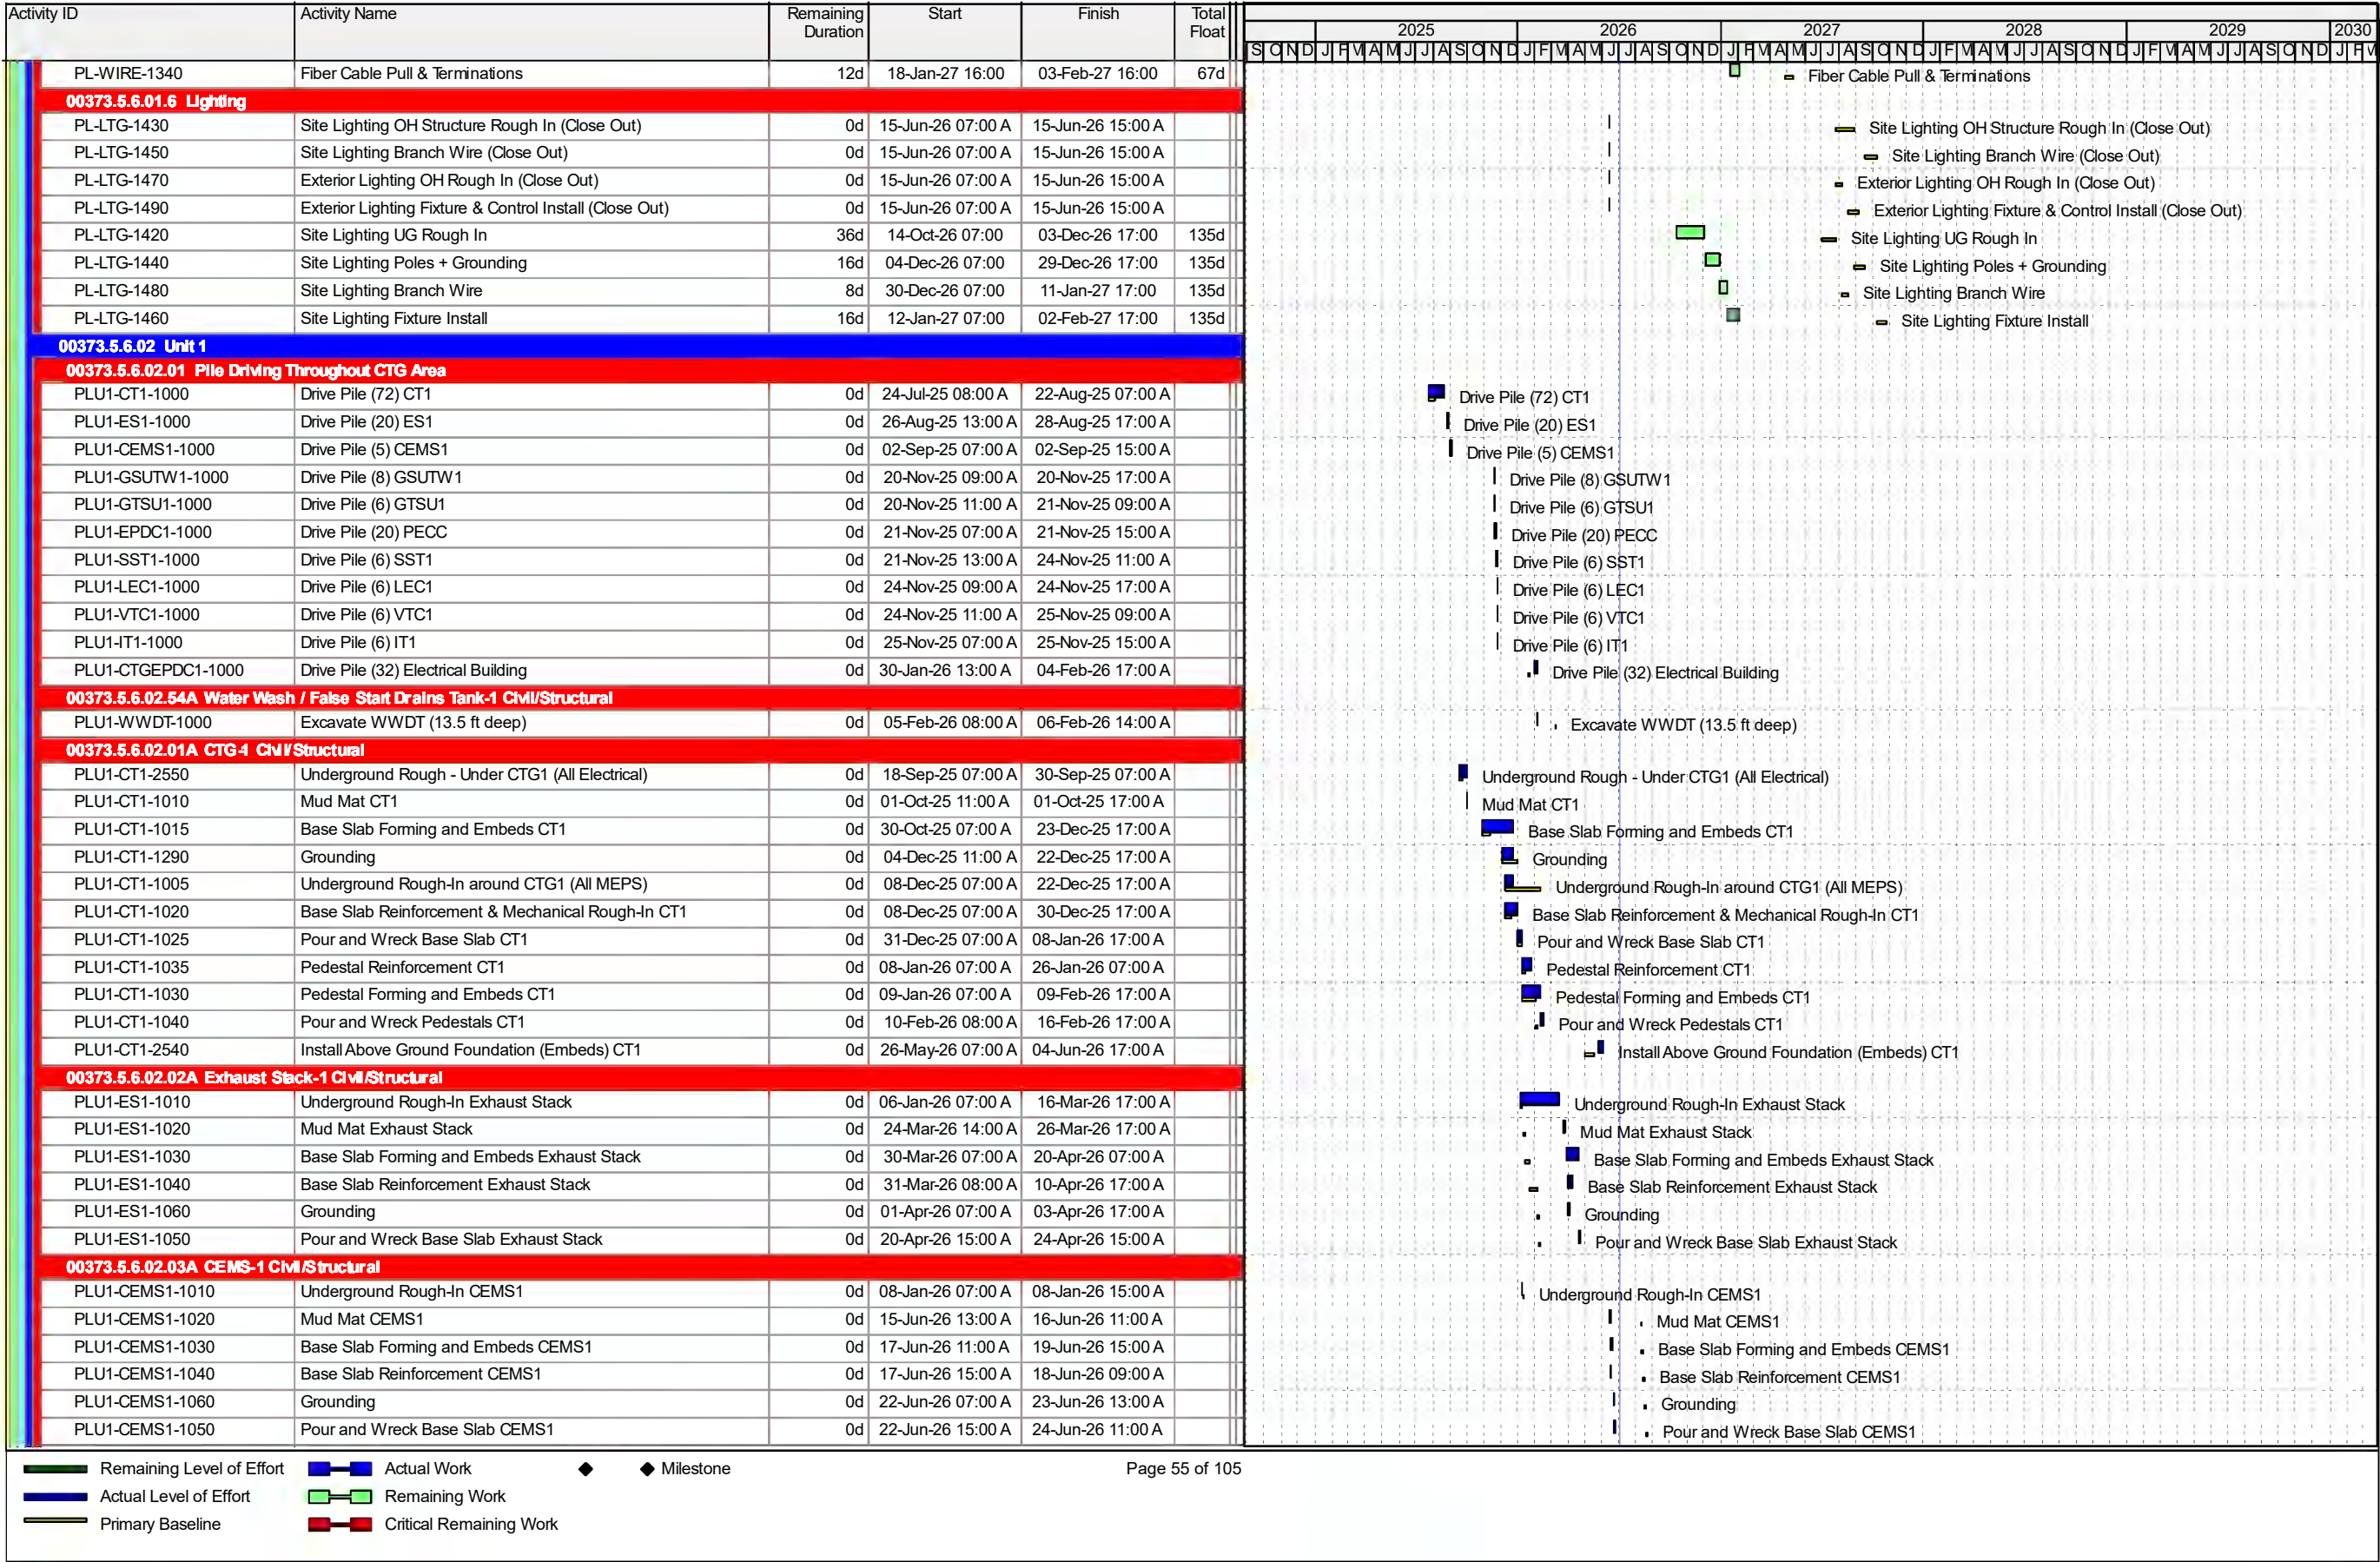


[illegible]

[illegible]


[illegible]

[illegible]


[illegible]

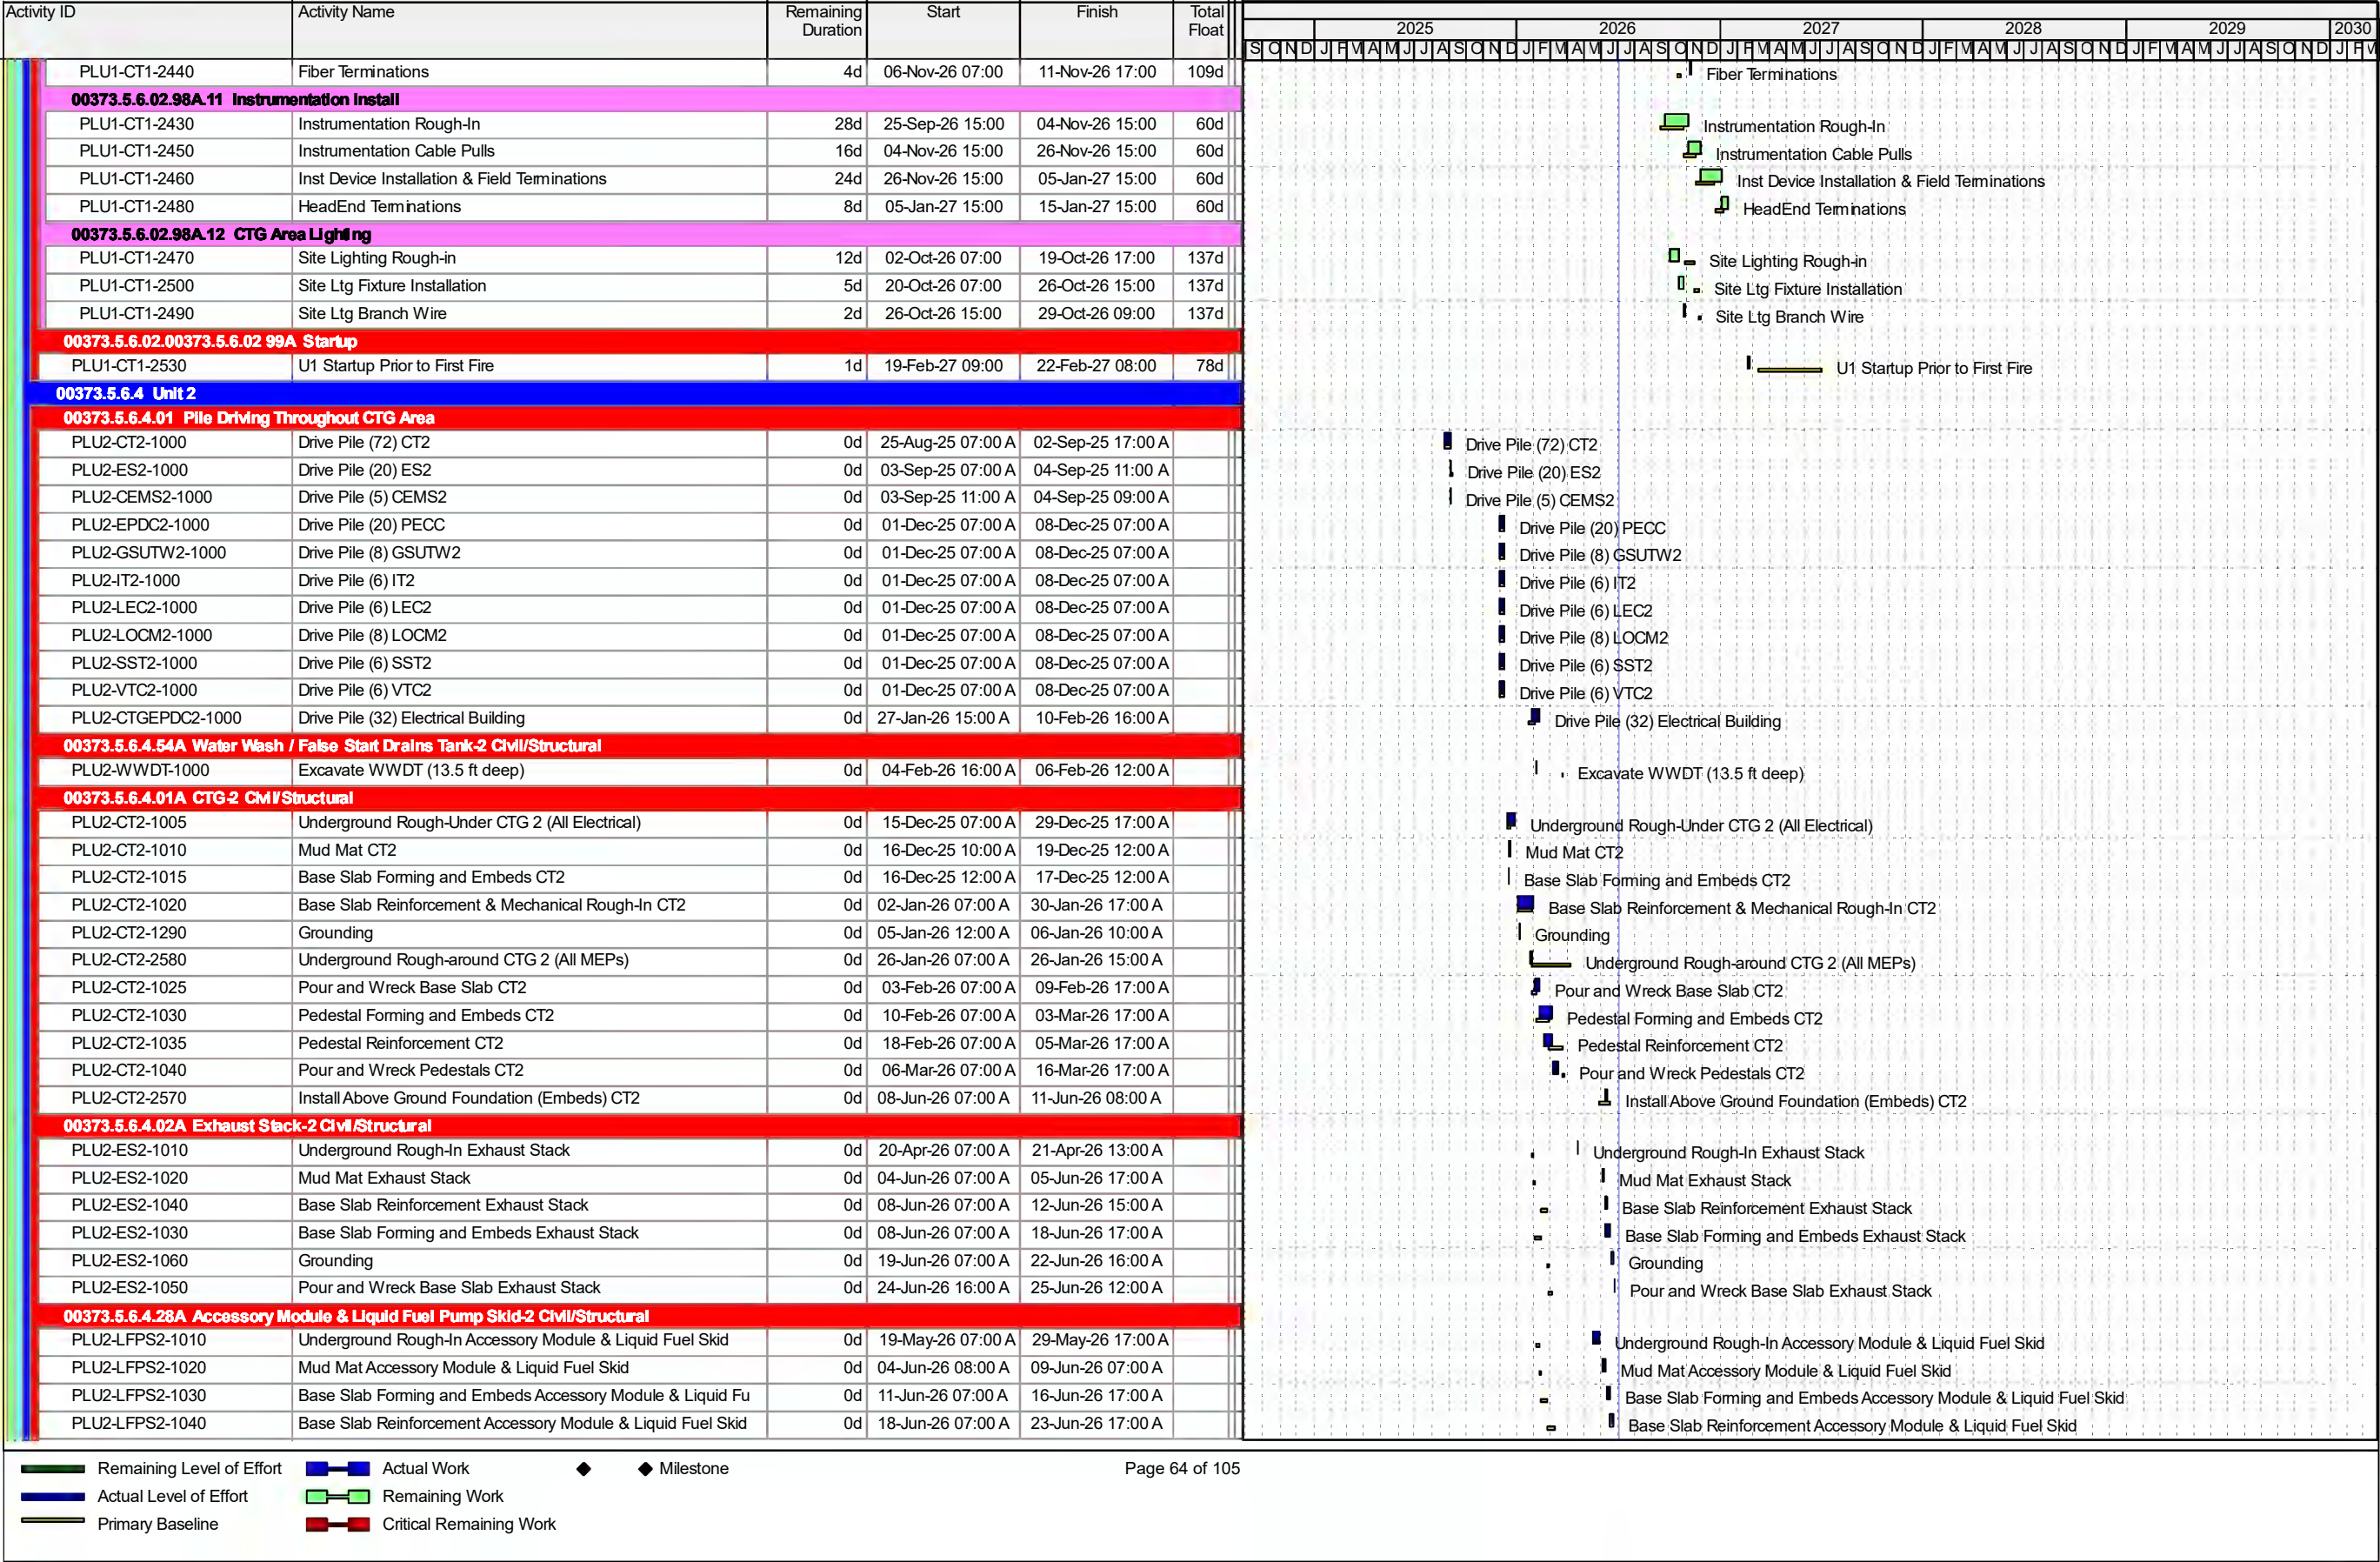

Page 64 of 105

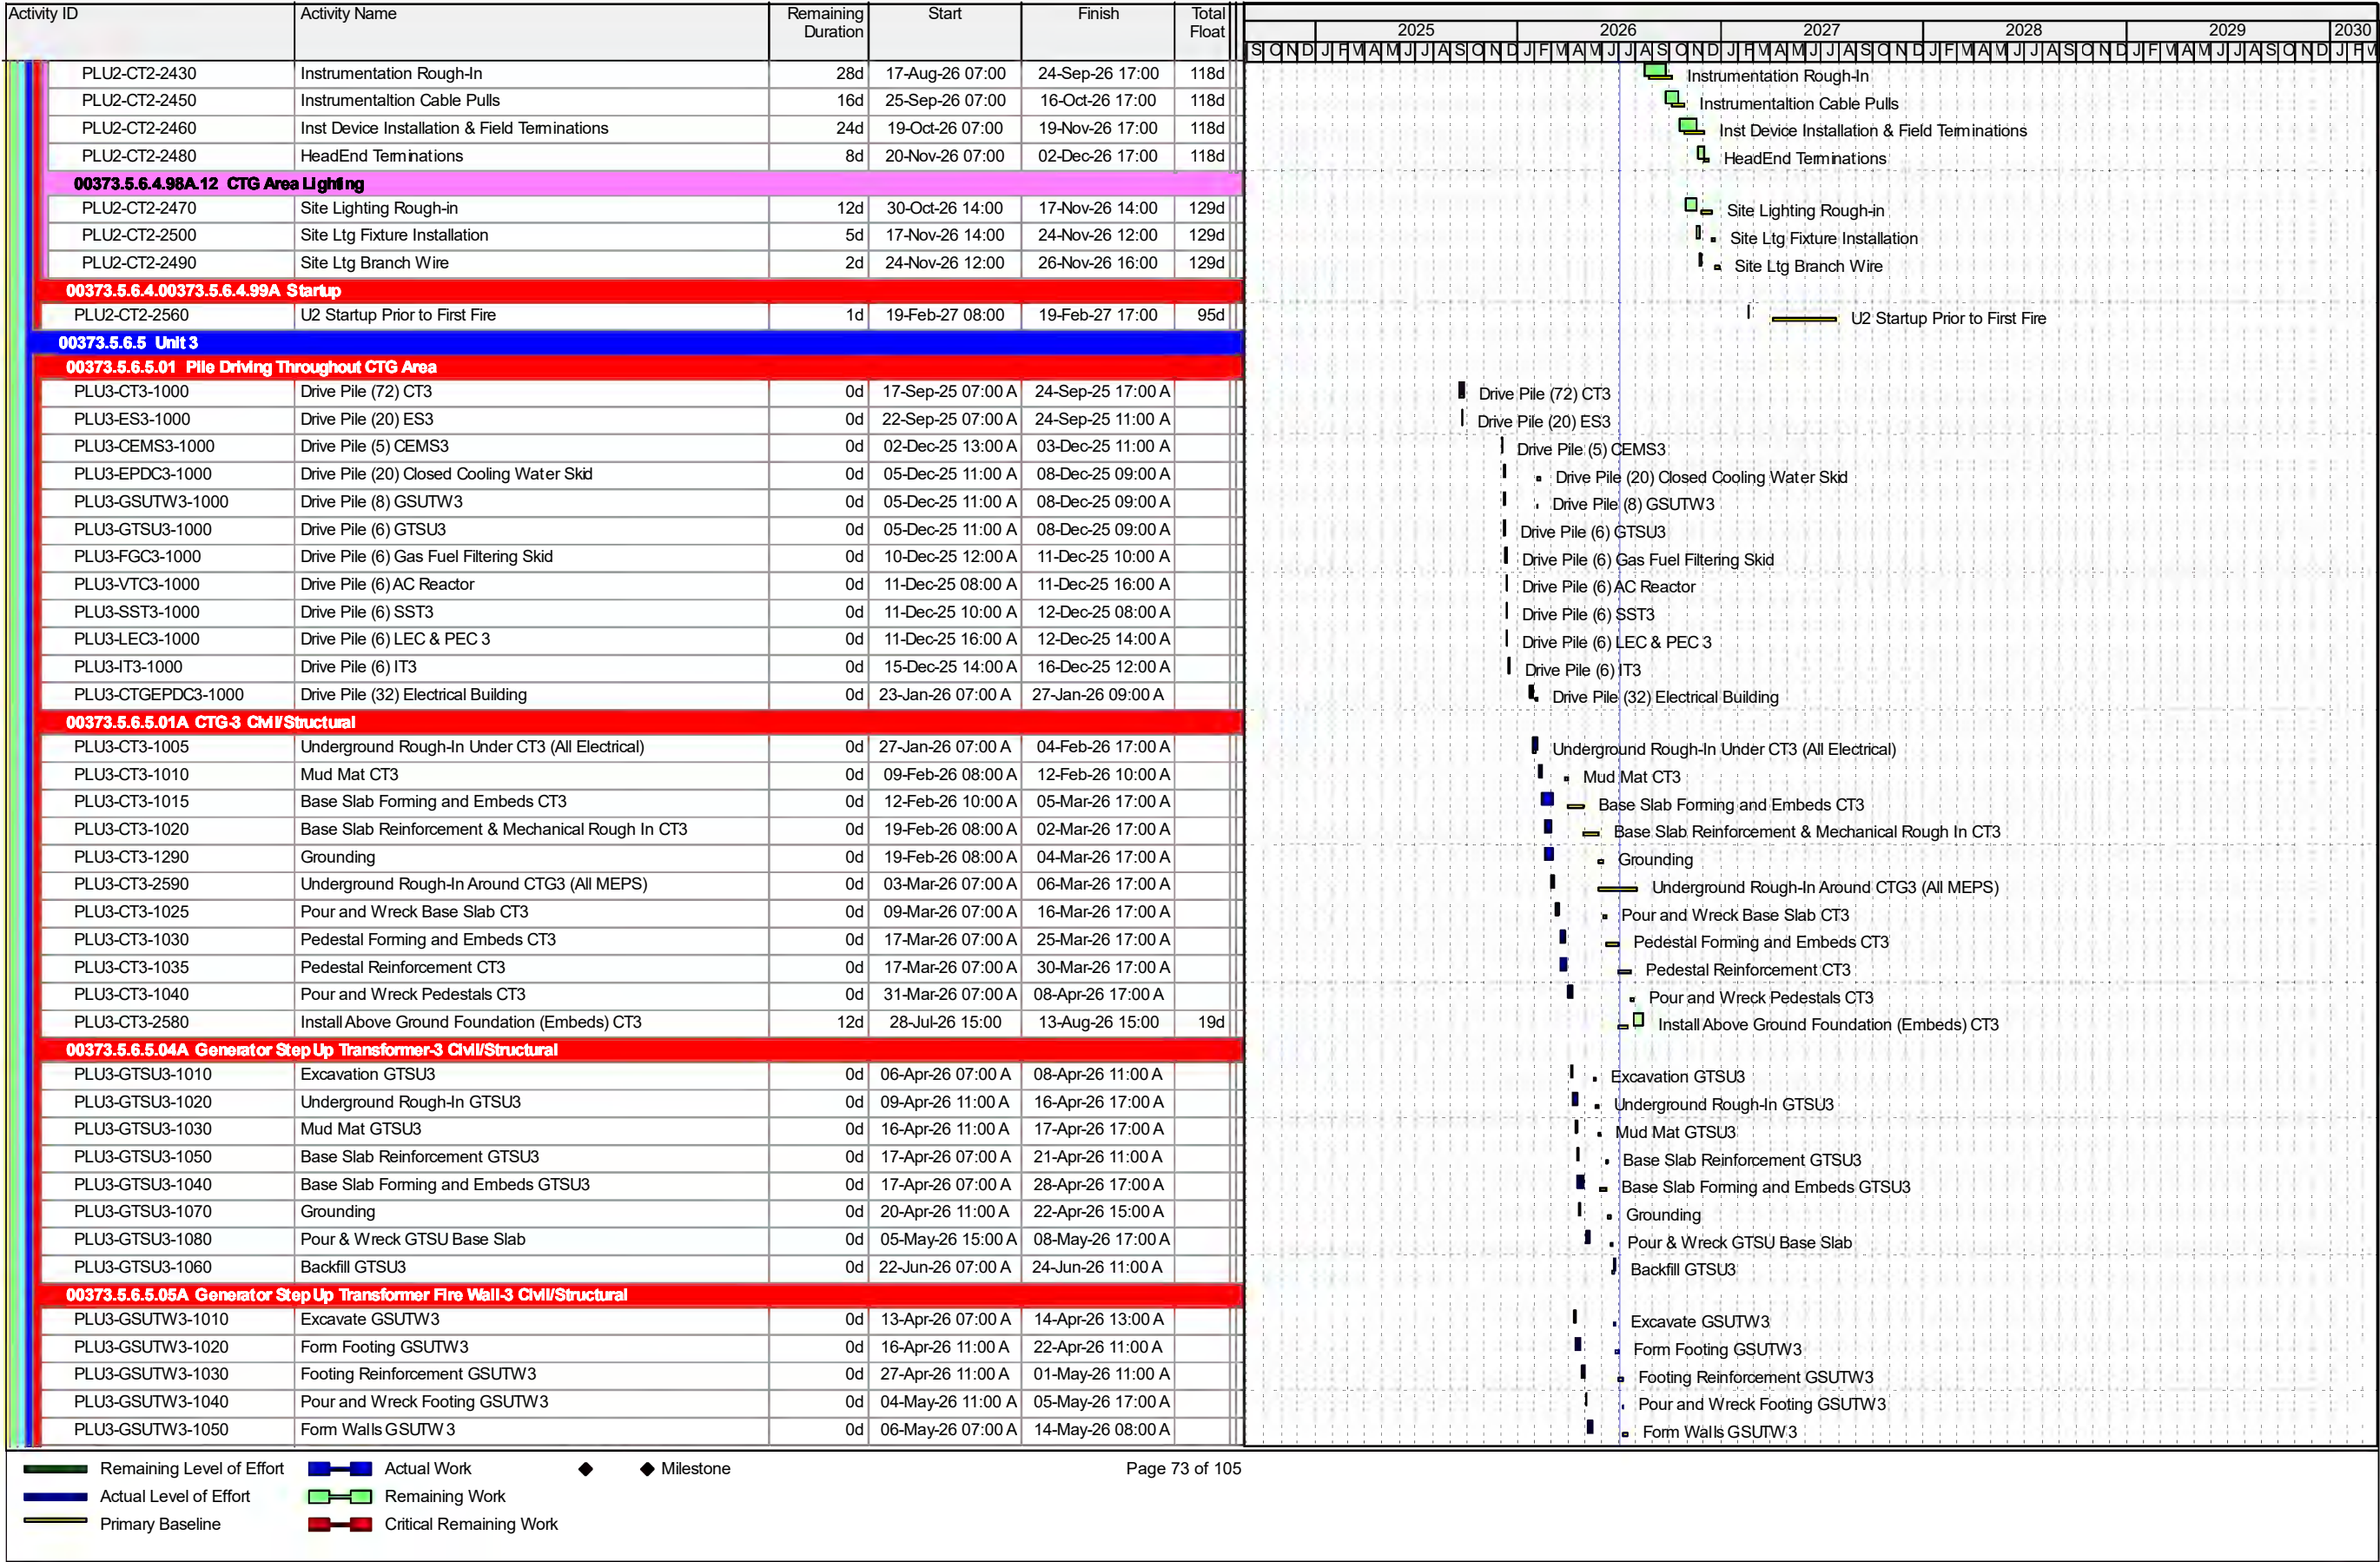


[illegible]

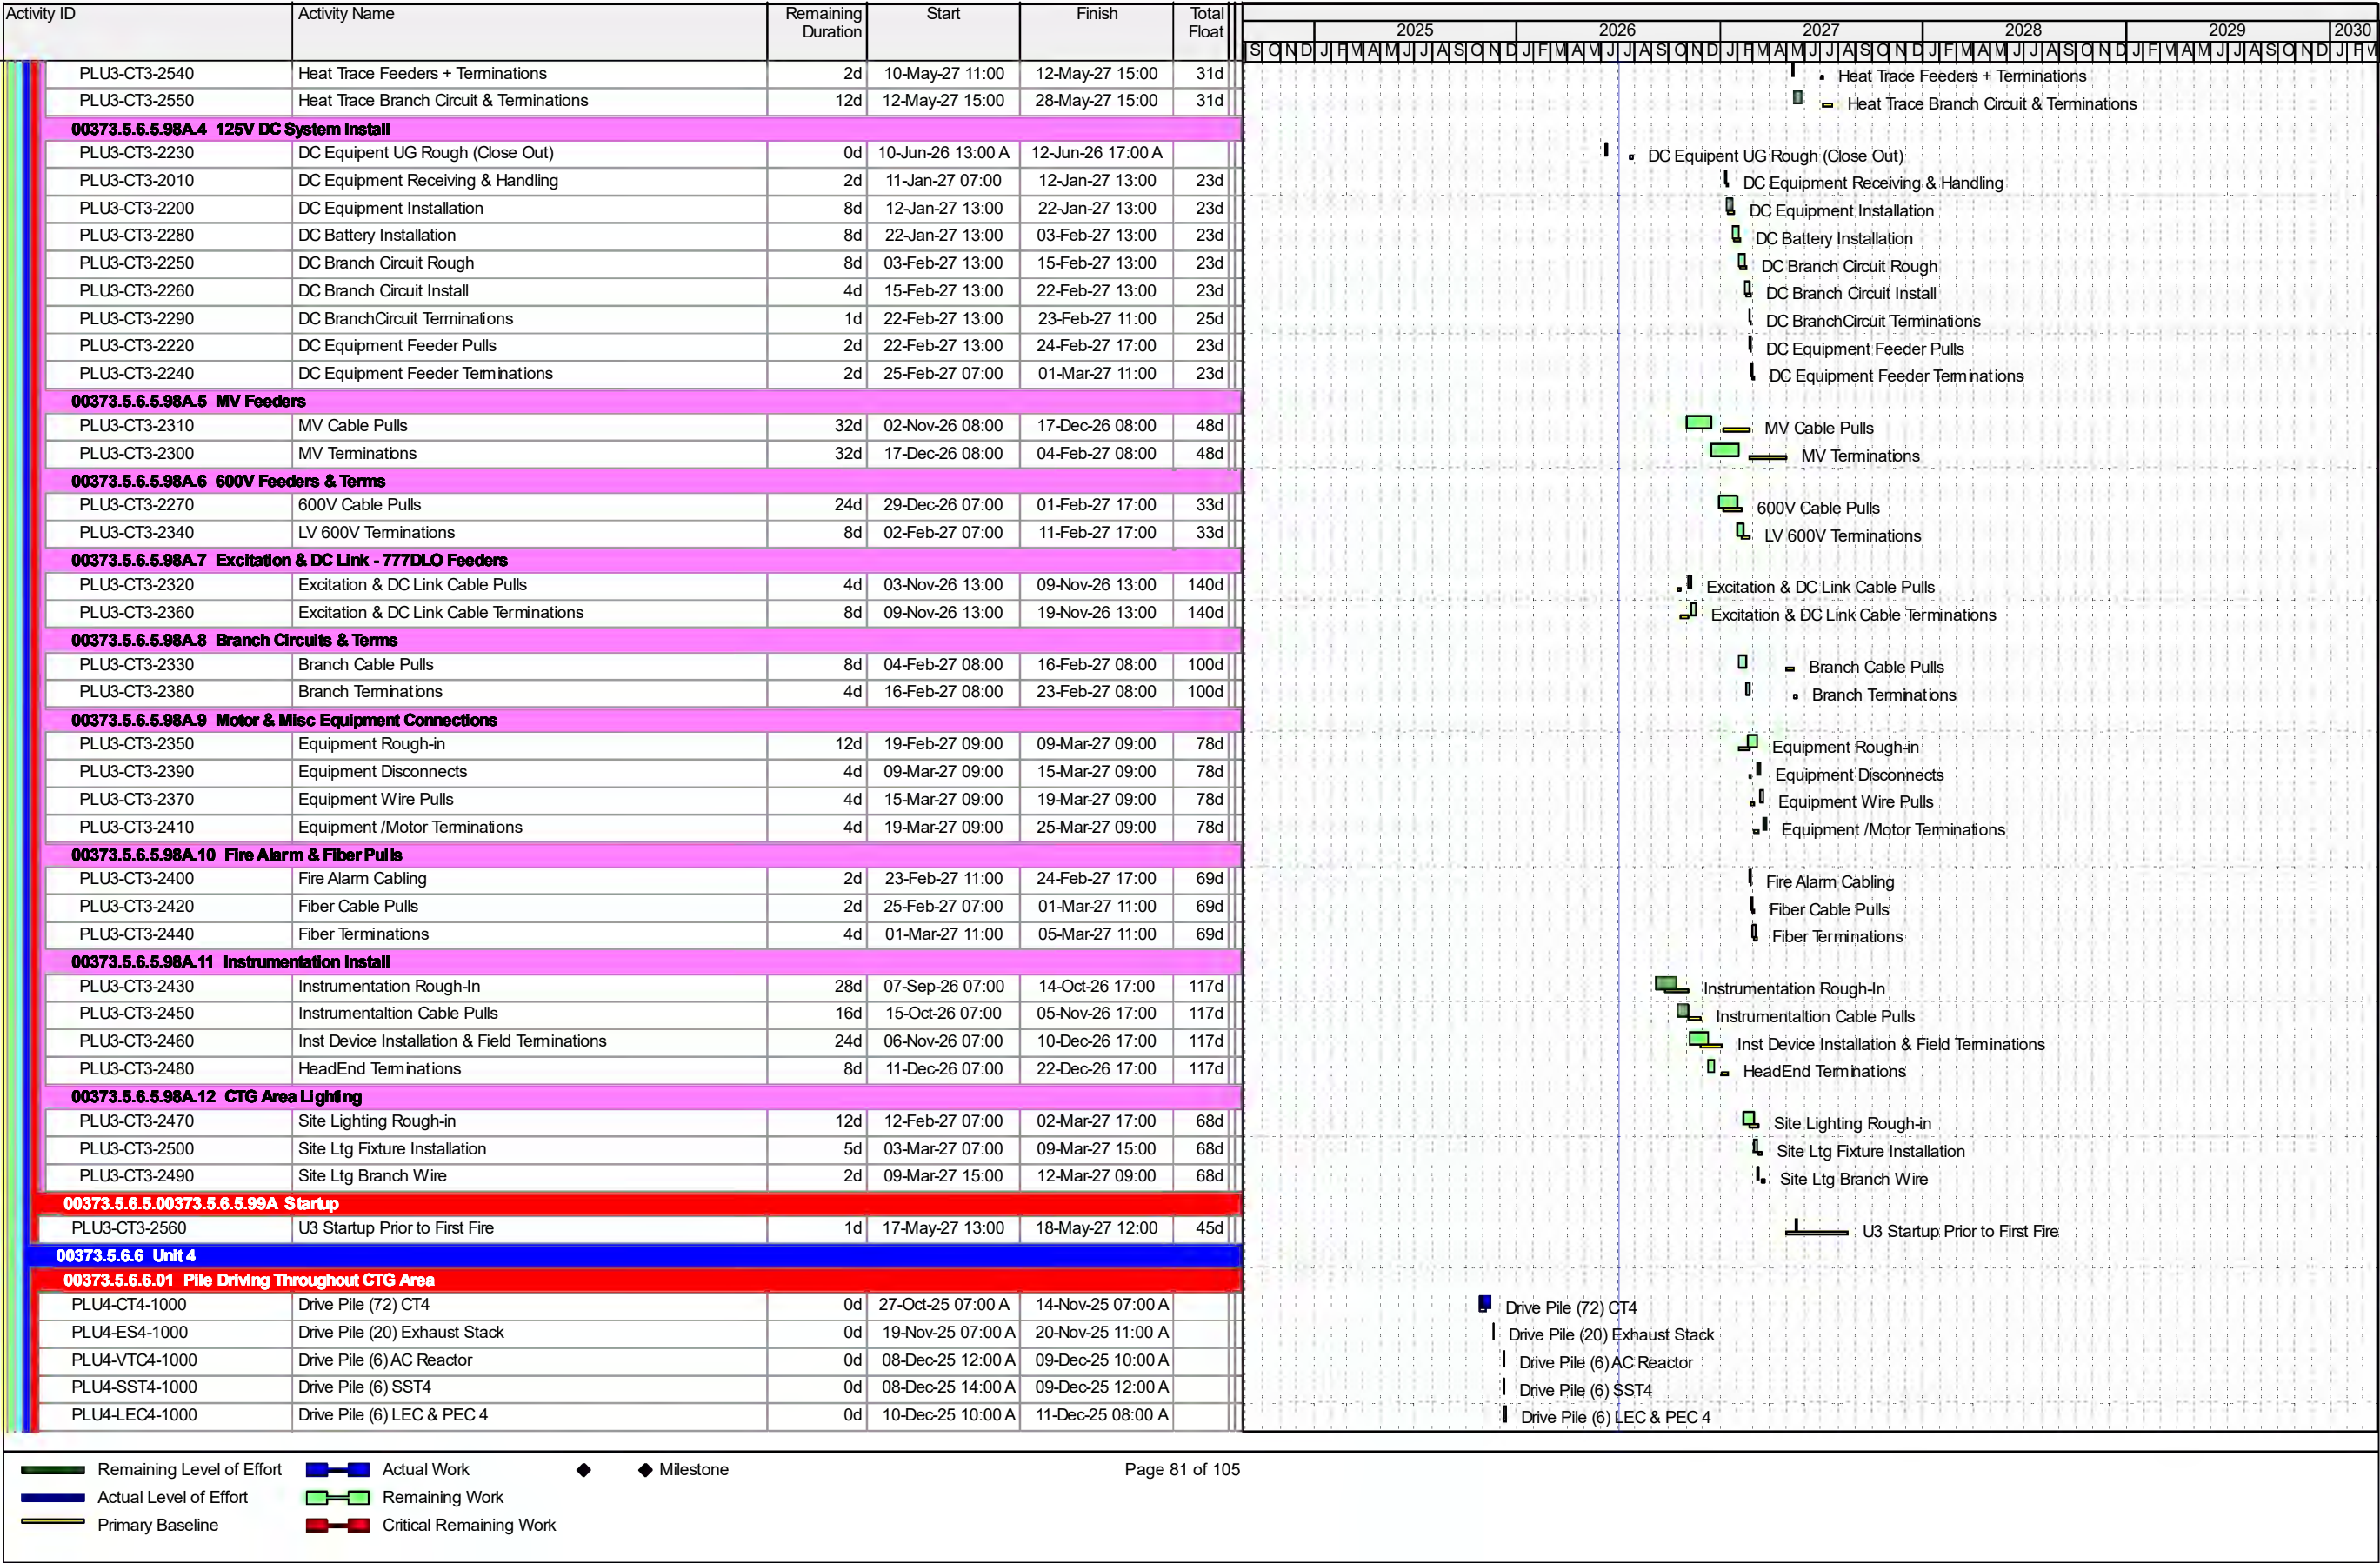

Page 81 of 105

[illegible]

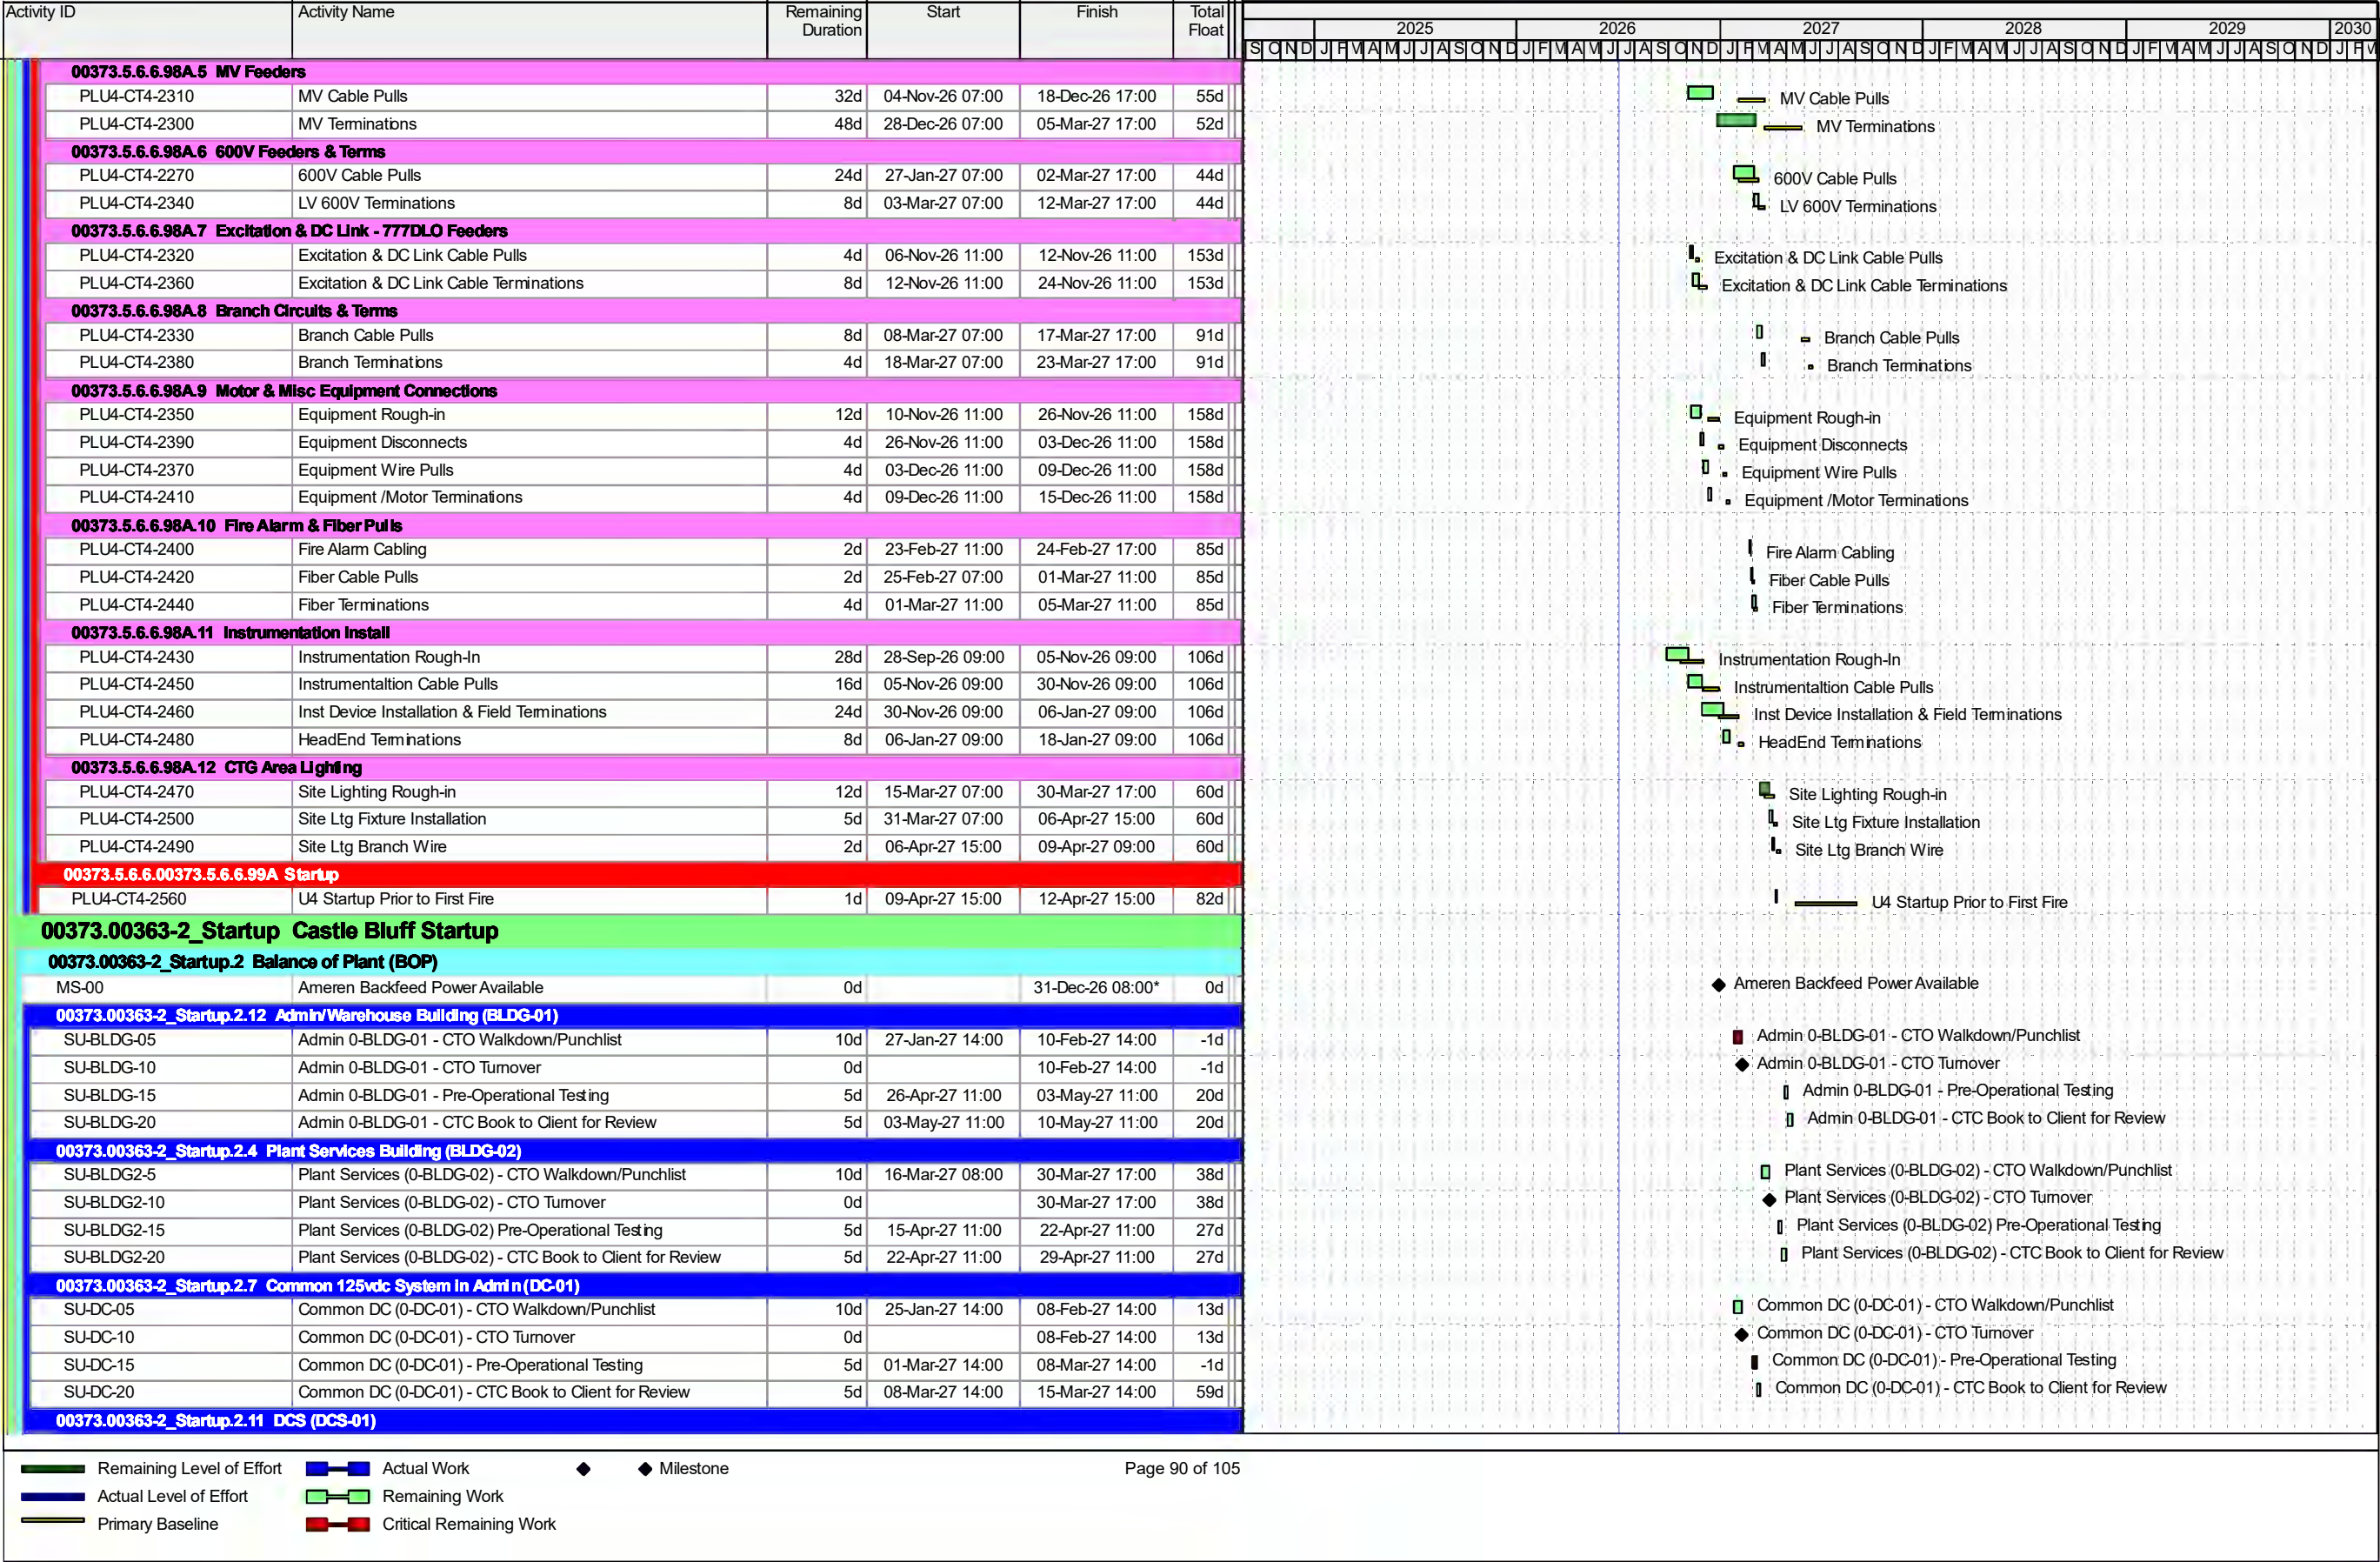

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						S	O	N	D	J	F	M	A	M	J	J	A
	SU1-CCW-40	Closed Cooling - CTO Walkdown/Punchlist	10d	22-Dec-26 08:00	06-Jan-27 17:00	76d											
	SU1-CCW-50	Closed Cooling - CTO Turnover	0d		06-Jan-27 17:00	76d											
	SU1-CCW-60	Closed Cooling - Pre-Operational Testing	6d	03-May-27 11:00	10-May-27 17:30	-4d											
	SU1-CCW-70	Closed Cooling - CTC Book to Client for Review	5d	11-May-27 08:00	17-May-27 17:00	14d											
	SU1-CCW-80	Cooling Water Initial Op/Flush Common	5d	11-May-27 08:00	17-May-27 17:00	-4d											
	SU1-CCW-90	Cooling Water Initial Op/Flush U1	5d	18-May-27 08:00	24-May-27 17:00	-4d											
00373.00363-2_Startup.17.8 Continuous Emissions Monitoring System (CEMS-01)																	
	SU1-CEMS-30	CEMS - CTO Walkdown/Punchlist	10d	22-Dec-26 08:00	06-Jan-27 17:00	96d											
	SU1-CEMS-40	CEMS - CTO Turnover	0d		06-Jan-27 17:00	96d											
	SU1-CEMS-50	CEMS - Pre-Operational Testing	4d	09-Apr-27 11:00	15-Apr-27 11:00	33d											
	SU1-CEMS-60	CEMS - CTC Book to Client for Review	5d	15-Apr-27 11:00	22-Apr-27 11:00	32d											
00373.00363-2_Startup.17.7 Compressed Air System (CAS-01)																	
	SU1-CAS-30	Compressed Air - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	41d											
	SU1-CAS-40	Compressed Air - CTO Turnover	0d		01-Mar-27 17:00	41d											
	SU1-CAS-50	Compressed Air - Pre-Operational Testing	4d	09-Apr-27 11:00	15-Apr-27 11:00	13d											
	SU1-CAS-60	Compressed Air - CTC Book to Client for Review	5d	15-Apr-27 11:00	22-Apr-27 11:00	32d											
	SU1-CAS-70	Compressed Air - Air Blows	5d	15-Apr-27 11:00	22-Apr-27 11:00	39d											
00373.00363-2_Startup.17.2 Compressed Water Wash (CWW-01)																	
	SU1-CWW-5	Water Wash (1-CWW-01) - CTO Walkdown/Punchlist	10d	22-Dec-26 08:00	06-Jan-27 17:00	72d											
	SU1-CWW-10	Water Wash (1-CWW-01) - CTO Turnover	0d		06-Jan-27 17:00	72d											
	SU1-CWW-15	Water Wash (1-CWW-01) - Pre-Operational Testing	4d	27-Apr-27 11:00	03-May-27 11:00	-4d											
	SU1-CWW-20	Water Wash (1-CWW-01) - CTC Book to Client for Review	5d	03-May-27 11:00	10-May-27 11:00	20d											
00373.00363-2_Startup.17.10 Demin Water (DEM-01)																	
	SU1-DEM-30	Demin Water - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	56d											
	SU1-DEM-40	Demin Water - CTO Turnover	0d		01-Mar-27 17:00	56d											
	SU1-DEM-50	Demin Water - Pre-Operational Testing	8d	15-Apr-27 11:00	27-Apr-27 11:00	25d											
	SU1-DEM-60	Demin Water - CTC Book to Client for Review	5d	27-Apr-27 11:00	04-May-27 11:00	24d											
	SU1-DEM-80	Demin Water - Flush	5d	27-Apr-27 1													

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
SU2-UPS-15	UPS - Pre-Operational Testing	4d	19-Mar-27 11:00	25-Mar-27 11:00	18d
SU2-UPS-20	UPS - CTC Book to Client for Review	5d	25-Mar-27 11:00	02-Apr-27 11:00	61d
00373.00363-2_Startup.36.15 Fuel Oil (FOS-01)					
SU2-FOS-5	Fuel Oil - CTO Walkdown/Punchlist	10d	12-Nov-26 08:00	25-Nov-26 17:00	139d
SU2-FOS-10	Fuel Oil - CTO Turnover	0d		25-Nov-26 17:00	139d
SU2-FOS-15	Fuel Oil - Pre-Operational Testing	4d	10-Jun-27 17:00	16-Jun-27 17:00	5d
SU2-FOS-20	Fuel Oil - CTC Book to Client for Review	5d	17-Jun-27 08:00	24-Jun-27 17:00	4d
SU2-FOS-25	Flush Fuel Oil Supply	5d	17-Jun-27 08:00	24-Jun-27 17:00	4d
00373.00363-2_Startup.36.3 Carbon Dioxide (CAR-01)					
SU2-CAR-5	Carbon Dioxide - CTO Walkdown/Punchlist	10d	23-Dec-26 10:00	08-Jan-27 10:00	110d
SU2-CAR-10	Carbon Dioxide - CTO Turnover	0d		08-Jan-27 10:00	110d
SU2-CAR-15	Carbon Dioxide - Pre-Operational Testing	4d	12-Apr-27 11:00	16-Apr-27 11:00	48d
SU2-CAR-20	Carbon Dioxide - CTC Book to Client for Review	5d	16-Apr-27 11:00	23-Apr-27 11:00	46d
00373.00363-2_Startup.36.5 Closed Cooling (CCW-01)					
SU2-CCW-5	Closed Cooling - CTO Walkdown/Punchlist	10d	15-Jan-27 08:00	29-Jan-27 17:00	96d
SU2-CCW-10	Closed Cooling - CTO Turnover	0d		29-Jan-27 17:00	96d
SU2-CCW-15	Closed Cooling - Pre-Operational Testing	4d	10-May-27 11:00	14-May-27 11:00	28d
SU2-CCW-20	Closed Cooling - CTC Book to Client for Review	5d	14-May-27 11:00	21-May-27 11:00	26d
SU2-CCW-25	Cooling Water Initial Op/Flush Common (Nb CCW scheulde fraget for BOP on	5d	14-May-27 11:00	21-May-27 11:00	231d
SU2-CCW-30	Cooling Water Initial Op/Flush U1	5d	21-May-27 11:00	28-May-27 11:00	231d
00373.00363-2_Startup.36.8 Continuous Emissions Monitoring System (CEMS-01)					
SU2-CEMS-5	CEMS - CTO Walkdown/Punchlist	10d	15-Jan-27 08:00	29-Jan-27 17:00	96d
SU2-CEMS-10	CEMS - CTO Turnover	0d		29-Jan-27 17:00	96d
SU2-CEMS-15	CEMS - Pre-Operational Testing	4d	06-Apr-27 11:00	12-Apr-27 11:00	52d
SU2-CEMS-20	CEMS - CTC Book to Client for Review	5d	12-Apr-27 11:00	19-Apr-27 11:00	50d
00373.00363-2_Startup.36.7 Compressed Air System (CAS-01)					
SU2-CAS-5	Compressed Air - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	76d
SU2-CAS-10	Compressed Air - CTO Turnover	0d		01-Mar-27 17:00	76d
SU2-CAS-15	Compressed Air - Pre-Operational Testing	4d	22-Apr-27 11:00	28-Apr-27 11:00	40d
SU2-CAS-20	Compressed Air - CTC Book to Client for Review	5d	28-Apr-27 11:00	05-May-27 11:00	38d
00373.00363-2_Startup.36.2 Compressed Water Wash (CWW-01)					
SU2-CWW-5	Water Wash - CTO Walkdown/Punchlist	10d	15-Jan-27 08:00	29-Jan-27 17:00	96d
SU2-CWW-10	Water Wash - CTO Turnover	0d		29-Jan-27 17:00	96d
SU2-CWW-15	Water Wash - Pre-Operational Testing	4d	10-May-27 11:00	14-May-27 11:00	28d
SU2-CWW-20	Water Wash - CTC Book to Client for Review	5d	14-May-27 11:00	21-May-27 11:00	26d
00373.00363-2_Startup.36.10 Demin Water (DEM-01)					
SU2-DEM-5	Demin Water - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	76d
SU2-DEM-10	Demin Water - CTO Turnover	0d		01-Mar-27 17:00	76d
SU2-DEM-15	Demin Water - Pre-Operational Testing	4d	04-May-27 11:00	10-May-27 11:00	32d
SU2-DEM-20	Demin Water - CTC Book to Client for Review	5d	10-May-27 11:00	17-May-27 11:00	30d
00373.00363-2_Startup.36.13 Fire Protection (FPS-01)					
SU2-FPS-5	Fire Protection - CTO Walkdown/Punchlist	10d	05-Mar-27 11:00	19-Mar-27 11:00	58d
SU2-FPS-10	Fire Protection - CTO Turnover	0d		19-Mar-27 11:00	58d
SU2-FPS-15	Fire Protection - Pre-Operational Testing	4d	21-May-27 17:00	27-May-27 17:00	15d
SU2-FPS-20	Fire Protection - CTC Book to Client for Review	5d	28-May-27 08:00	04-Jun-27 17:00	17d
00373.00363-2_Startup.36.11 Gas Fuel System (GFS-01)					
SU2-GFS-5	GFS - CTO Walkdown/Punchlist	10d	12-Nov-26 08:00	25-Nov-26 17:00	139d
SU2-GFS-10	GFS - CTO Turnover	0d		25-Nov-26 17:00	139d
SU2-GFS-15	GFS - Pre-Operational Testing	4d	27-May-27 15:30	02-Jun-27 15:30	15d
SU2-GFS-20	GFS - CTC Book to Client for Review	5d	02-Jun-27 15:30	09-Jun-27 15:30	14d
SU2-GFS-25	Gas Blow Common Supply Line	5d	02-Jun-27 15:30	09-Jun-27 15:30	218d

Remaining Level of Effort

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Milestone

Page 96 of 105

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
SU2-GFS-30	Common Gas Line Blow Restore/Check Out	5d	09-Jun-27 15:30	16-Jun-27 15:30	218d
00373.00363-2_Startup.36.14 Starter Package (LCI-01)					
SU2-LCI-5	Starter Package - CTO Walkdown/Punchlist	10d	06-Nov-26 08:00	20-Nov-26 17:00	138d
SU2-LCI-10	Starter Package - CTO Turnover	0d		20-Nov-26 17:00	138d
SU2-LCI-15	Starter Package - Pre-Operational Testing	4d	10-May-27 11:00	14-May-27 11:00	24d
SU2-LCI-20	Starter Package - CTC Book to Client for Review	5d	14-May-27 11:00	21-May-27 11:00	26d
00373.00363-2_Startup.36.18 Lighting System (LGT-01)					
SU2-LGT-5	Lighting - CTO Walkdown/Punchlist	10d	27-Nov-26 08:00	10-Dec-26 17:00	129d
SU2-LGT-10	Lighting - CTO Turnover	0d		10-Dec-26 17:00	129d
SU2-LGT-15	Lighting - Pre-Operational Testing	4d	10-May-27 11:00	14-May-27 11:00	28d
SU2-LGT-20	Lighting - CTC Book to Client for Review	5d	14-May-27 11:00	21-May-27 11:00	26d
00373.00363-2_Startup.36.20 Low Voltage Switchgear & 01-SSE-MCC-004 BOP MCC-A (1-LSG-01)					
SU2-LSG-5	LV Switchgear - CTO Walkdown/Punchlist	10d	31-Dec-26 08:00	14-Jan-27 17:00	20d
SU2-LSG-10	LV Switchgear - CTO Turnover	0d		14-Jan-27 17:00	20d
SU2-LSG-15	LV Switchgear - Pre-Operational Testing	4d	16-Feb-27 14:00	22-Feb-27 14:00	-1d
SU2-LSG-20	LV Switchgear - CTC Book to Client for Review	5d	22-Feb-27 14:00	01-Mar-27 14:00	84d
00373.00363-2_Startup.36.19 Medium Voltage Switchgear (1-MSG-01)					
SU2-MSG-5	MV Switchgear - CTO Walkdown/Punchlist	10d	12-Nov-26 08:00	25-Nov-26 17:00	93d
SU2-MSG-10	MV Switchgear - CTO Turnover	0d		25-Nov-26 17:00	93d
SU2-MSG-15	MV Switchgear - Pre-Operational Testing	4d	19-Mar-27 11:00	25-Mar-27 11:00	18d
SU2-MSG-20	MV Switchgear - CTC Book to Client for Review	5d	25-Mar-27 11:00	02-Apr-27 11:00	61d
00373.00363-2_Startup.36.21 CTG Elec Enclosure 480v Power (MCC1-AC, MCC2-AC, MCC-1E-AC (PEECC-01)					
SU2-PEECC-5	PEECC - CTO Walkdown/Punchlist	10d	15-Jan-27 08:00	29-Jan-27 17:00	78d
SU2-PEECC-10	PEECC - CTO Turnover	0d		29-Jan-27 17:00	78d
SU2-PEECC-15	PEECC - Pre-Operational Testing	4d	27-Apr-27 11:00	03-May-27 11:00	19d
SU2-PEECC-20	PEECC - CTC Book to Client for Review	5d	03-May-27 11:00	10-May-27 11:00	35d
SU2-PEECC-30	Energize Unit 2 PEECC	5d	03-May-27 11:00	10-May-27 11:00	19d
00373.00363-2_Startup.36.23 Elec Enclosure 125/24vdc & 120 UPS (PEECC-02)					
SU2-PEECC2-5	PEECC-02 - CTO Walkdown/Punchlist	10d	15-Jan-27 08:00	29-Jan-27 17:00	88d
SU2-PEECC2-10	PEECC-02 - CTO Turnover	0d		29-Jan-27 17:00	88d
SU2-PEECC2-15	PEECC-02 - Pre-Operational Testing	4d	03-May-27 11:00	07-May-27 11:00	25d
SU2-PEECC2-20	PEECC-02 - CTC Book to Client for Review	5d	07-May-27 11:00	14-May-27 11:00	31d
00373.00363-2_Startup.36.22 Service Water System (SWS-01)					
SU2-SWS-5	Service Water - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	76d
SU2-SWS-10	Service Water - CTO Turnover	0d		01-Mar-27 17:00	76d
SU2-SWS-15	Service Water - Pre-Operational Testing	4d	12-May-27 15:30	18-May-27 15:30	26d
SU2-SWS-20	Service Water - CTC Book to Client for Review	5d	18-May-27 15:30	25-May-27 15:30	24d
00373.00363-2_Startup.36.24 Turbine Cooling & Sealing Air (TCS-01)					
SU2-TCS-5	Turbine Cooling - CTO Walkdown/Punchlist	10d	03-Dec-26 08:00	16-Dec-26 17:00	121d
SU2-TCS-10	Turbine Cooling - CTO Turnover	0d		16-Dec-26 17:00	121d
SU2-TCS-15	Turbine Cooling - Pre-Operational Testing	4d	14-May-27 11:00	20-May-27 11:00	20d
SU2-TCS-20	Turbine Cooling - CTC Book to Client for Review	5d	20-May-27 11:00	27-May-27 11:00	22d
00373.00363-2_Startup.36.25 Turbine Air Inlet (TAI-01)					
SU2-TAI-5	Turbine Air - CTO Walkdown/Punchlist	10d	03-Dec-26 08:00	16-Dec-26 17:00	121d
SU2-TAI-10	Turbine Air - CTO Turnover	0d		16-Dec-26 17:00	121d
SU2-TAI-15	Turbine Air - Pre-Operational Testing	4d	10-May-27 11:00	14-May-27 11:00	24d
SU2-TAI-20	Turbine Air - CTC Book to Client for Review	5d	14-May-27 11:00	21-May-27 11:00	26d
00373.00363-2_Startup.36.26 Turbine Controls & Instrumentation Devices (TCI-01)					
SU2-TCI-5	Turbine Controls - CTO Walkdown/Punchlist	10d	03-Dec-26 08:00	16-Dec-26 17:00	125d
SU2-TCI-10	Turbine Controls - CTO Turnover	0d		16-Dec-26 17:00	125d
SU2-TCI-15	Turbine Controls - Pre-Operational Testing	4d	14-May-27 11:00	20-May-27 11:00	24d

Remaining Level of Effort

Actual Work

Actual Level of Effort

Primary Baseline

Milestone

Remaining Work

Critical Remaining Work

Page 97 of 105

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						S	O	N	D	J	F	M	A	M	J	J	A
	SU3-HC-170	U3 Full Speed No Load (FSNL) & Synchronize on Fuel Oil	1d	28-Jul-27 10:30	29-Jul-27 08:30	3d											
	SU3-HC-220	U3 First Fire Fuel Oil	0d	29-Jul-27 08:30		3d											
	SU3-HC-190	U3 Fuel Oil Tuning to Base Load	3d	29-Jul-27 08:30	03-Aug-27 08:30	3d											
	SU3-HC-200	U3 Base Load Checks on Fuel Oil	2d	03-Aug-27 08:30	05-Aug-27 08:30	3d											
	SU3-HC-210	U3 Fuel Oil Transfer	8d	05-Aug-27 08:30	17-Aug-27 08:30	3d											
00373.00363-2_Startup.6 Unit 4 CTG																	
	SU4-SST-30	Energize SST4	2d	12-May-27 11:00	14-May-27 11:00	23d											
	SU4-SST-40	Energize Unit 4 MSG & LSG Switchgear (Power Available)	1d	14-May-27 11:00	17-May-27 11:00	23d											
00373.00363-2_Startup.6.35 Station Service Transformer (1-SST-01)																	
	SU4-SST-5	SST - CTO Walkdown/Punchlist	10d	08-Mar-27 08:00	19-Mar-27 17:00	55d											
	SU4-SST-10	SST - CTO Turnover	0d		19-Mar-27 17:00	55d											
	SU4-SST-15	SST - Pre-Operational Testing	4d	06-May-27 11:00	12-May-27 11:00	24d											
	SU4-SST-20	SST - CTC Book to Client for Review	5d	12-May-27 11:00	19-May-27 11:00	50d											
00373.00363-2_Startup.6.4 Electrical Enclosure 125vdc (DC-01)																	
	SU4-DC-5	DC - CTO Walkdown/Punchlist	10d	15-Mar-27 08:00	29-Mar-27 17:00	43d											
	SU4-DC-10	DC - CTO Turnover	0d		29-Mar-27 17:00	43d											
	SU4-DC-15	480v Temp Power Charger	5d	19-Apr-27 11:00	26-Apr-27 11:00	24d											
	SU4-DC-20	DC - Pre-Operational Testing	4d	26-Apr-27 11:00	30-Apr-27 11:00	24d											
	SU4-DC-25	DC - CTC Book to Client for Review	5d	30-Apr-27 11:00	07-May-27 11:00	58d											
00373.00363-2_Startup.6.6 Electrical Enclosure UPS (UPS-01)																	
	SU4-UPS-5	UPS - CTO Walkdown/Punchlist	10d	15-Mar-27 08:00	29-Mar-27 17:00	46d											
	SU4-UPS-10	UPS - CTO Turnover	0d		29-Mar-27 17:00	46d											
	SU4-UPS-15	UPS - Pre-Operational Testing	4d	30-Apr-27 11:00	06-May-27 11:00	24d											
	SU4-UPS-20	UPS - CTC Book to Client for Review	5d	06-May-27 11:00	13-May-27 11:00	54d											
00373.00363-2_Startup.6.15 Fuel Oil (FOS-01)																	
	SU4-FOS-5	Fuel Oil - CTO Walkdown/Punchlist	10d	08-Mar-27 08:00	19-Mar-27 17:00	82d											
	SU4-FOS-10	Fuel Oil - CTO Turnover	0d		19-Mar-27 17:00	82d											
	SU4-FOS-15	Fuel Oil - Pre-Operational Testing	4d	10-Jun-27 17:00	16-Jun-27 17:00	27d											
	SU4-FOS-20	Fuel Oil - CTC Book to Client for Review	5d	17-Jun-27 08:00	24-Jun-27 17:00	25d											
	SU4-FOS-25	Flush Fuel Oil Supply	5d	17-Jun-27 08:													

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
SU4-PEECC2-10	PEECC-02 - CTO Turnover	0d		29-Mar-27 17:00	69d
SU4-PEECC2-15	PEECC-02 - Pre-Operational Testing	4d	04-Jun-27 11:00	10-Jun-27 11:00	24d
SU4-PEECC2-20	PEECC-02 - CTC Book to Client for Review	5d	10-Jun-27 11:00	17-Jun-27 11:00	30d
00373.00363-2_Startup.6.22 Service Water System (SWS-01)					
SU4-SWS-5	Service Water - CTO Walkdown/Punchlist	10d	16-Feb-27 08:00	01-Mar-27 17:00	96d
SU4-SWS-10	Service Water - CTO Turnover	0d		01-Mar-27 17:00	96d
SU4-SWS-15	Service Water - Pre-Operational Testing	4d	04-Jun-27 11:00	10-Jun-27 11:00	32d
SU4-SWS-20	Service Water - CTC Book to Client for Review	5d	10-Jun-27 11:00	17-Jun-27 11:00	30d
00373.00363-2_Startup.6.24 Turbine Cooling & Sealing Air (TCS-01)					
SU4-TCS-5	Turbine Cooling - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	107d
SU4-TCS-10	Turbine Cooling - CTO Turnover	0d		01-Feb-27 17:00	107d
SU4-TCS-15	Turbine Cooling - Pre-Operational Testing	4d	10-Jun-27 11:00	16-Jun-27 11:00	20d
SU4-TCS-20	Turbine Cooling - CTC Book to Client for Review	5d	16-Jun-27 11:00	24-Jun-27 11:00	26d
00373.00363-2_Startup.6.25 Turbine Air Inlet (TAI-01)					
SU4-TAI-5	Turbine Air - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	111d
SU4-TAI-10	Turbine Air - CTO Turnover	0d		01-Feb-27 17:00	111d
SU4-TAI-15	Turbine Air - Pre-Operational Testing	4d	10-Jun-27 11:00	16-Jun-27 11:00	24d
SU4-TAI-20	Turbine Air - CTC Book to Client for Review	5d	16-Jun-27 11:00	24-Jun-27 11:00	26d
00373.00363-2_Startup.6.26 Turbine Controls & Instrumentation Devices (TCI-01)					
SU4-TCI-5	Turbine Controls - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	115d
SU4-TCI-10	Turbine Controls - CTO Turnover	0d		01-Feb-27 17:00	115d
SU4-TCI-15	Turbine Controls - Pre-Operational Testing	4d	16-Jun-27 11:00	22-Jun-27 11:00	24d
SU4-TCI-20	Turbine Controls - CTC Book to Client for Review	5d	22-Jun-27 11:00	29-Jun-27 11:00	23d
00373.00363-2_Startup.6.29 Turbine Generator Accessory Module (TGA-01)					
SU4-TGA-5	Turbine Accessory Module - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	104d
SU4-TGA-10	Turbine Accessory Module - CTO Turnover	0d		01-Feb-27 17:00	104d
SU4-TGA-15	Turbine Accessory Module - Pre-Operational Testing	4d	04-Jun-27 11:00	10-Jun-27 11:00	20d
SU4-TGA-20	Turbine Accessory Module - CTC Book to Client for Review	5d	10-Jun-27 11:00	17-Jun-27 11:00	30d
00373.00363-2_Startup.6.28 Turbine Hazardous Gas Detector (THG-01)					
SU4-THG-5	Turbine Haz Gas - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	115d
SU4-THG-10	Turbine Haz Gas - CTO Turnover	0d		01-Feb-27 17:00	115d
SU4-THG-15	Turbine Haz Gas - Pre-Operational Testing	4d	22-Jun-27 11:00	28-Jun-27 11:00	20d
SU4-THG-20	Turbine Haz Gas - CTC Book to Client for Review	5d	28-Jun-27 11:00	06-Jul-27 11:00	19d
00373.00363-2_Startup.6.9 Turbine Heating & Ventilation (THV-01)					
SU4-THV-5	Turbine Heating - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	111d
SU4-THV-10	Turbine Heating - CTO Turnover	0d		01-Feb-27 17:00	111d
SU4-THV-15	Turbine Heating - Pre-Operational Testing	4d	16-Jun-27 11:00	22-Jun-27 11:00	20d
SU4-THV-20	Turbine Heating - CTC Book to Client for Review	5d	22-Jun-27 11:00	29-Jun-27 11:00	23d
00373.00363-2_Startup.6.27 Waste Water System (WWS-01)					
SU4-WWS-5	Water Wash - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	115d
SU4-WWS-10	Water Wash - CTO Turnover	0d		01-Feb-27 17:00	115d
SU4-WWS-15	Water Wash - Pre-Operational Testing	4d	04-Jun-27 11:00	10-Jun-27 11:00	32d
SU4-WWS-20	Water Wash - CTC Book to Client for Review	5d	10-Jun-27 11:00	17-Jun-27 11:00	30d
00373.00363-2_Startup.6.12 Generator & GSU Transformer (1-GEN-01)					
SU4-GEN-5	GSU - CTO Walkdown/Punchlist	10d	19-Jan-27 08:00	01-Feb-27 17:00	111d
SU4-GEN-10	GSU - CTO Turnover	0d		01-Feb-27 17:00	111d
SU4-GEN-15	GSU - Pre-Operational Testing	4d	14-May-27 11:00	20-May-27 11:00	43d
SU4-GEN-20	GSU - CTC Book to Client for Review	5d	20-May-27 11:00	27-May-27 11:00	44d
00373.00363-2_Startup.6.16 Hydrogen Cooling (HYD-01)					
SU4-HYD-5	Hydrogen Cooling - CTO Walkdown/Punchlist	10d	07-Jan-27 11:00	22-Jan-27 11:00	122d
SU4-HYD-10	Hydrogen Cooling - CTO Turnover	0d		22-Jan-27 11:00	122d

Remaining Level of Effort

Actual Work

Milestone

Actual Level of Effort

Remaining Work

Primary Baseline

Critical Remaining Work

Page 104 of 105

[illegible]
