BEFORE THE PUBLIC SERVICE COMMISSION
OF THE STATE OF MISSOURI

In the Matter of the Application of Union Electric Company, d/b/a Ameren Missouri, for Permission and Approval and Certificates of Convenience and Necessity Authorizing it to Construct Renewable Generation Facilities.	)))))	**File No. EA-2025-0239**

SUBMISSION OF QUARTERLY REPORT UNDER ¶ 6.d OF STIPULATION AND AGREEMENT

COMES NOW Union Electric Company d/b/a Ameren Missouri ("Ameren Missouri" or "Company"), and pursuant to ¶ 6.d of the March 20, 2026, Non-Unanimous Stipulation and Agreement[1] filed in this case and approved by the Commission, hereby submits its Quarterly Progress Report for the 3rd quarter of 2026, as follows:

Engineering and design are supporting active field construction across the civil, structural/post, electrical and environmental work fronts. Due to file sizes, drawings will be provided to the Staff via Ameren Missouri's ShareFile site.

Reform's construction update shows civil grading and SWPPP work advancing in Areas 4 and 5; inverter and combiner post installation progressing; and medium-voltage collection work, crossings, trenching and installation continuing across multiple circuits. Procurement is generally aligned with the advancing design. Major tracker, pile, combiner, collection-cable, SCADA/telecom, substation and O&M Building packages are issued or in review. Open submittals continue to be worked to avoid material-order delays and to incorporate approved design clarifications into the project documents.

For details on the Construction Schedule and milestones during the quarter, see Exhibit A. See attached Exhibit B for the current status of permitting efforts.

[1] No party objected to the Stipulation, and it was thus treated as unanimous and approved by the Commission.

The base case and risk-adjusted project cost estimates remain unchanged. There have been no identified tariff impacts to-date, but the PV supplier did issue preliminary notice identifying the August 6, 2026, Presidential Proclamation as a potential change in tariff for module deliveries schedule in or after January 2027. There are no other updates regarding legislative or executive actions.

A final tax credit election has not yet been made, but at present, the expectation continues to be that the ITC will be the most beneficial election.


/s/ James B. Lowery
James B. Lowery, Mo. Bar #40503
JBL LAW, LLC
9020 S. Barry Rd. Columbia,
MO 65201
Telephone: 573-476-0050
E-Mail: lowery@jbllawllc.com
Jennifer L. Hernandez, MO Bar #59814
Corporate Counsel
1901 Chouteau Avenue, MC 1310
P.O. Box 66149
St. Louis, MO 63166-6149
(314) 978-8418 (Telephone)
(314) 554-4014 (Facsimile)
AmerenMOService@ameren.com
ATTORNEYS FOR UNION ELECTRIC COMPANY d/b/a AMEREN MISSOURI

CERTIFICATE OF SERVICE

The undersigned certifies that true and correct copies of the foregoing was served on counsel for all parties of record via electronic mail (e-mail) on this 9th day of November, 2026.

/s/ *James B. Lowery*

#	ID	Activity Name	Dur	Start	Finish
2		AMEREN REFORM - 323.98MWDC	1398d	01-May-23 A	30-Oct-28
3		SUMMARY & MILESTONES	1107d	21-Jun-24 A	30-Oct-28
4		SUMMARY - PROJ DURATION (WK DAYS)	556d	12-Jun-26 A	29-Sep-28
5		SUMMARY - MECH DURATION (WORK DAYS)	314d	30-Nov-26	23-Feb-28
6		CONST DURATION SUMMARY	1024d	21-Jun-24 A	24-Jul-28
7		SUMMARY - PRECON / LNTP TO CONST START	161d	21-Jun-24 A	12-Jun-26 A
8		SUMMARY - DURATION - CIRCUIT 3	484d	26-Jun-26 A	14-Jun-28
9		SUMMARY - DURATION - CIRCUIT 2	440d	07-Jul-26 A	05-May-28
10		SUMMARY - DURATION - CIRCUIT 4	442d	28-Aug-26 A	30-May-28
11		SUMMARY - DURATION - CIRCUIT 1	427d	16-Sep-26	19-May-28
12		SUMMARY - DURATION - CIRCUIT 5	450d	23-Sep-26	29-Jun-28
13		SUMMARY - DURATION - CIRCUIT 6	453d	12-Oct-26	24-Jul-28
14		SUBSTATION SUMMARY/ MILESTONES	461d	30-Apr-26 A	18-May-28
15		ARRAY SUMMARY	742d	11-Dec-25 A	30-Oct-28
16		SUMMARY - MAKE READY / TREE CLEARING (CLEARING BETWEEN NOV 1ST T0 MAR 31)	85d	11-Dec-25 A	23-Mar-26 A
17		SUMMARY - CONST MOBILIZATION	20d	14-Apr-26 A	10-Jun-26 A
18		SUMMARY - EARTHWORK / GRADING	127d	15-Jun-26 A	28-Dec-26
19		SUMMARY - DC ELECT - FEEDERS & GROUND CABLE	266d	03-Sep-26	21-Sep-27
20		SUMMARY - MV UG ELECT & FIBER	263d	09-Sep-26	21-Sep-27
21		SUMMARY - COMBINER BOX INSTALL & TERMS	241d	15-Oct-26	27-Sep-27
22		SUMMARY - POST PRODUCTION	243d	19-Nov-26	03-Nov-27
23		SUMMARY - TRACKER PRODUCTION	269d	18-Jan-27	07-Feb-28
24		SUMMARY - MODULE PRODUCTION	219d	14-Apr-27	23-Feb-28
25		SUMMARY - DC ELECT - WIRE HARNESS & STRINGS	217d	28-Apr-27	06-Mar-28
26		SUMMARY - DC ELECT - STRING PLUG & PLAY/ FINAL TERMS	213d	04-May-27	06-Mar-28
27		SUMMARY - INVERTER EQUIPSET	25d	16-Sep-27	20-Oct-27
28		SUMMARY - MV INV TERMS	93d	17-Sep-27	31-Jan-28
29		SUMMARY - DC INV TERMS	93d	17-Sep-27	31-Jan-28
30		SUMMARY - CIRC TESTING / MECH COMPLETION	160d	07-Oct-27	23-May-28
31		SUMMARY - SUBSTATION BACKFEED AVAIL TO SYNC	6d	20-Mar-28	27-Mar-28
32		SUMMARY - CIRC COMMISSIONING / SUBST COMPLETION	132d	27-Mar-28	29-Sep-28
33		SUMMARY - FINAL COMPLETION (SUBST TO FINAL)	21d	02-Oct-28	30-Oct-28
34		PROJECT MILESTONES	1107d	21-Jun-24 A	30-Oct-28
35		ARRAY MILESTONES	1107d	21-Jun-24 A	30-Oct-28
36		*MILESTONE: ISSUE EPC CONTRACT	0d		21-Jun-24 A
37		*MILESTONE: 30% DESIGN COMPLETION (INCL SUBSTATION)	0d		21-May-25 A
38		*MILESTONE: START MAKE READY / TREE REMOVAL	0d	15-Dec-25 A	
39		**MILESTONE: 60% DESIGN COMPLETION (INCL SUBSTATION)	0d		23-Jan-26 A
40		**MILESTONE: CONST START / MOBILIZATION	0d	12-Jun-26 A	
41		**MILESTONE: PROCUREMENT RELEASE	0d	24-Jun-26 A	
42		*MILESTONE: RELEASE SUBSTATION PROCUREMENT	0d		01-Jul-26 A
43		*MILESTONE: 90% DESIGN COMPLETION (INCL SUBSTATION)	0d		22-Jul-26 A
44		*MILESTONE: IFC SET COMPLETE (CD'S COMPLETE)	0d		02-Nov-26
45		*MILESTONE: ENVIRONMENTAL PERMIT CLOSEOUT	0d		21-Jun-28
46		*MILESTONE: PROJ SUBST COMPLETION	0d		30-Sep-28
47		**MILESTONE: PROJECT FINAL COMPLETION	0d		30-Oct-28
48		MILESTONES - PV MECH COMPLETIONS	63d	24-Feb-28	23-May-28
49		*MILESTONE: MECH COMPLETION - CIRCUIT 2	0d		24-Feb-28
50		*MILESTONE: MECH COMPLETION - CIRCUIT 1	0d		02-Mar-28
51		*MILESTONE: MECH COMPLETION - CIRCUIT 4	0d		09-Mar-28
52		*MILESTONE: MECH COMPLETION - CIRCUIT 3	0d		16-Mar-28
53		*MILESTONE: MECH COMPLETION - CIRCUIT 5	0d		12-Apr-28
54		*MILESTONE: MECH COMPLETION - CIRCUIT 6	0d		23-May-28
55		MILESTONES - PV PLACED IN SERVICE	54d	25-Apr-28	12-Jul-28
56		MILESTONES - PV SUBSTANTIAL COMPLETIONS	102d	05-May-28	30-Sep-28
57		**MILESTONE: SUBST COMPLETION - CIRCUIT 2	0d		05-May-28
58		**MILESTONE: SUBST COMPLETION - CIRCUIT 1	0d		19-May-28
59		**MILESTONE: SUBST COMPLETION - CIRCUIT 4	0d		30-May-28
60		**MILESTONE: SUBST COMPLETION - CIRCUIT 3	0d		14-Jun-28
61		**MILESTONE: SUBST COMPLETION - CIRCUIT 5	0d		29-Jun-28
62		**MILESTONE: SUBST COMPLETION - CIRCUIT 6	0d		24-Jul-28
63		**MILESTONE: PROJ SUBSTANTIAL COMPLETION	0d		30-Sep-28*

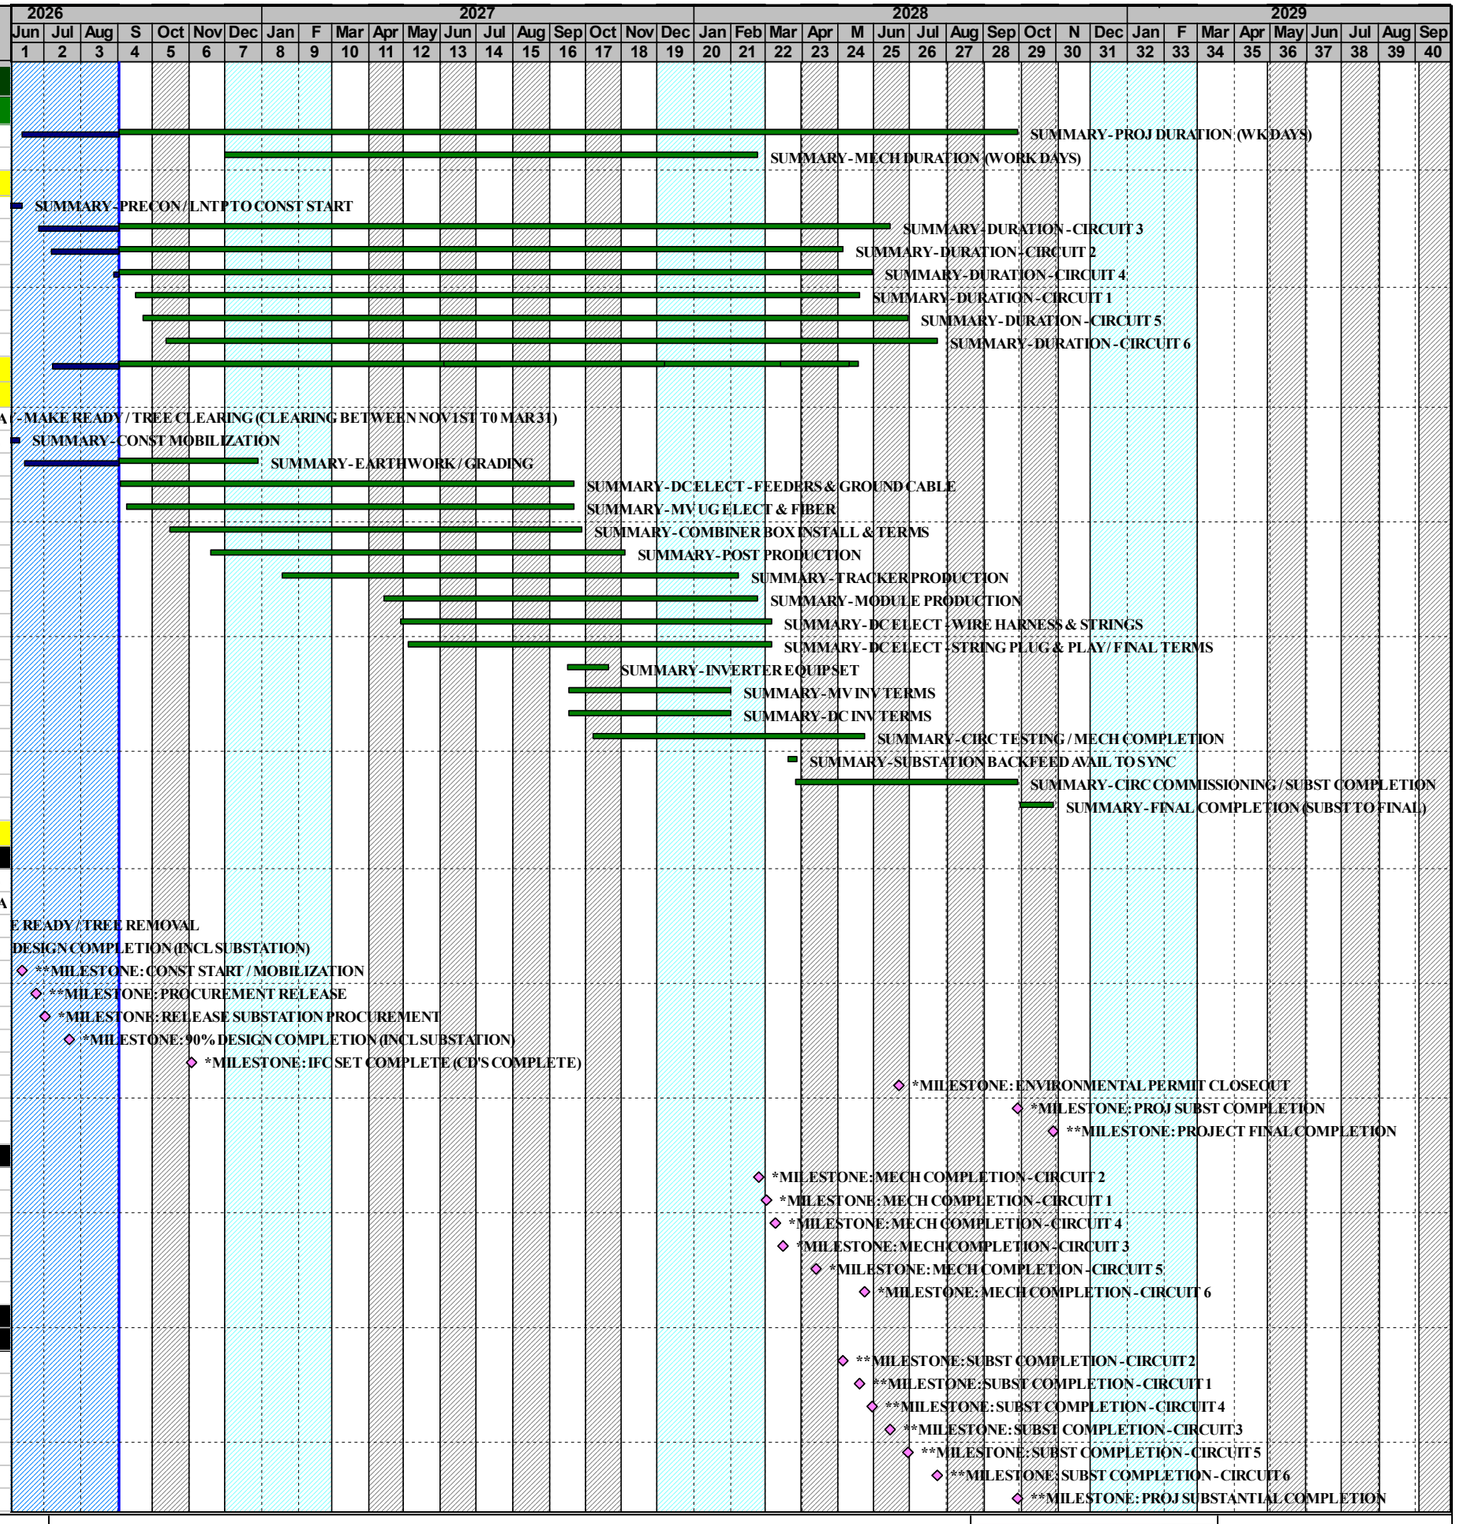

Data Date: 02-Sep-26
Print Date: 08-Sep-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Ameren - Reform - Jefferson City, MO - 323.98MWdc

McCARTHY

Summary
Page 1 of 3

EXHIBIT A

#	ID	Activity Name	Dur	Start	Finish
64		PRECON	1395d	01-May-23 A	25-Oct-28
65		CONTRACTING / PERMITTING	806d	01-May-23 A	24-Jun-26 A
66		PROPOSAL / AWARD	167d	01-May-23 A	27-Dec-23 A
67		LNTP / EPC	45d	28-Dec-23 A	21-Jun-24 A
68		PROJECT HOLDS	313d	04-Apr-24 A	28-Jul-25 A
69		FNTP / PROCUREMENT RELEASE	86d	27-Jan-26 A	24-Jun-26 A
70		DESIGN (MCC)	665d	01-Jan-24 A	02-Nov-26
71		DESIGN TOPO / GEOTECH	507d	01-Jan-24 A	04-May-26 A
72		SITE LAYOUT REVISIONS	256d	17-Jan-25 A	06-Mar-26 A
73		30% REVISIONS	137d	17-Mar-25 A	12-Sep-25 A
74		CIVIL DESIGN	216d	15-Sep-25 A	02-Jul-26 A
75		60% DESIGN - CIVIL	98d	15-Sep-25 A	23-Jan-26 A
76		90% DESIGN - CIVIL	135d	02-Oct-25 A	21-Apr-26 A
77		IFC DESIGN - CIVIL	59d	22-Apr-26 A	02-Jul-26 A
78		POST/STRUCTURAL DESIGN	202d	15-Sep-25 A	01-Jun-26 A
79		60% DESIGN - POST	25d	15-Sep-25 A	24-Sep-25 A
80		90% DESIGN - POST	106d	25-Sep-25 A	05-May-26 A
81		IFC DESIGN - POST	25d	06-May-26 A	01-Jun-26 A
82		ELECTRICAL DESIGN	216d	15-Sep-25 A	19-Jun-26 A
83		60% DESIGN - ELECTRICAL	25d	15-Sep-25 A	24-Sep-25 A
84		90% DESIGN - ELECTRICAL	101d	25-Sep-25 A	17-Apr-26 A
85		IFC DESIGN - ELECTRICAL	59d	20-Apr-26 A	19-Jun-26 A
86		SCADA DESIGN	48d	15-Jul-26 A	21-Sep-26
87		SUBSTATION DESIGN	289d	15-Sep-25 A	02-Nov-26
88		PERMITTING	25d	02-Oct-25 A	05-Dec-25 A
89		PROJECT PLANNING / COORDINATION	763d	26-Feb-24 A	25-Oct-28
90		PROCUREMENT	473d	24-Mar-26 A	15-Mar-28
91		SUB CONTRACTS / PURCHASE ORDERS	86d	24-Mar-26 A	30-Sep-26
92		SUBSTATION (MBC)	325d	28-Aug-26 A	29-Oct-27
93		SUBSTATION (OWNER)	473d	01-May-26 A	15-Mar-28
94		MPT	473d	01-May-26 A	15-Mar-28
95		HV BREAKERS	350d	01-May-26 A	16-Sep-27
96		ELECT INVERTER EQUIP	265d	01-Oct-26	15-Oct-27
97		AC CABLE / CONDUCTORS	100d	04-Jun-26 A	23-Oct-26
98		DC CABLE / CONDUCTORS	17d	08-Jun-26 A	10-Sep-26
99		POSTS	166d	01-Jun-26 A	04-Feb-27
100		TRACKERS	263d	08-Sep-26	20-Sep-27
101		MODULES (OWNER)	313d	01-May-26 A	28-Jul-27
102		MODULES - FAB LEAD TIME	208d	01-May-26 A	08-Apr-27
103		MODULES - DELIVERIES	77d	09-Apr-27	28-Jul-27
104		WIRE HARNESS	161d	10-Jun-26 A	20-Apr-27
105		COMBINER BOXES	95d	08-Sep-26	22-Jan-27
106		SCADA	190d	22-Sep-26	21-Jun-27
107		CONSTRUCTION	734d	11-Dec-25 A	30-Oct-28
108		PROJECT CHALLENGES	99d	28-Apr-26 A	04-Sep-26
109		MOBILIZATION	150d	11-Dec-25 A	12-Jun-26 A
110		MAKE READY / TREE REMOVAL	5d	11-Dec-25 A	15-Dec-25 A
111		PROJECT PRODUCTION	34d	14-Apr-26 A	12-Jun-26 A
112		CIVIL - TREE CLEARING & MASS EARTHWORK	268d	11-Dec-25 A	31-Dec-26
113		TREE CLEARING (BY AREA)	245d	11-Dec-25 A	25-Nov-26
114		AREA 1 (PBs 41, 42, 43, 44)	149d	11-Dec-25 A	06-Jul-26 A
115		AREA 2 (PBs 21, 22, 23, 24, 45, 49, 50, 51)	160d	31-Dec-25 A	17-Jul-26 A
116		AREA 3 (PBs 9, 10, 11, 12, 13, 14, 15, 16, 17, 18, 19, 20)	183d	18-Dec-25 A	09-Sep-26
117		AREA 4 (PBs 46, 47, 48, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69)	186d	13-Jan-26 A	02-Oct-26
118		AREA 5 (PBs 34, 35, 36, 37, 38, 39, 40)	180d	02-Feb-26 A	21-Oct-26
119		AREA 6 (PBs 1, 2, 3, 4, 5, 6, 7, 8)	182d	11-Feb-26 A	04-Nov-26
120		AREA 7 (PBs 25, 26, 27, 28, 29, 30, 31, 32, 33, 52, 53, 54, 55, 56, 57, 58)	185d	26-Feb-26 A	25-Nov-26
121		MASS EARTHWORK (BY AREA)	139d	15-Jun-26 A	31-Dec-26
122		AREA 1 (PBs 41 - 44) (39 AC) (90K CY)	68d	15-Jun-26 A	18-Sep-26
123		AREA 2 (PBs 21 - 24, 45, 49 - 51) (32 AC) (81K CY)	49d	29-Jun-26 A	23-Sep-26
124		AREA 3 (PBs 9 - 20) (76 AC) (22K CY)	41d	12-Aug-26 A	28-Sep-26
125		AREA 4 (PBs 46 - 48, 59 - 69) (111 AC) (151K CY)	64d	02-Sep-26	03-Dec-26

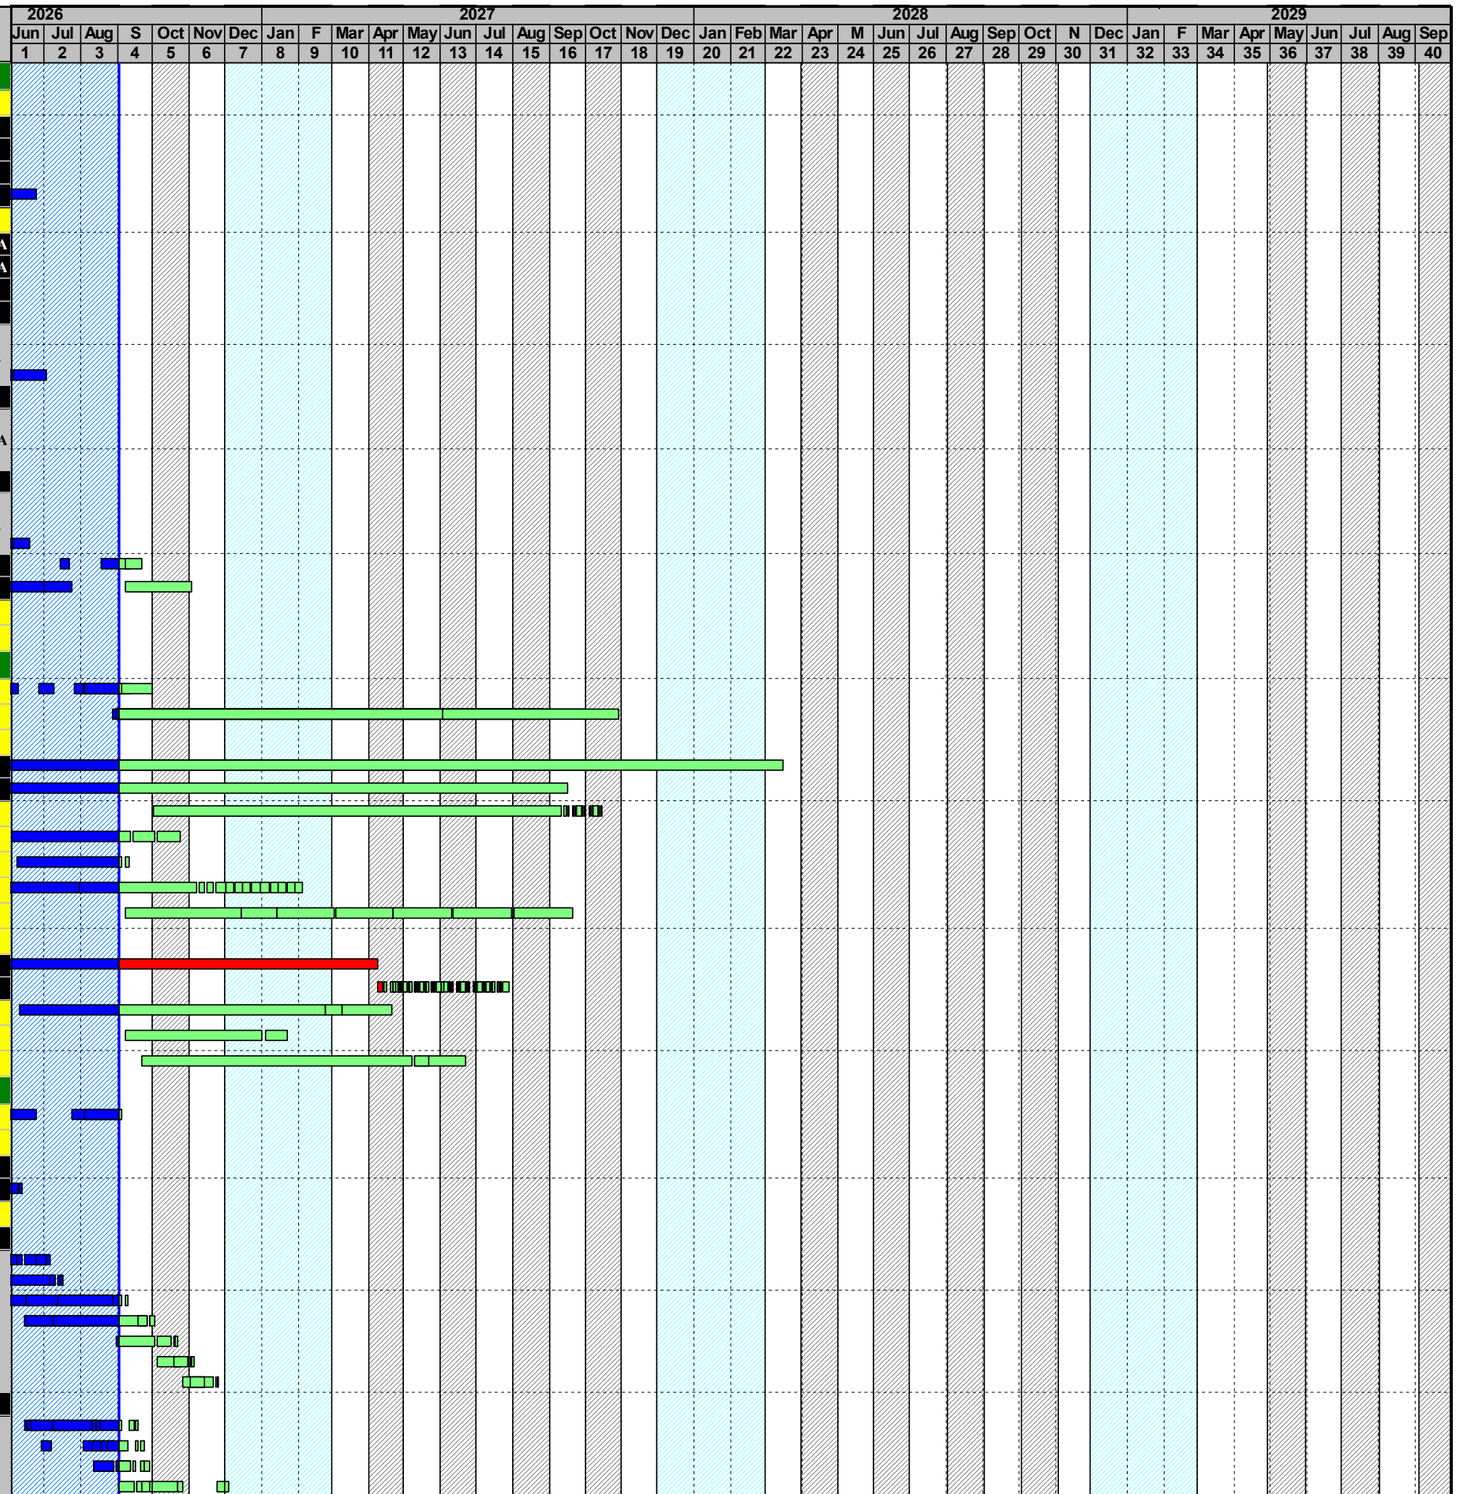

Data Date: 02-Sep-26
Print Date: 08-Sep-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren - Reform - Jefferson City, MO - 323.98MWdc

McCARTHY

Summary
Page 2 of 3

EXHIBIT A

#	ID	Activity Name	Dur	Start	Finish
126		AREA 5 (PBs 34 - 40) (43 AC) (38K CY)	58d	16-Sep-26	08-Dec-26
127		AREA 6 (PBs 1 - 8) (57 AC) (58K CY)	56d	23-Sep-26	11-Dec-26
128		AREA 7 (PBs 25 - 33, 52 - 58) (68 AC) (50K CY)	63d	01-Oct-26	31-Dec-26
129		FENCING	328d	14-Sep-26	29-Dec-27
130		SUBSTATION	435d	08-Jul-26 A	18-May-28
131		SUBGRADE CONSTRUCTION	10d	08-Jul-26 A	04-Sep-26
132		SUBSTRUCT / FOUNDATIONS	101d	01-Mar-27	21-Jul-27
133		EQUIPMENT INSTALL	193d	04-Jun-27	08-Mar-28
134		HV BREAKER INSTALL	30d	17-Sep-27	28-Oct-27
135		MAIN POWER TRANSFORMERS	150d	18-Oct-27	18-May-28
136		CIRCUIT #2	426d	03-Aug-26 A	05-May-28
137		MV 2-2 ARRAY PRODUCTION	279d	03-Aug-26 A	07-Oct-27
138		MV 2-1 ARRAY PRODUCTION	200d	23-Dec-26	15-Nov-27
139		MECH COMPLETION	99d	05-Oct-27	24-Feb-28
140		STARTUP / COMMISSIONING	43d	24-Feb-28	25-Apr-28
141		SUBST COMPLETION	8d	26-Apr-28	05-May-28
142		CIRCUIT #1	364d	16-Dec-26	19-May-28
143		MV 1-2 ARRAY PRODUCTION	196d	11-Jan-27	12-Nov-27
144		MV 1-1 ARRAY PRODUCTION	203d	16-Dec-26	16-Nov-27
145		MECH COMPLETION	76d	12-Nov-27	02-Mar-28
146		STARTUP / COMMISSIONING	50d	02-Mar-28	11-May-28
147		SUBST COMPLETION	6d	12-May-28	19-May-28
148		CIRCUIT #4	442d	24-Aug-26 A	30-May-28
149		MV 4-2 ARRAY PRODUCTION	258d	24-Aug-26 A	25-Oct-27
150		MV 4-1 ARRAY PRODUCTION	195d	22-Feb-27	01-Dec-27
151		MECH COMPLETION	95d	25-Oct-27	09-Mar-28
152		STARTUP / COMMISSIONING	46d	16-Mar-28	19-May-28
153		SUBST COMPLETION	6d	20-May-28	30-May-28
154		CIRCUIT #3	453d	10-Aug-26 A	14-Jun-28
155		MV 3-1 ARRAY PRODUCTION	260d	10-Aug-26 A	27-Oct-27
156		MV 3-2 ARRAY PRODUCTION	286d	13-Aug-26 A	06-Dec-27
157		MECH COMPLETION	97d	27-Oct-27	16-Mar-28
158		STARTUP / COMMISSIONING	56d	16-Mar-28	05-Jun-28
159		SUBST COMPLETION	7d	06-Jun-28	14-Jun-28
160		CIRCUIT #5	356d	08-Feb-27	29-Jun-28
161		MV 5-1 ARRAY PRODUCTION	214d	08-Feb-27	12-Jan-28
162		MV 5-2 ARRAY PRODUCTION	206d	09-Mar-27	26-Jan-28
163		MECH COMPLETION	80d	21-Dec-27	12-Apr-28
164		STARTUP / COMMISSIONING	49d	12-Apr-28	21-Jun-28
165		SUBST COMPLETION	6d	22-Jun-28	29-Jun-28
166		CIRCUIT #6	348d	12-Mar-27	24-Jul-28
167		MV 6-1 ARRAY PRODUCTION	201d	12-Mar-27	19-Jan-28
168		MV 6-2 ARRAY PRODUCTION	208d	25-Mar-27	07-Mar-28
169		MECH COMPLETION	101d	04-Jan-28	23-May-28
170		STARTUP / COMMISSIONING	34d	23-May-28	12-Jul-28
171		SUBST COMPLETION	8d	13-Jul-28	24-Jul-28
172		PROJ COMPLETION	69d	25-Jul-28	30-Oct-28
173		PROJ SUSBT COMPLETION	48d	25-Jul-28	30-Sep-28
174		FINAL CORRECTIONS / SUBMIT FOR PROJ SUBST COMPLETION	10d	25-Jul-28	07-Aug-28
175		OPERATIONAL TESTING (PROJECT SITE)	10d	08-Aug-28	21-Aug-28
176		CONTROL SYSTEM RELIABILITY TESTING (CAL DAYS)	10d	08-Aug-28	17-Aug-28
177		PROJECT CAPACITY TESTING (7 DAY CAL)	15d	22-Aug-28	05-Sep-28
178		PROJECT SITE TESTING WEATHER ALLOWANCE	12d	06-Sep-28	21-Sep-28
179		ISSUE PROJ SUBSTANTIAL COMPLETION	8d	22-Sep-28	30-Sep-28
180		*MILESTONE: PROJ SUBST COMPLETION	0d		30-Sep-28
181		PROJ FINAL COMPLETION / ACCEPTANCE	21d	02-Oct-28	30-Oct-28

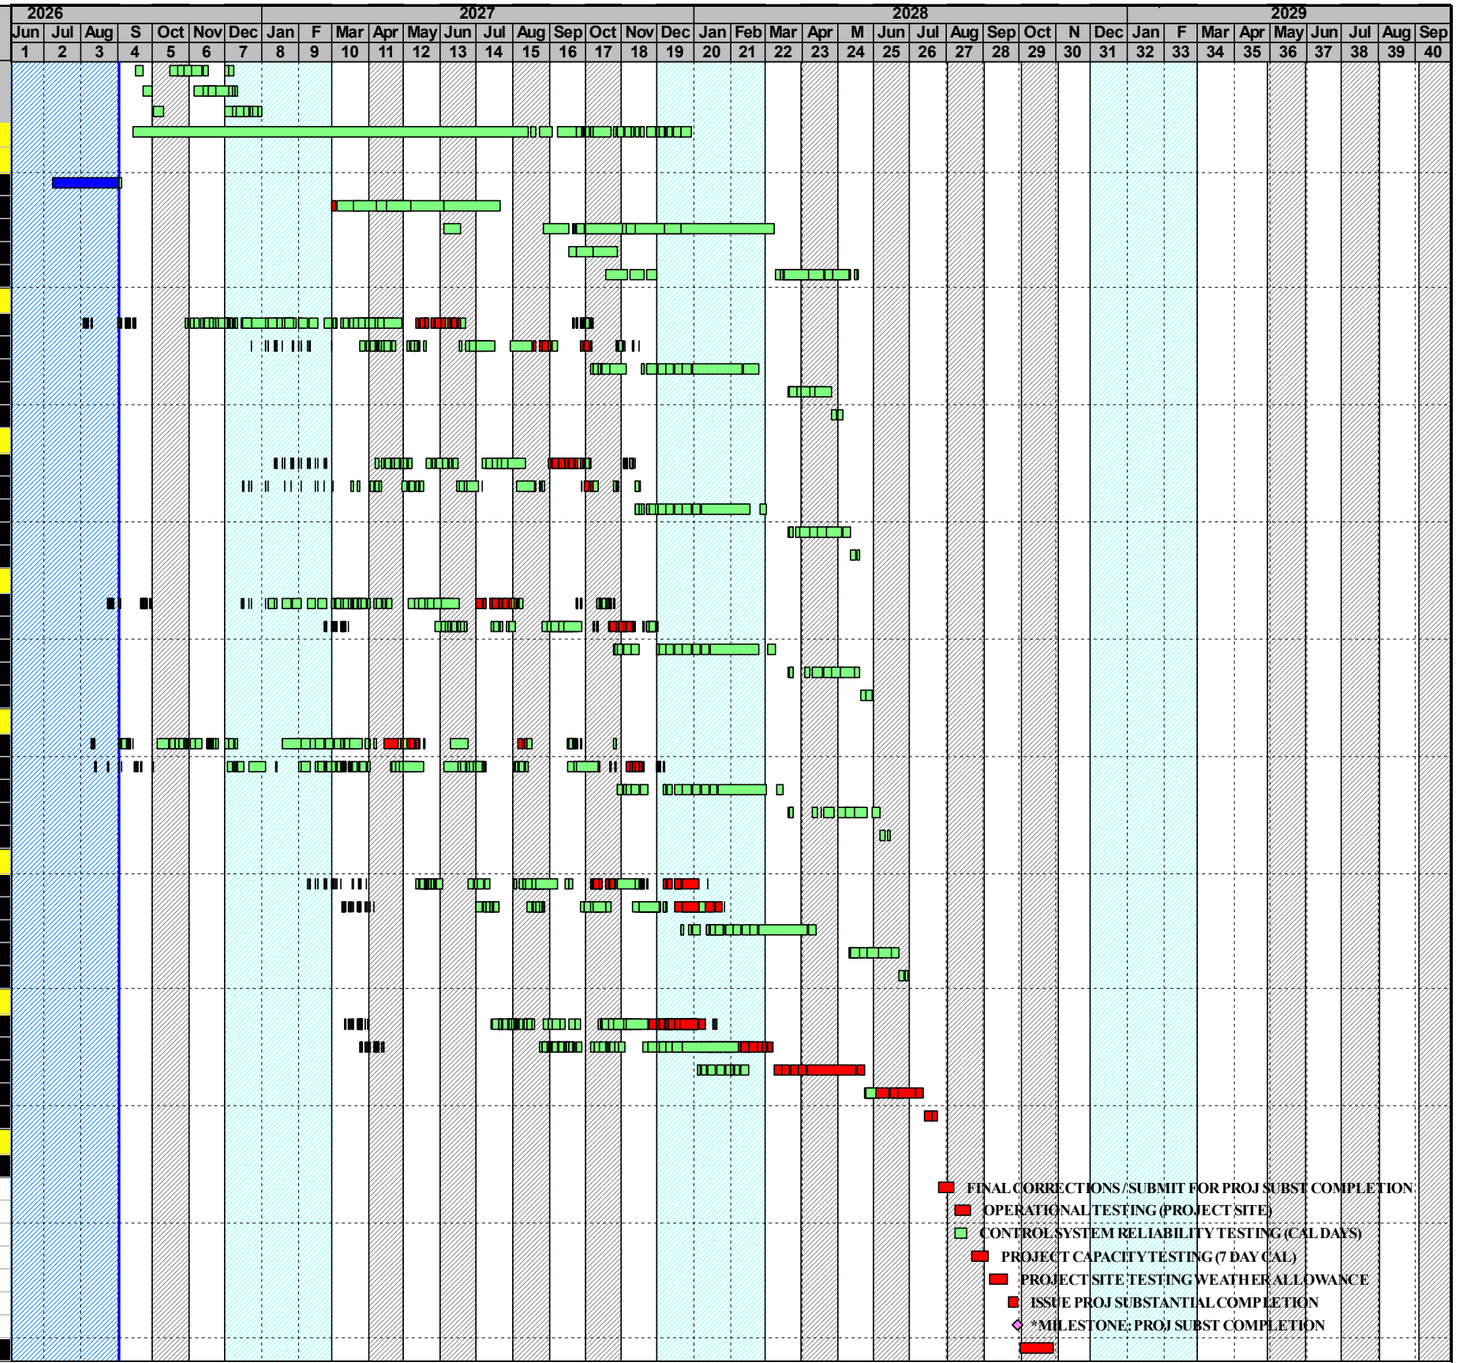


EXHIBIT A

REFORM SOLAR PROJECT

Permit Status Update

REFORM SOLAR PROJECT

Detailed Permit Matrix

Permit / Scope	Authority	Holder	Status	Permit / Ref.	Issue Date
MDNR construction stormwater / NPDES and SWPPP	MDNR	Ameren	Issued; Reform coverage effective	MOR-100098	12/01/2025
MoDOT entrance permit - Block 5	MoDOT	McCarthy	Issued	CD-26-121754	06/03/2026
MoDOT entrance permit - Block 6	MoDOT	McCarthy	Issued	CD-26-121755	06/03/2026
MoDOT entrance permit - Block 8	MoDOT	McCarthy	Issued	CD-26-121756	06/03/2026
MoDOT entrance permit - Block 23	MoDOT	McCarthy	Issued	CD-26-121757	06/03/2026
MoDOT entrance permit - Block 31	MoDOT	McCarthy	Issued	CD-26-121760	06/03/2026
MoDOT entrance permit - Block 33	MoDOT	McCarthy	Issued	CD-26-121758	06/03/2026
MoDOT entrance permit - Block 35	MoDOT	McCarthy	Issued	CD-26-121759	06/03/2026
MoDOT entrance permit - Block 45	MoDOT	McCarthy	Issued	CD-26-121762	06/03/2026
Callaway County bore permit - Road 428	Callaway County	McCarthy	Issued	2026-09-10-0428-01	09/08/2026
Callaway County bore permit - Road 448 (01)	Callaway County	McCarthy	Issued	2026-09-10-0448-01	09/08/2026
Callaway County bore permit - Road 448 (02)	Callaway County	McCarthy	Issued	2026-09-10-0448-02	09/08/2026
Callaway County bore permit - Road 448 (03)	Callaway County	McCarthy	Issued	2026-09-10-0448-03	09/08/2026
MoDOT bore permit - CR-4 / Route CC (2 circuits)	MoDOT	Ameren	Required	TBD	Not issued
MoDOT bore permit - CR-10 / Route CC (1 circuit)	MoDOT	Ameren	Required	TBD	Not issued
MoDOT bore permit - CR-12 / Route CC (2 circuits)	MoDOT	Ameren	Required	TBD	Not issued
MISO Generator Interconnection Agreement	MISO	Ameren	Issued	J1836	08/11/2026

EXHIBIT B
